


Do not scale. All dimensions in mm. Check all dimensions on site.

GROUND FLOOR SOLE PLATE SETTING OUT PLAN

Scale 1:50 @ A3 | Hatched red = sole plate cut away on site at door openings

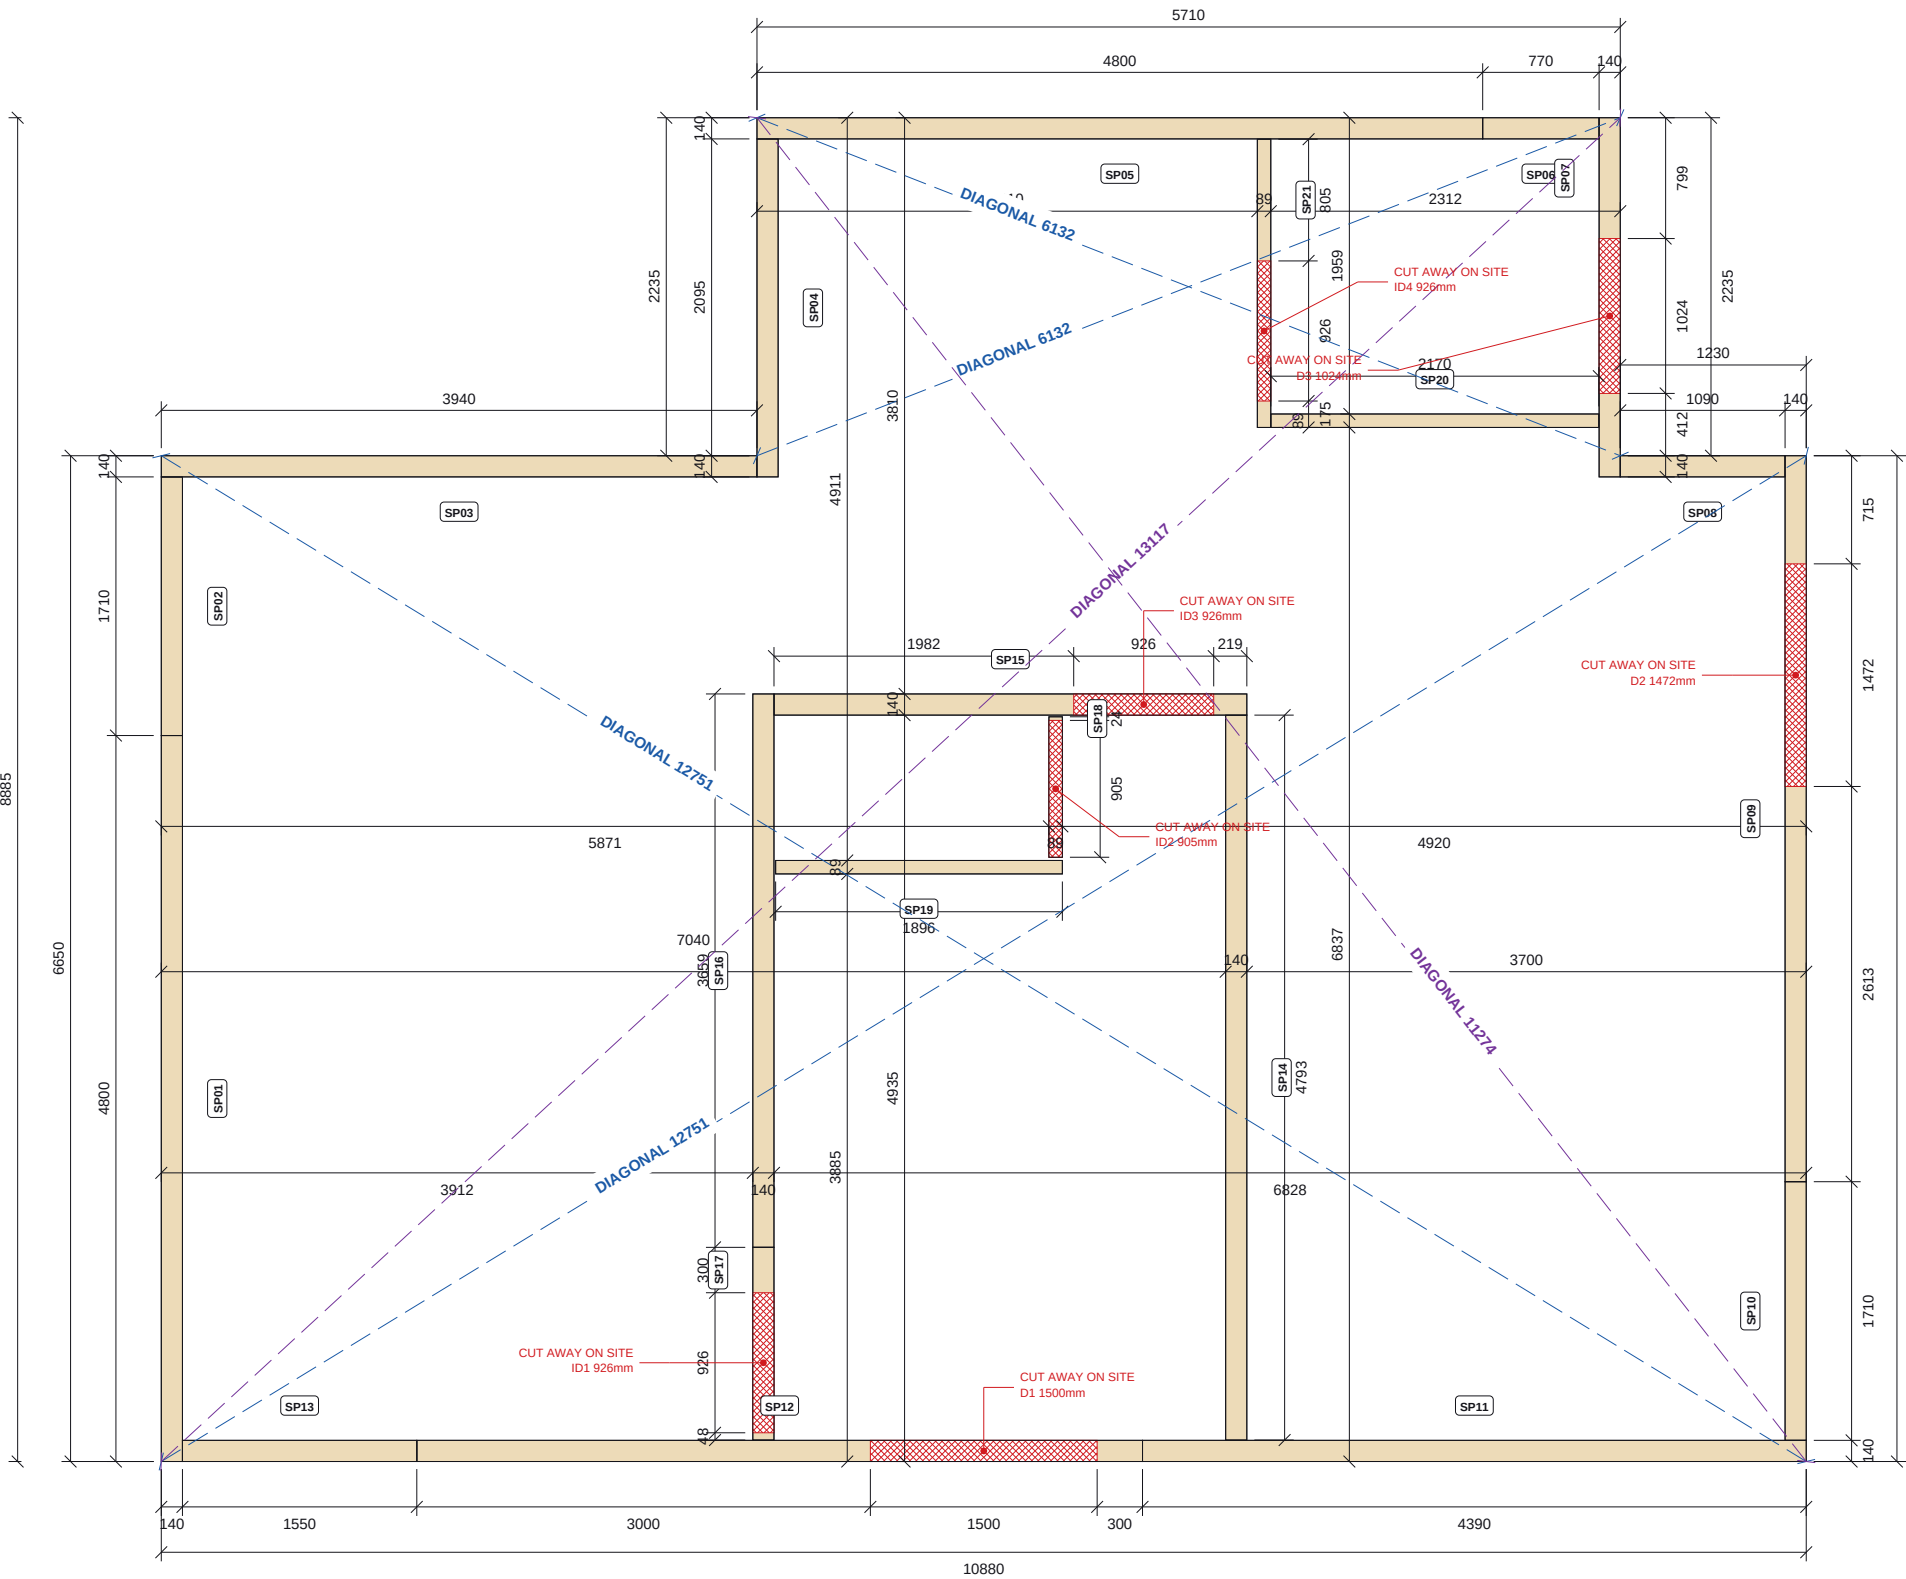

SOLE PLATE SCHEDULE

SOLE PLATES

Section	Pieces	Run m	4.8m lengths
38x140 C16	17	51.8	12
38x89 C16	4	6.9	3

Cut-optimised 4.8m stock, 3mm kerf, +5%.

SOLE PLATE CUT LIST

Mark	Section	Length	Cut-away	Mark	Section	Length	Cut-away
SP01	38x140	4800		SP02	38x140	1710	
SP05	38x140	4800		SP10	38x140	1710	
SP09	38x140	4800	D2	SP13	38x140	1550	
SP12	38x140	4800	D1	SP17	38x140	1274	ID1
SP14	38x140	4793		SP08	38x140	1090	
SP11	38x140	4390		SP06	38x140	770	
SP03	38x140	3940		SP20	38x89	2170	
SP16	38x140	3659		SP21	38x89	1906	ID4
SP15	38x140	3127	ID3	SP19	38x89	1896	
SP07	38x140	2375	D3	SP18	38x89	929	ID2
SP04	38x140	2235					

Door cut-aways are within the piece: fix the plate, then cut the door section away. All C16.

CHECK DIAGONALS

Block	Size	Diag 1	Diag 2
Main building	10880 x 6650	12751	12751
Block 2	5710 x 2235	6132	6132
Main to Block 2	corner-corner	13117	11274

Outer plate corners. Block diagonals equal; purple = main body to pop-out, match figures.

CONSUMABLES (NOT SHOWN)

Item	Quantity	Order
600mm DPC	39.0m + 8 laps	2 x 30m roll
300mm DPC	19.8m + 10 laps	1 x 30m roll
M7.5x100 concrete screw	114 (6.5mm pilot)	2 box of 100
Silicone 15ml per hole	1.71 L	7 x 280ml

DPC laps = own width at corners/junctions, +5%. Fixings +10%.

NOTES

- Sole plates: 38x140 C16 under external and internal load-bearing walls; 38x89 C16 under internal partitions. Outer face of sole plate = outer face of timber frame.
- DPC under all sole plates: 600mm wide centred under external walls, 300mm wide under internal walls. Lap DPC by its own width at every corner and junction.
- Fix sole plates with M7.5x100 concrete screws at max 600mm centres, one 50mm from each door opening (retained side) and one at each plate end at corners and junctions.
- Pre-drill each hole with a 6.5mm bit and fill with 15ml silicone before fixing.
- Sole plate across door openings (hatched red) is left in for erection and CUT AWAY ON SITE.
- Check each block for square before fixing: its two diagonals (blue dashed) must be equal.
- Dimensions are to sole plate faces. Read with P3-GA-01 and engineer's drawing 26-431-S-0001.

REVISIONS

REV	DATE	DESCRIPTION
C01	13.09.26	Construction issue



TLS TIMBER FRAME

Design & Manufacture

Scan: 3D model + drawings



CLIENT	PROJECT
MP Adams	MP Adams Plot 3, Eckington

DRAWING TITLE

GROUND FLOOR SOLE PLATE SETTING OUT


DPC, fixings and silicone are scheduled - not shown

SCALE	SIZE	DATE	DRAWN
1:50	A3	13.09.26	TS


STATUS	DRAWING No.	REV
CONSTRUCTION	P3-SP-01	C01

DETAIL 1 - ETFSS HOLDING DOWN STRAP

Engineer's detail reproduced from Skyhooks 26-431-S-0001 P02 (not to scale)

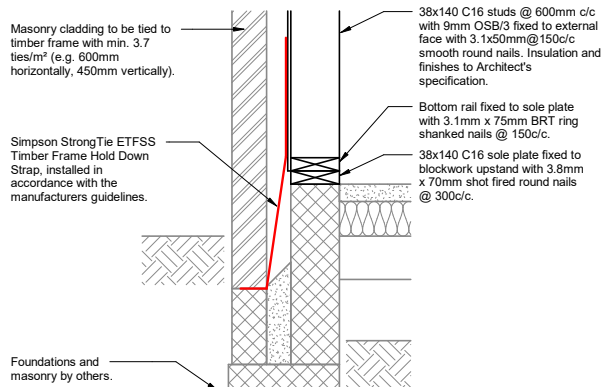

1 Plot 3 - Holding Down Strap Detail
1 : 10

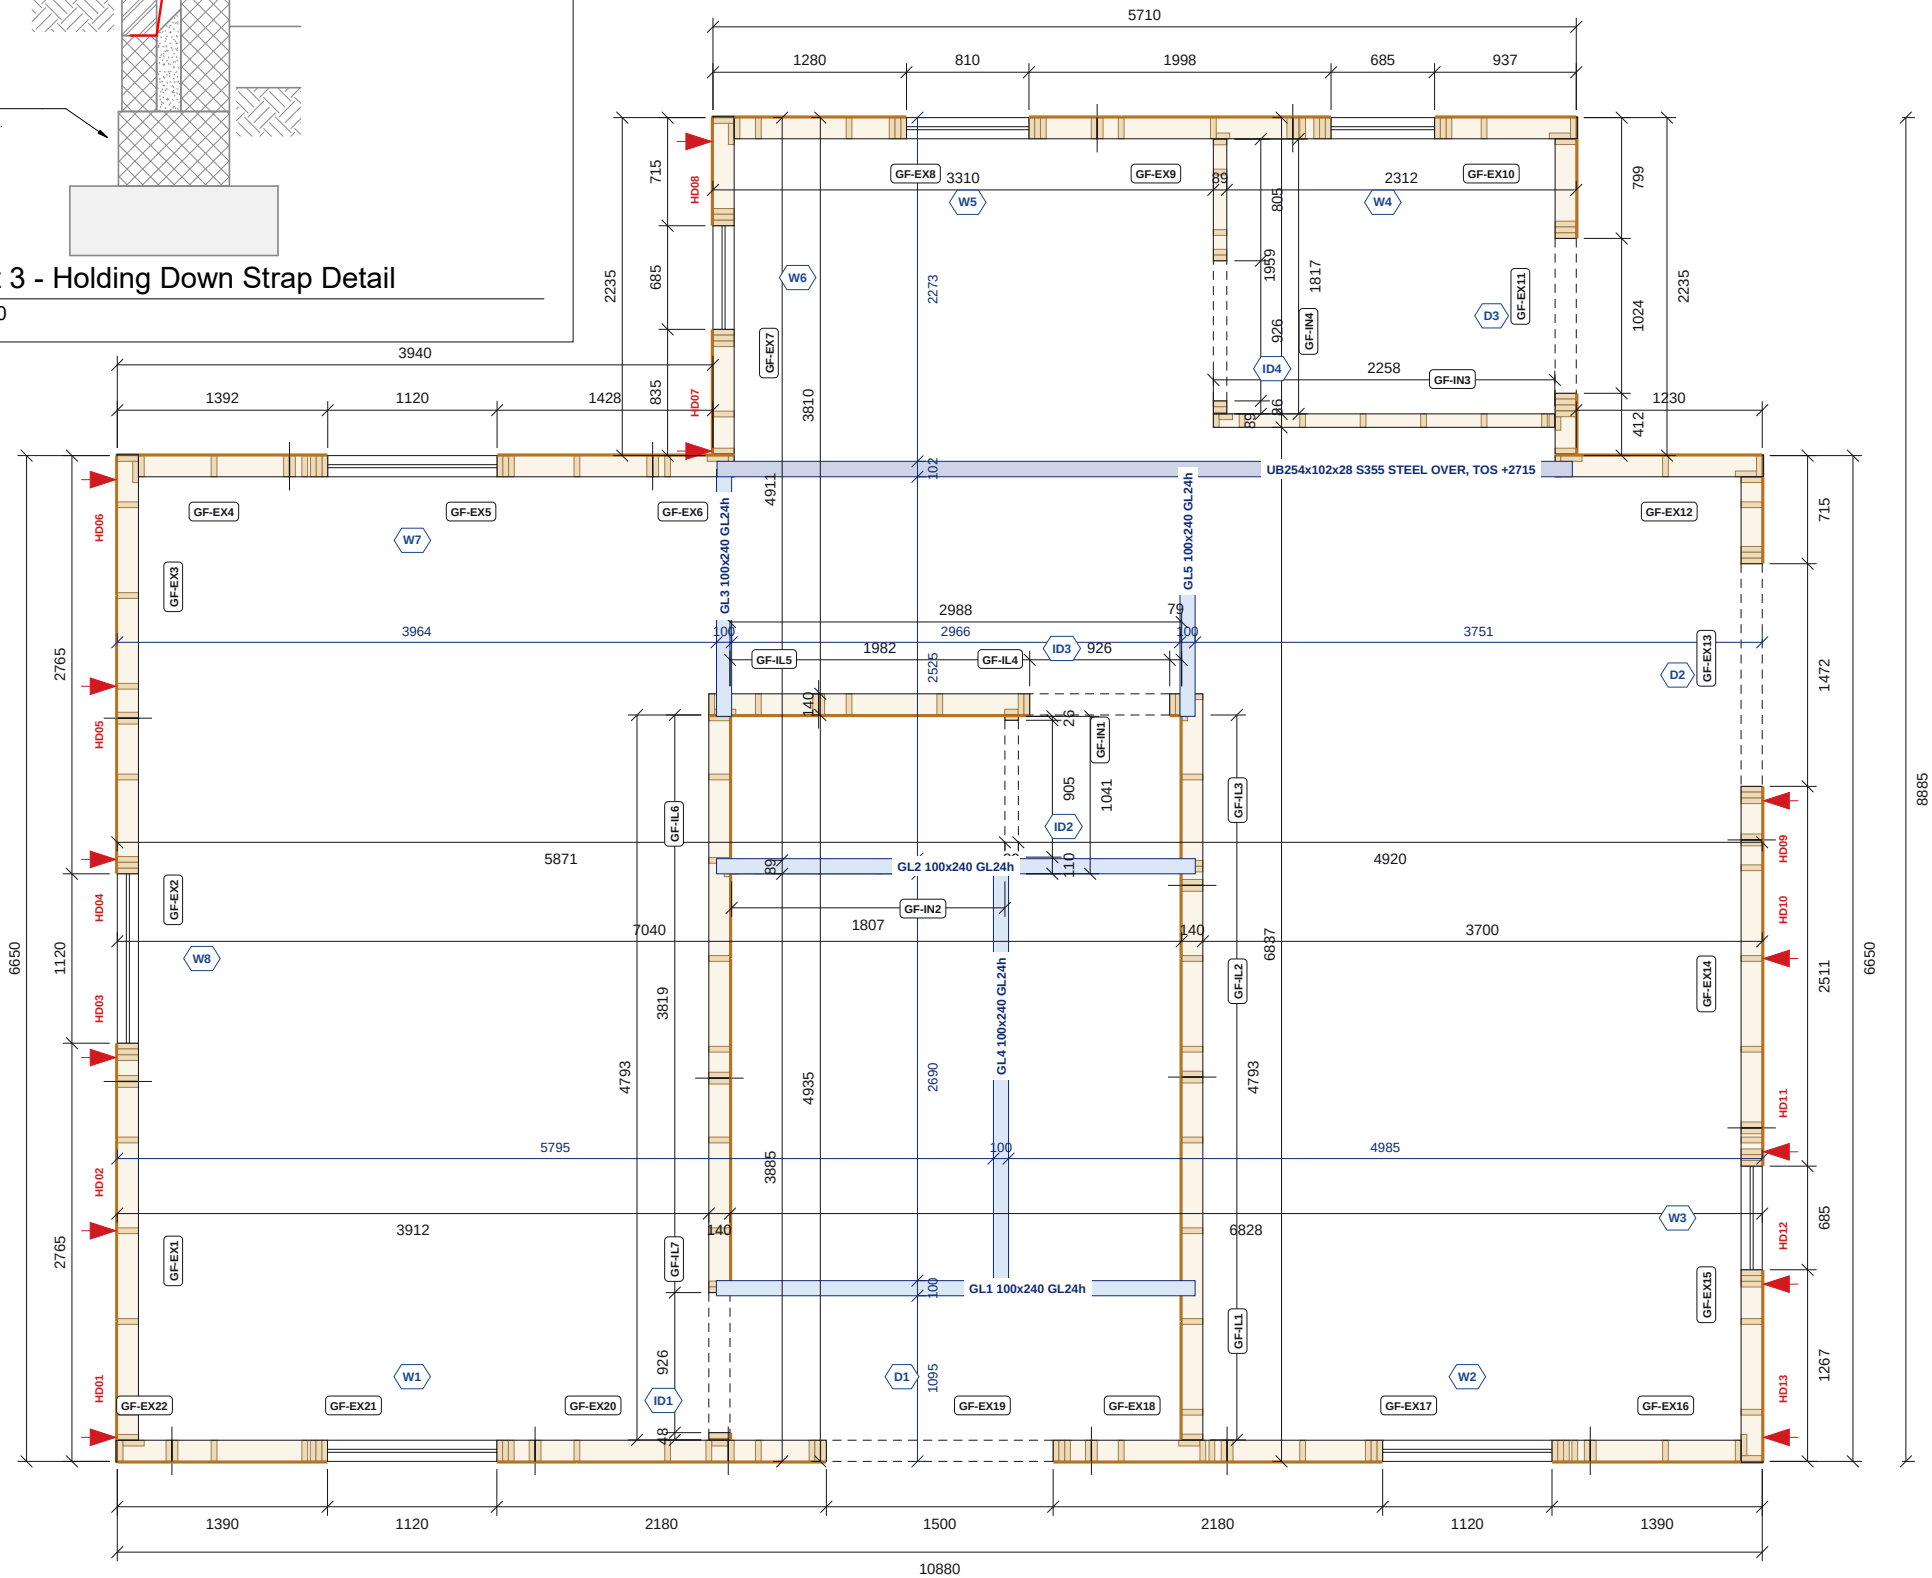

GROUND FLOOR GENERAL ARRANGEMENT PLAN

Scale 1:50 @ A3 | Plan cut at 1200 above slab

- Timber frame panel, studs cut at plan level
- 9mm OSB/3 sheathing
- Beam / steel over, set out as dimensioned
- Panel joint
- ETFSS holding-down strap



GROUND FLOOR SCHEDULES

HEAD BINDER

Section	Pieces	Run m	4.8m lengths
38x140 C16	18	51.7	12

External and load-bearing walls only. Cut-optimised 4.8m stock, 3mm kerf, +5%.

TEMPORARY BRACING (NOT SHOWN)

Item	No.	Order
Brace 4x1 treated rough-sawn, 2.7m	18	10 x 5.4m
Noggin 38x89 C16, 600	18	4 x 4.8m
M7.5x100 concrete screw (2 per noggin)	36	1 box of 100

One brace per panel joint on external / load-bearing walls (18 joints), 2 braces per 5.4m; +5%.

WINDOW BATTENS 38X43

Item	Qty	Order
Battens (head, sill, jambs)	41 / 55.0m	14 x 4.8m 38x43
Ripped from 38x89 C16 4.8m	2 per length	7 x 4.8m 38x89

External openings only. Head/sill = width + 76; jambs = height. Cut-optimised, 3mm kerf, +5%.

HOLDING-DOWN STRAPS (ETFSS)

Mark	Wall	At	On	Mark	Wall	At	On
HD01	W3/0	159	end stud	HD08	W3/2	2077	junction
HD02	W3/0	1525	stud	HD09	W3/6	2282	king D2
HD03	W3/0	2670	king W8	HD10	W3/6	3325	stud
HD04	W3/0	3980	king W8	HD11	W3/6	4603	king W3
HD05	W3/0	5125	stud	HD12	W3/6	5478	king W3
HD06	W3/0	6491	junction	HD13	W3/6	6491	junction
HD07	W3/2	30	end stud				

13 No. Simpson Strong-Tie ETFSS, engineer 26-431-S-0001 Detail 1. 'At' = from the wall's start corner along the external frame face.

OPENING SCHEDULE

Label	Width	Height	Head	Label	Width	Height	Head
W1	1120	1535	2110	D1	1500	2110	2110
W2	1120	1235	2110	D2	1472	2110	2110
W3	685	1385	2110	D3	1024	2110	2110
W4	685	1235	2110	ID1	926	2050	2050
W5	810	1535	2110	ID2	905	2050	2050
W6	685	1385	2110	ID3	926	2050	2050
W7	1120	1235	2110	ID4	926	2050	2050
W8	1120	1535	2110				

Structural opening sizes. W = window, D = external door, ID = internal door. Head level above underside of sole plate.

NOTES

- Panels: 38x140 C16 studs at 600 centres, 9mm OSB/3 to the external face (external and load-bearing walls); 38x89 C16 partitions. Panel marks refer to the manufacture drawings.
- Head binder 38x140 C16 over external and load-bearing walls only; joints staggered from panel joints.
- Temporary bracing (not shown): one 2.7m 4x1 treated brace at every panel joint of external and load-bearing walls, through a 600 38x89 noggin fixed with 2 No. M7.5x100 concrete screws.
- Window battens 38x43 to external openings: head and sill run over the jambs by 38; doors head and jambs.
- ETFSS holding-down straps (red) on the stud scheduled, to engineer's Detail 1 and Simpson guidance.
- Beams and steel over (dark blue) set out as dimensioned; TOS = top of steel above underside of sole plate. Dimensions to timber frame faces. Read with P3-SP-01, P3-FL-01 and engineer's drawing 26-431-S-0001.

REVISIONS

REV	DATE	DESCRIPTION
C01	13.09.26	Construction issue



TLS TIMBER FRAME

Design & Manufacture

Scan: 3D model + drawings



CLIENT

MP Adams

PROJECT

MP Adams Plot 3, Eckington

DRAWING TITLE

GROUND FLOOR GENERAL ARRANGEMENT

Panels, openings, holding-down straps, beams and steel over

SCALE	SIZE	DATE	DRAWN
1:50	A3	13.09.26	TS

STATUS

CONSTRUCTION


DRAWING No.

P3-GA-01

REV

C01

Do not scale. All dimensions in mm. Check all dimensions on site.

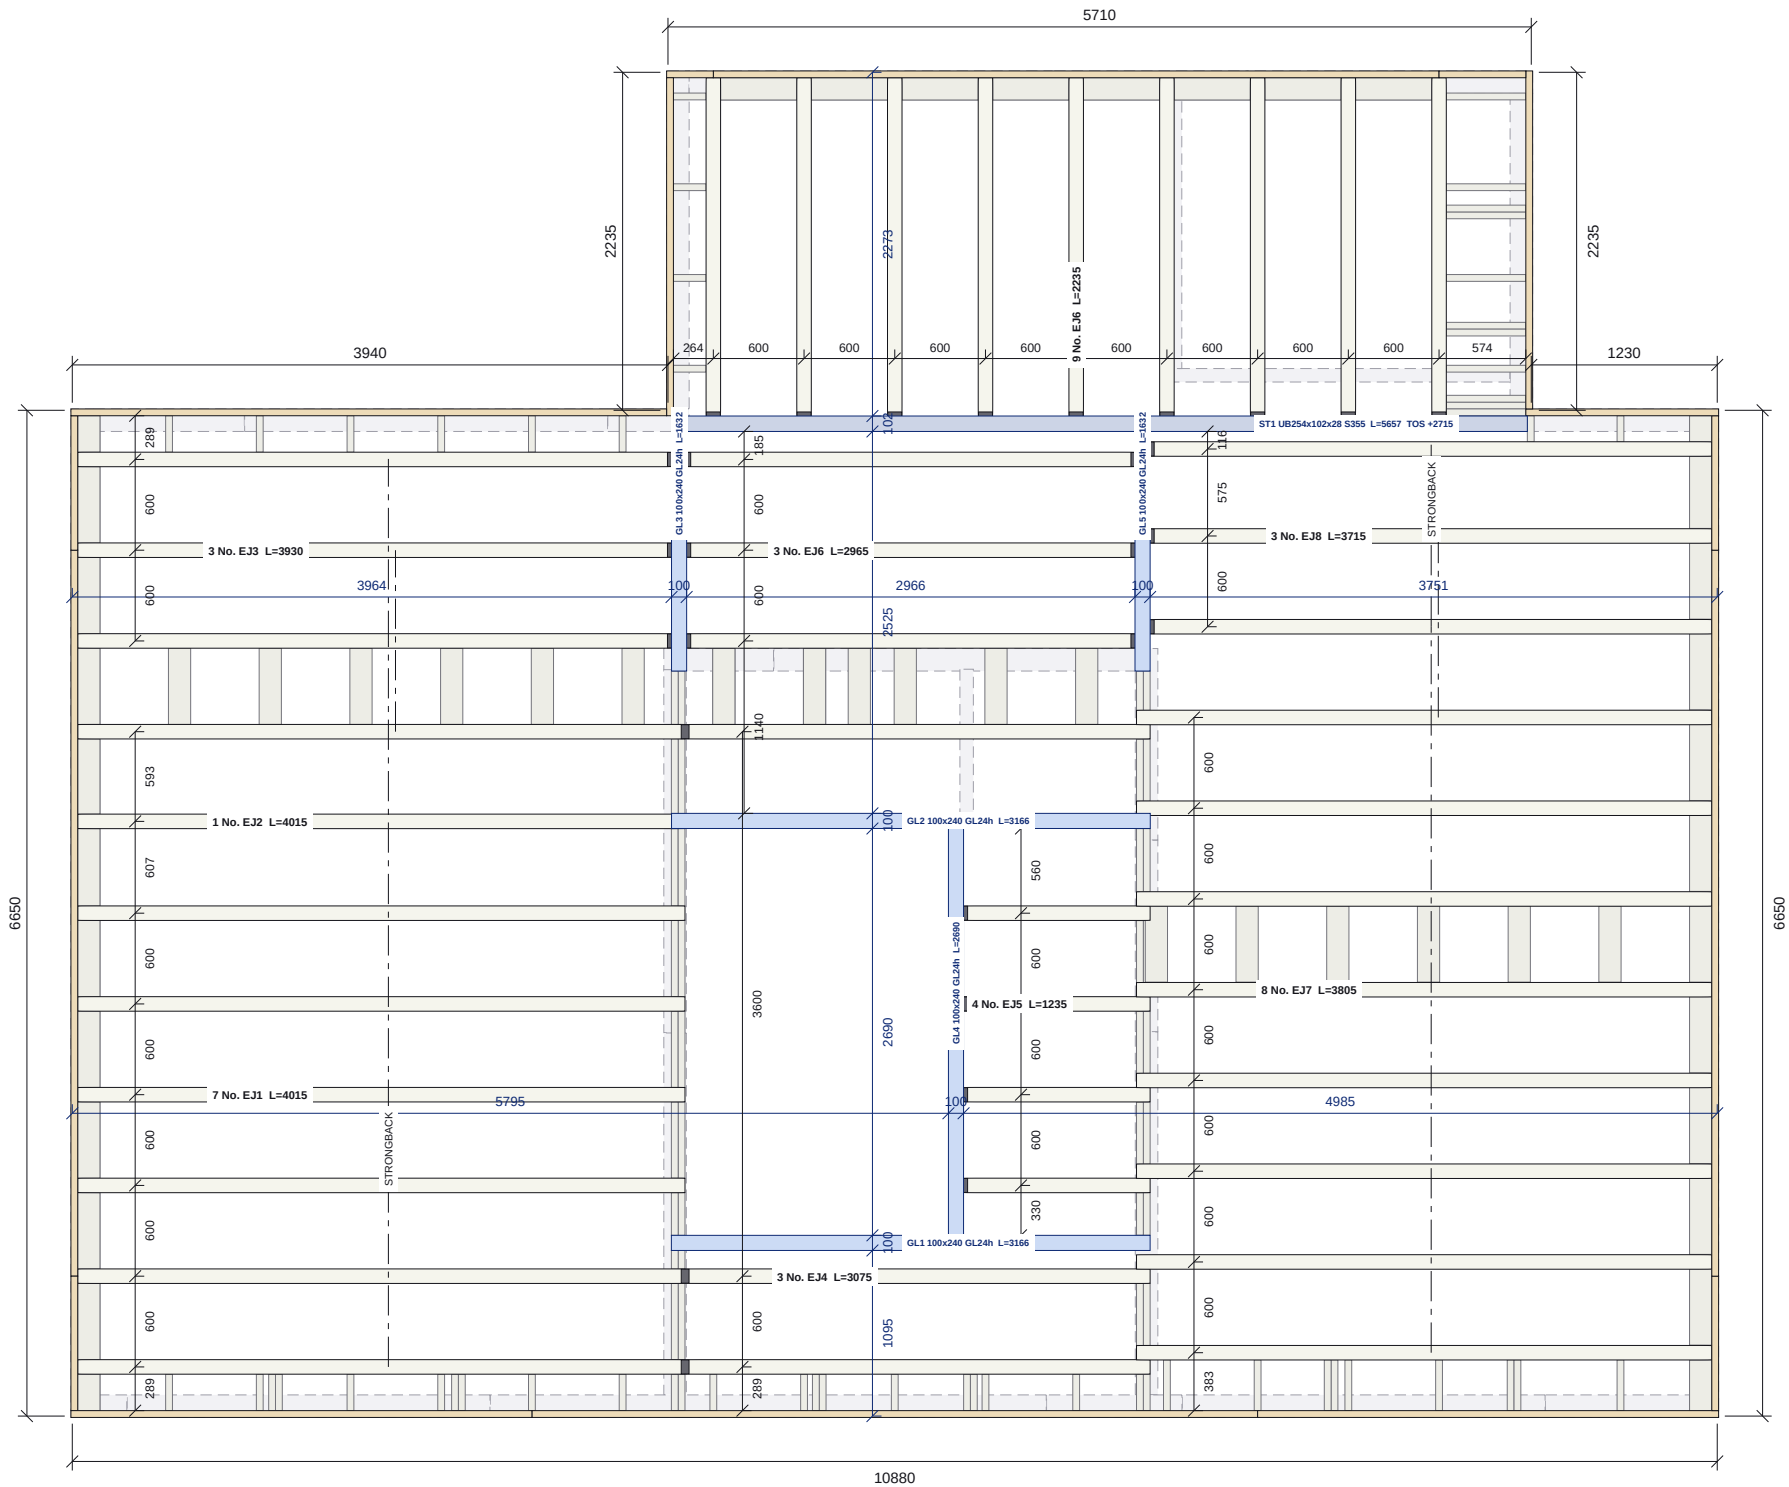

FIRST FLOOR STRUCTURE PLAN - INDICATIVE

Scale 1:50 @ A3 | Ground floor walls below shown grey dashed; joists by Acorn Timber Engineering



FIRST FLOOR STRUCTURE SCHEDULES

BEAMS

Mark	Section	Length	No.
GL1	100x240 GL24h	3166	1
GL2	100x240 GL24h	3166	1
GL3	100x240 GL24h	1632	1
GL4	100x240 GL24h	2690	1
GL5	100x240 GL24h	1632	1
ST1	UB254x102x28 S355 (TLS supply)	5657	1
PK	14mm marine ply packer, 100 wide	12.1m	5

PK: 14mm marine ply fixed to the top of each 240mm glulam to give the full 254mm floor depth (240 + 14 = 254, flush with the joists and edgebinder). Glulam and steel supplied by TLS; set out to faces as dimensioned; bearings to engineer. Steel TOS above underside of sole plate.

METAL-WEB JOISTS - BY ACORN

Type	Section	Length	No.
EJ1	97x254 metal web	4015	7
EJ2	97x254 metal web	4015	1
EJ3	97x254 metal web	3930	3
EJ4	97x254 metal web	3075	3
EJ5	97x254 metal web	1235	4
EJ6	97x254 metal web	2235	9
EJ6	97x254 metal web	2965	3
EJ7	97x254 metal web	3805	8
EJ8	97x254 metal web	3715	3

Acorn Timber Engineering supply, with 28 hangers, 2 strongback runs and noggins. Not in TLS procurement. Indicative; Acorn's layout supersedes.

EDGEBINDER, WAIST BAND, BREATHER

Item	Quantity	Order
Edgebinder 254 (45x195 + 45x59 rip)	39.4m	10 x 4.8m 45x195
45x59 C24 ribs, 3 per 45x195	39.4m	4 x 4.8m 45x195
45x195 C24 total		14 x 4.8m
OSB/3 waist band 290x9	17 strips	5 x 1197x2397
Breather 450 x 2.7m strips, 150 lap	16 strips	17 (1 roll)

Run = modelled edgebinders. Timber cut-optimised +5%; OSB +7.5%; membrane laps +5%.

FLOOR DECKING

Item	Area	Order
22mm Egger P5 600x2400	80.8 m2	61 sheets
D4 adhesive 1L (per 6.5 sheets)		10 x 1L

Laid area from the model (25 full sheets + 55 cut pieces) = 56.1 sheets, +7.5%.

NOTES

- INDICATIVE ONLY. Metal-web joists, hangers, strongbacks and noggins are designed and supplied by Acorn Timber Engineering; this drawing is superseded by Acorn's engineered floor layout on receipt.
- Glulam beams 100x240 GL24h (dark blue) set out to the faces dimensioned, bearing on multi-ply studs to engineer's drawing 26-431-S-0001. 14mm marine ply fixed to the top of each 240mm glulam to give the full 254mm floor depth. Steel UB254x102x28 S355 supplied by TLS.
- Edgebinder 254mm = 45x195 C24 with a 45x59 C24 rip fixed on top (rips cut 3 per 45x195, 3mm kerf).
- OSB/3 waist band 290x9 to the outer face of the edgebinder, strips ripped 4 per 1197x2397 sheet.
- Breather membrane over the waist band in 450 deep x 2.7m strips, each lapped 150 over the next.
- 22mm Egger P5 flooring glued with D4 adhesive, fixed to Acorn's specification. Dimensions to frame and beam faces.

REVISIONS

REV	DATE	DESCRIPTION
C01	13.09.26	Construction issue



TLS TIMBER FRAME

Design & Manufacture

Scan: 3D model + drawings



CLIENT	PROJECT
MP Adams	MP Adams Plot 3, Eckington


FIRST FLOOR STRUCTURE - INDICATIVE

Beams, set-out and metal-web joist positions; Acorn layout supersedes

SCALE	SIZE	DATE	DRAWN
1:50	A3	13.09.26	TS

STATUS	DRAWING No.	REV
CONSTRUCTION	P3-FL-01	C01

Do not scale. All dimensions in mm. Check all dimensions on site.

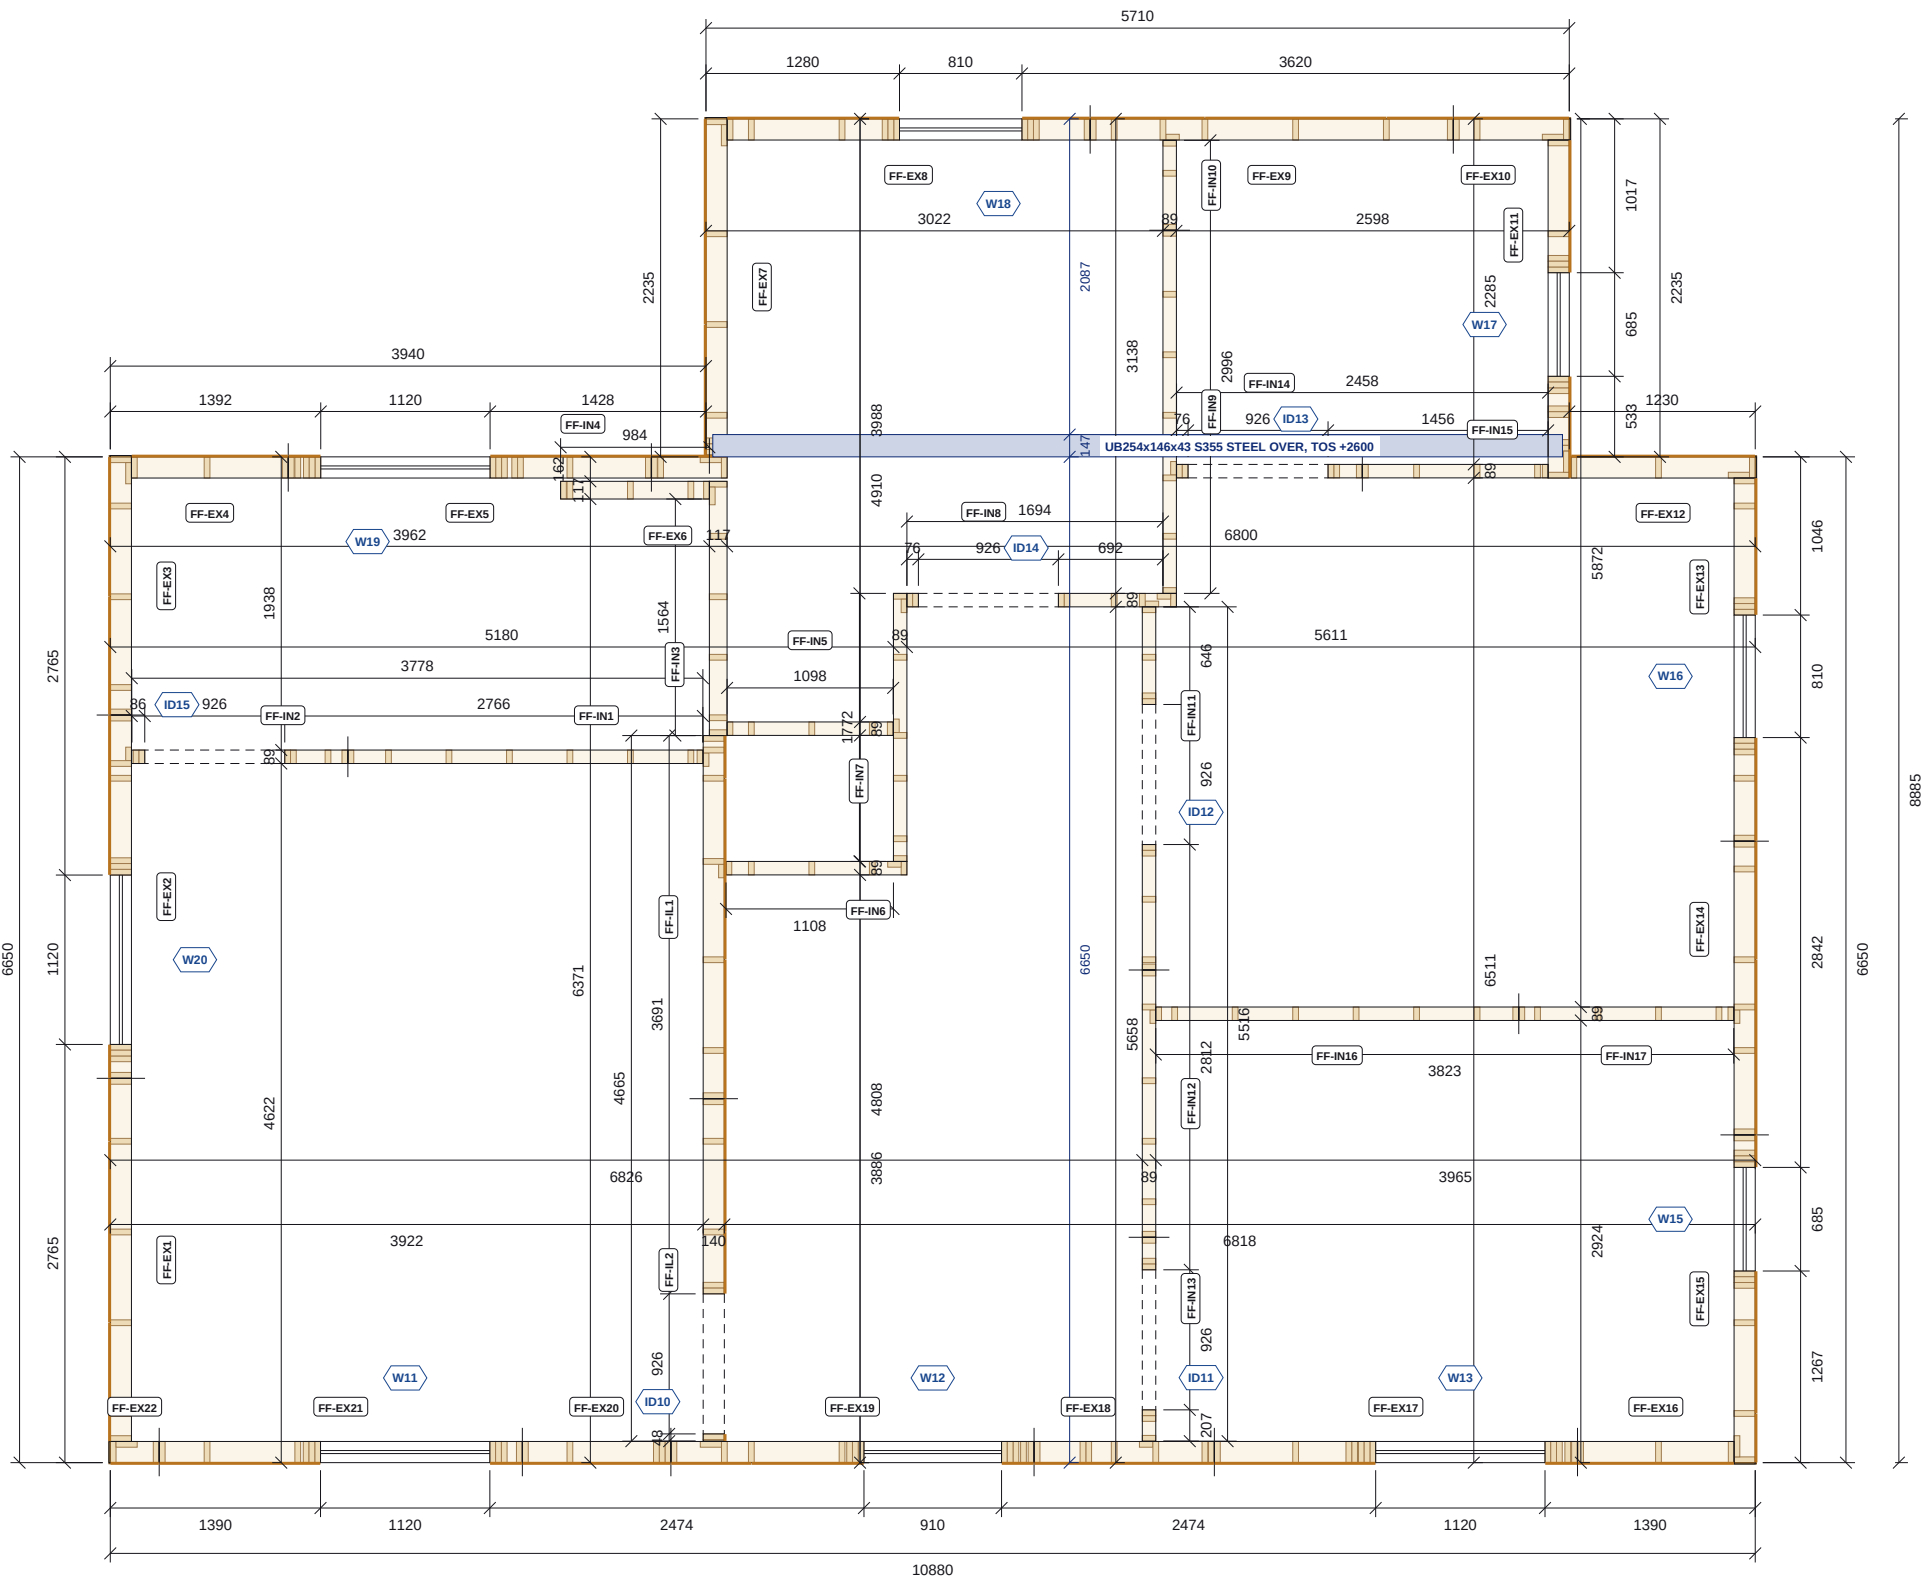

- Timber frame panel, studs cut at plan level
-
- 9mm OSB/3 sheathing

FIRST FLOOR GENERAL ARRANGEMENT PLAN

Scale 1:50 @ A3 | Plan cut at 1200 above floor deck



FIRST FLOOR SCHEDULES

HEAD BINDER

Section	Pieces	Run m	4.8m lengths
38x140 C16	15	43.6	11

External and load-bearing walls only. Cut-optimised 4.8m stock, 3mm kerf, +5%.

TEMPORARY BRACING (NOT SHOWN)

Item	No.	Order
Brace 4x1 treated rough-sawn, 2.7m	15	9 x 5.4m
Noggin 38x89 C16, 600	15	4 x 4.8m

One brace per panel joint on external / load-bearing walls (15 joints). 2 braces per 5.4m; +5%.

WINDOW BATTENS 38X43

Item	Qty	Order
Battens (head, sill, jambs)	36 / 42.8m	11 x 4.8m 38x43
Ripped from 38x89 C16 4.8m	2 per length	6 x 4.8m 38x89

External openings only. Head/sill = width + 76; jambs = height. Cut-optimised, 3mm kerf, +5%.

OPENING SCHEDULE

Label	Width	Height	Head	Label	Width	Height	Head
W11	1120	1487	2050	W20	1120	1487	2050
W12	910	1487	2050	ID10	926	2050	2050
W13	1120	1337	2050	ID11	926	2050	2050
W15	685	1337	2050	ID12	926	2050	2050
W16	810	1337	2050	ID13	926	2050	2050
W17	685	1337	2050	ID14	926	2050	2050
W18	810	1337	2050	ID15	926	2050	2050
W19	1120	1187	2050				

Structural opening sizes. Head level above underside of panel bottom rail.

NOTES

- Panels: 38x140 C16 studs at 600 centres, 9mm OSB/3 to the external face (external and load-bearing walls); 38x89 C16 partitions. Panel marks refer to the manufacture drawings.
- Head binder 38x140 C16 over external and load-bearing walls only; joints staggered from panel joints.
- Temporary bracing (not shown): one 2.7m 4x1 treated brace at every panel joint of external and load-bearing walls, through a 600 38x89 noggin nailed to the deck.
- Window battens 38x43 to external openings: head and sill run over the jambs by 38; doors head and jambs.
- Steel over (dark blue, TLS supply) set out as dimensioned; TOS = top of steel above top of 22mm deck. Attic trusses and cut roof members over by Acorn Timber Engineering, see P3-RF-02. Dimensions to timber frame faces. Read with P3-FL-01 and engineer's drawing 26-431-S-0001.

REVISIONS

REV	DATE	DESCRIPTION
C01	13.09.26	Construction issue



TLS TIMBER FRAME

Design & Manufacture

Scan: 3D model + drawings




CLIENT	PROJECT
MP Adams	MP Adams Plot 3, Eckington

DRAWING TITLE

FIRST FLOOR GENERAL ARRANGEMENT


SCALE	SIZE	DATE	DRAWN
1:50	A3	13.09.26	TS

STATUS	DRAWING No.	REV
CONSTRUCTION	P3-GA-02	C01

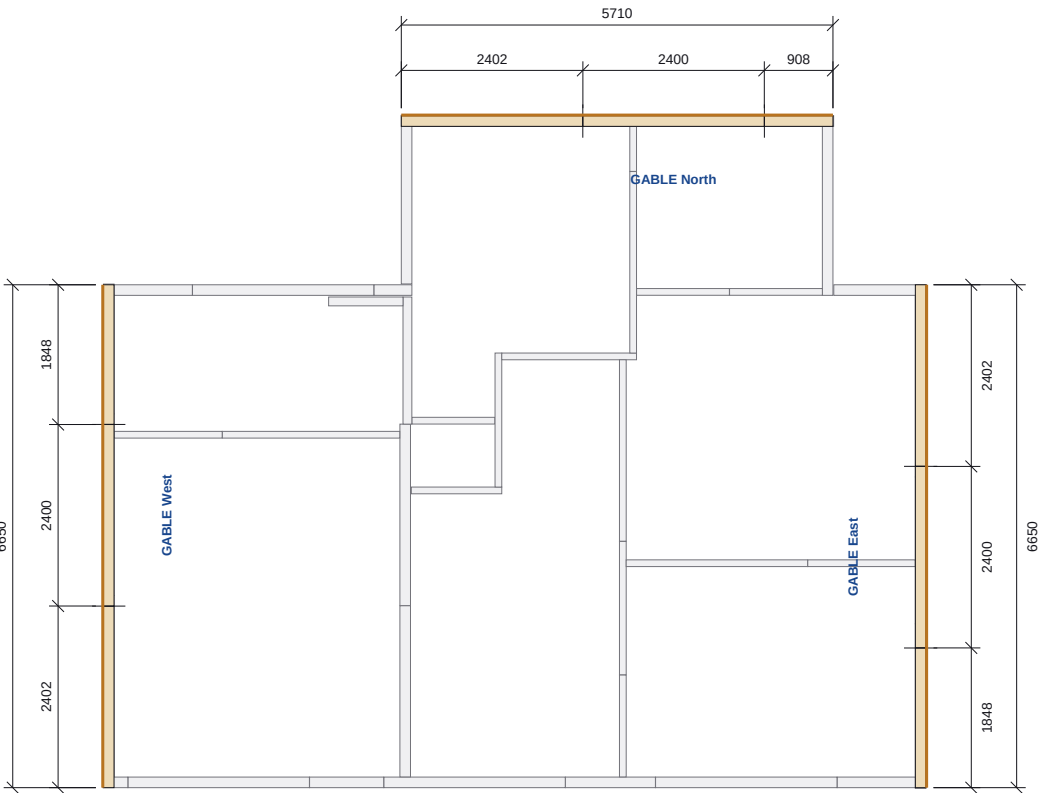

KEY PLAN - GABLES ON FIRST FLOOR WALLS

Scale 1:100 | Gable panels heavy; first floor walls below grey

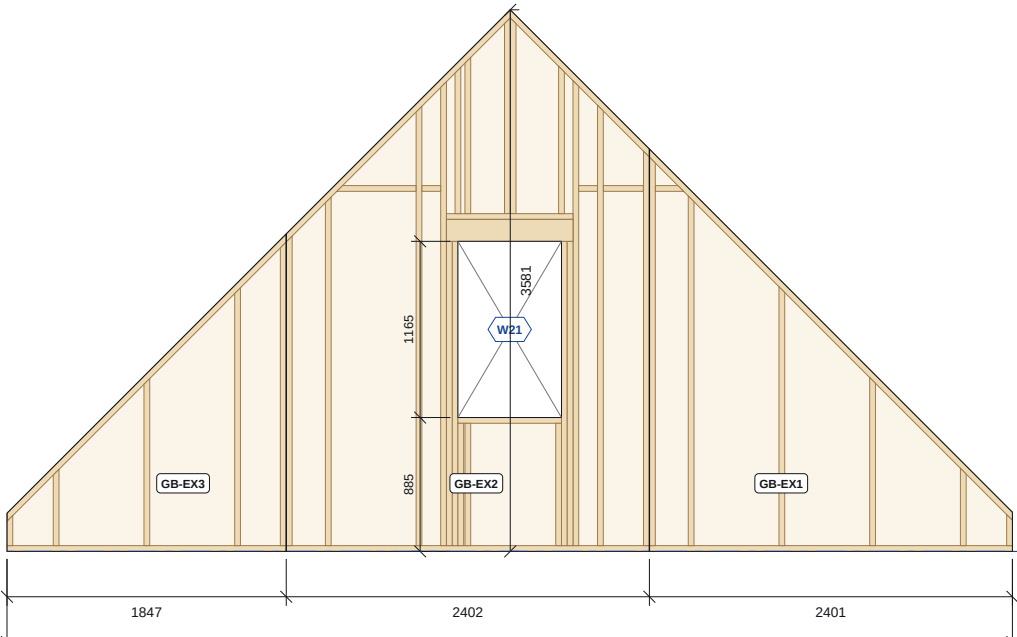

Gable base = top of first floor head binder, +5115 above slab

GABLE WEST - ELEVATION FROM OUTSIDE

Scale 1:50 | Wall 2, panels GB-EX1, GB-EX2, GB-EX3

GABLE PANEL SCHEDULES

GABLE PANELS

Mark	Gable	Width	Height
GB-EX1	West	2400	2659
GB-EX2	West	2400	3581
GB-EX3	West	1846	2098
GB-EX4	North	2400	2656
GB-EX5	North	2400	3111
GB-EX6	North	906	1162
GB-EX7	East	2400	2658
GB-EX8	East	2400	3580
GB-EX9	East	1846	2097

Width along the wall, height to the top of the raked rail.

TEMPORARY BRACING (NOT SHOWN)

Item	No.	Order
Brace 4x1 treated rough-sawn, 2.7m	6	4 x 5.4m
Noggin 38x89 C16, 600 (nailed)	6	2 x 4.8m

One brace per gable panel joint. +5%.

WINDOW BATTENS 38X43

Item	Qty	Order
Battens (head, sill, jambs)	4 / 3.9m	2 x 4.8m 38x43
Ripped from 38x89 C16 4.8m	2 per length	1 x 4.8m 38x89

Head/sill = width + 76; jambs = height. +5%.

OPENING SCHEDULE

Label	Width	Height	Head
W21	685	1165	2050

Head level above underside of panel bottom rail.

NOTES

- Gable panels: 38x140 C16 studs, 9mm OSB/3 to the external face, raked top rails to the roof pitch. No sole plate or head binder: panels bear on the first floor head binder and truss bottom chords.
- Set out each gable from the outer edges of its central (ridge) panel to the ends of the first floor wall below, as dimensioned on the key plan.
- Temporary bracing (not shown): one 2.7m 4x1 treated brace at every gable panel joint, fixed through a 600 38x89 noggin nailed to the deck.
- Window battens 38x43 to gable openings: head and sill run over the jambs by 38.
- Opening heads are measured from the underside of the panel bottom rail. Read with P3-GA-02 and P3-RF-02.

REVISIONS

REV	DATE	DESCRIPTION
C01	13.09.26	Construction issue



TLS TIMBER FRAME

Design & Manufacture

Scan: 3D model + drawings



CLIENT	PROJECT
MP Adams	MP Adams Plot 3, Eckington


DRAWING TITLE
GABLE PANELS GENERAL ARRANGEMENT

Key plan 1:100, gable framing elevations 1:50

SCALE	SIZE	DATE	DRAWN
1:100 / 1:50	A3	13.09.26	TS

STATUS	DRAWING No.	REV
CONSTRUCTION	P3-GA-03	C01


Do not scale. All dimensions in mm. Check all dimensions on site.

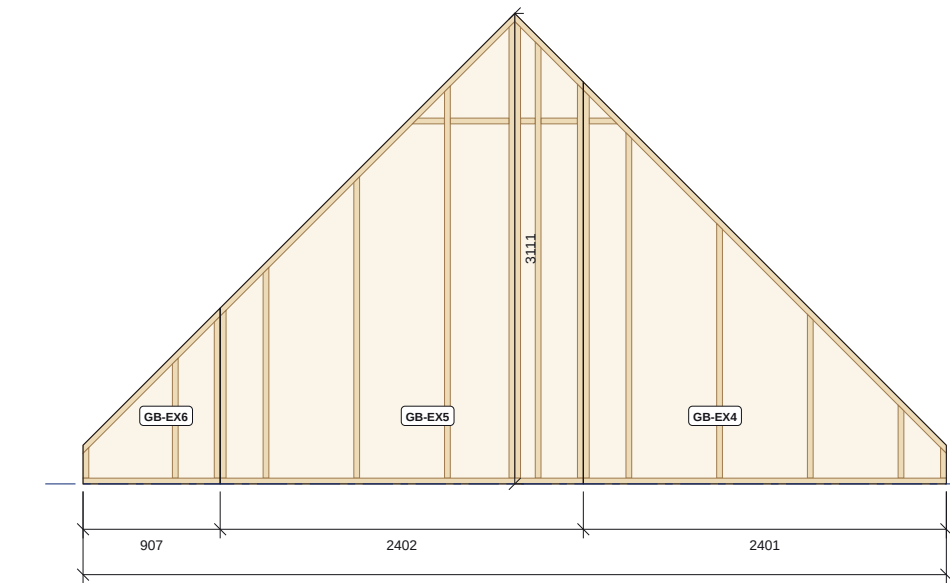

Gable base = top of first floor head binder, +5115 above slab

GABLE NORTH - ELEVATION FROM OUTSIDE

Scale 1:50 | Wall 6, panels GB-EX4, GB-EX5, GB-EX6

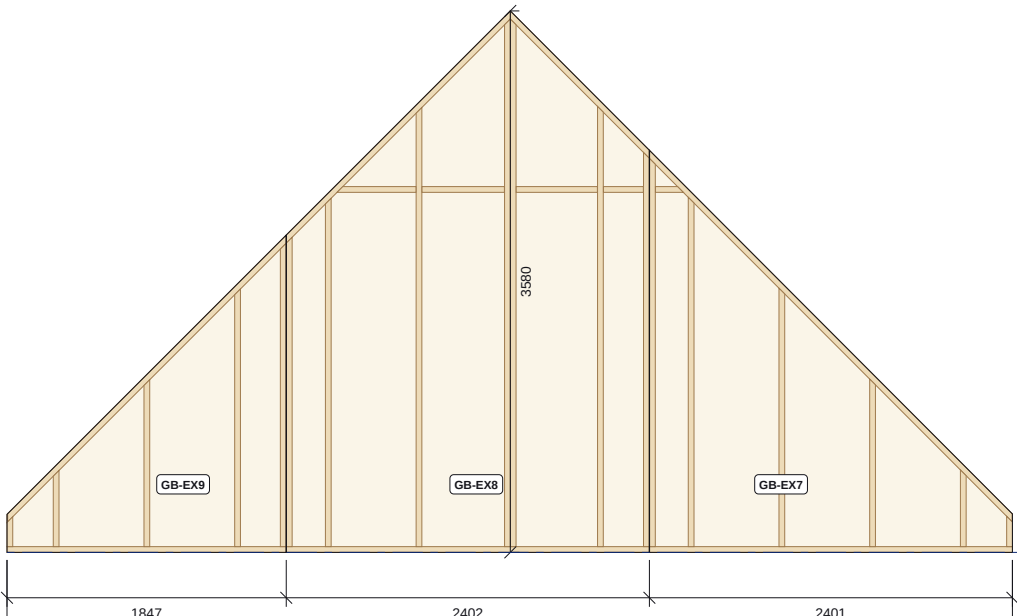

Gable base = top of first floor head binder, +5115 above slab


GABLE EAST - ELEVATION FROM OUTSIDE

Scale 1:50 | Wall 16, panels GB-EX7, GB-EX8, GB-EX9

Do not scale. All dimensions in mm. Check all dimensions on site.

ROOF - CEILING LEVEL PLAN

Scale 1:50 @ A3 | Plan at +5415; first floor walls below grey dashed

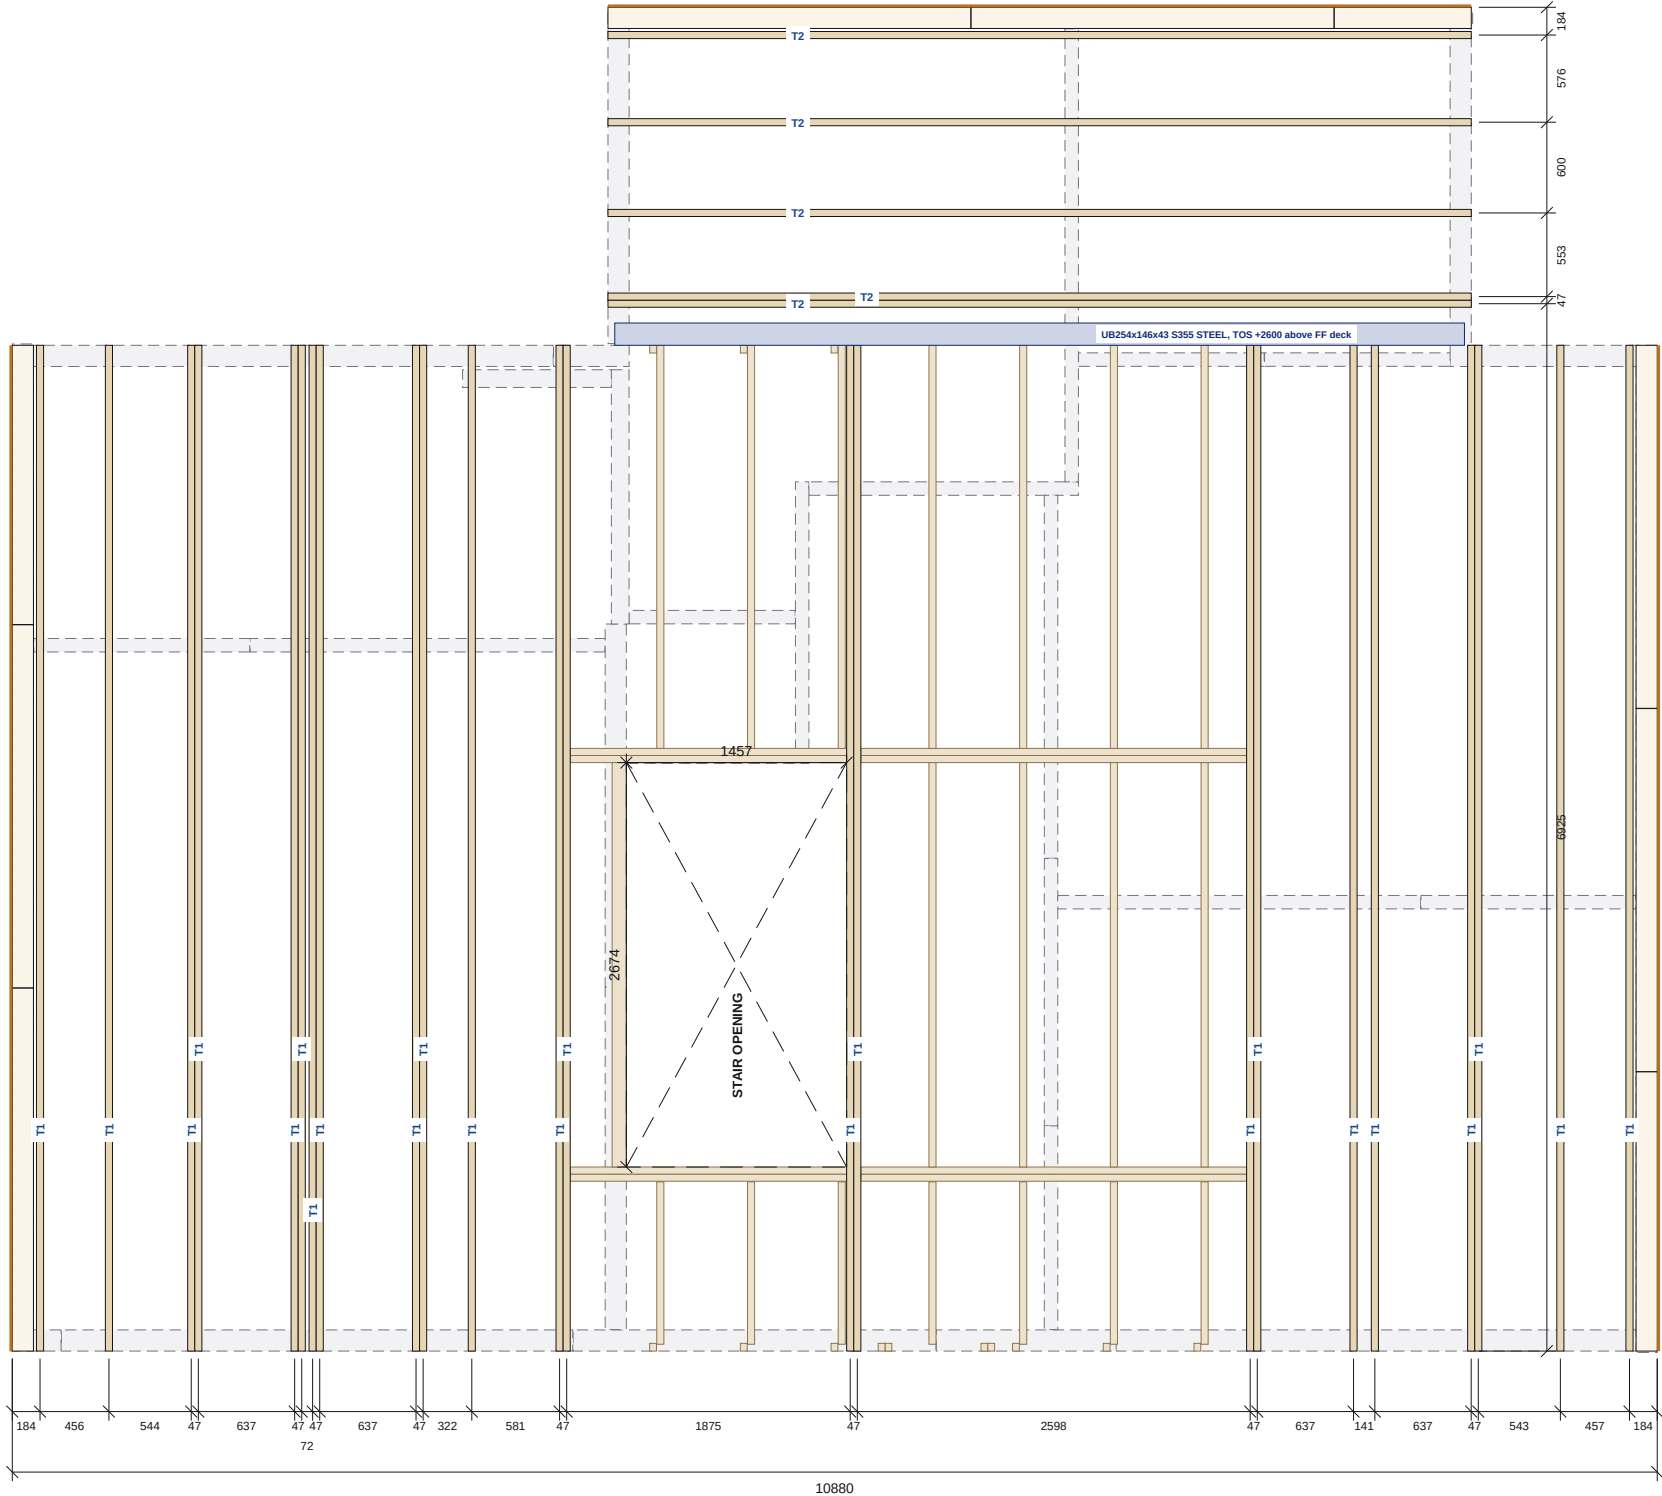

CEILING LEVEL SCHEDULE

ATTIC TRUSSES

Type	No.	Span	Height	Doubles
T1	23	6650	3588	8
T2	5	5710	3118	1

Span over external frame faces; height from underside of bottom chord.

CEILING-LEVEL ROOF MEMBERS

Item	No.
Cut roof members bearing at ceiling level	40

Pop-out valley and junction framing, indicative.

NOTES

- Ceiling level: attic truss bottom chords bear on the first floor head binder at +5115 above slab.
- Truss bottom chords form the attic floor zone; double trusses trim the stair void and the pop-out junction.
- Cut roof members at the pop-out valley shown at their low (ceiling-level) ends; see P3-RF-02.
- Truss and roof member positions indicative; read with the truss manufacturer's layout and engineer's drawing 26-431-S-0001.

REVISIONS

REV	DATE	DESCRIPTION
C01	13.09.26	Construction issue



TLS TIMBER FRAME

Design & Manufacture

Scan: 3D model + drawings



CLIENT

MP Adams

PROJECT

MP Adams Plot 3, Eckington

DRAWING TITLE

ROOF - CEILING LEVEL

Attic truss bottom chords and ceiling-level roof members

SCALE	SIZE	DATE	DRAWN
1:50	A3	13.09.26	TS

STATUS

CONSTRUCTION

DRAWING No.

P3-RF-01


REV

C01

Do not scale. All dimensions in mm. Check all dimensions on site.

ROOF - TRUSS LAYOUT PLAN

Scale 1:50 @ A3 | Ridge lines blue dash-dot; first floor walls below grey dashed

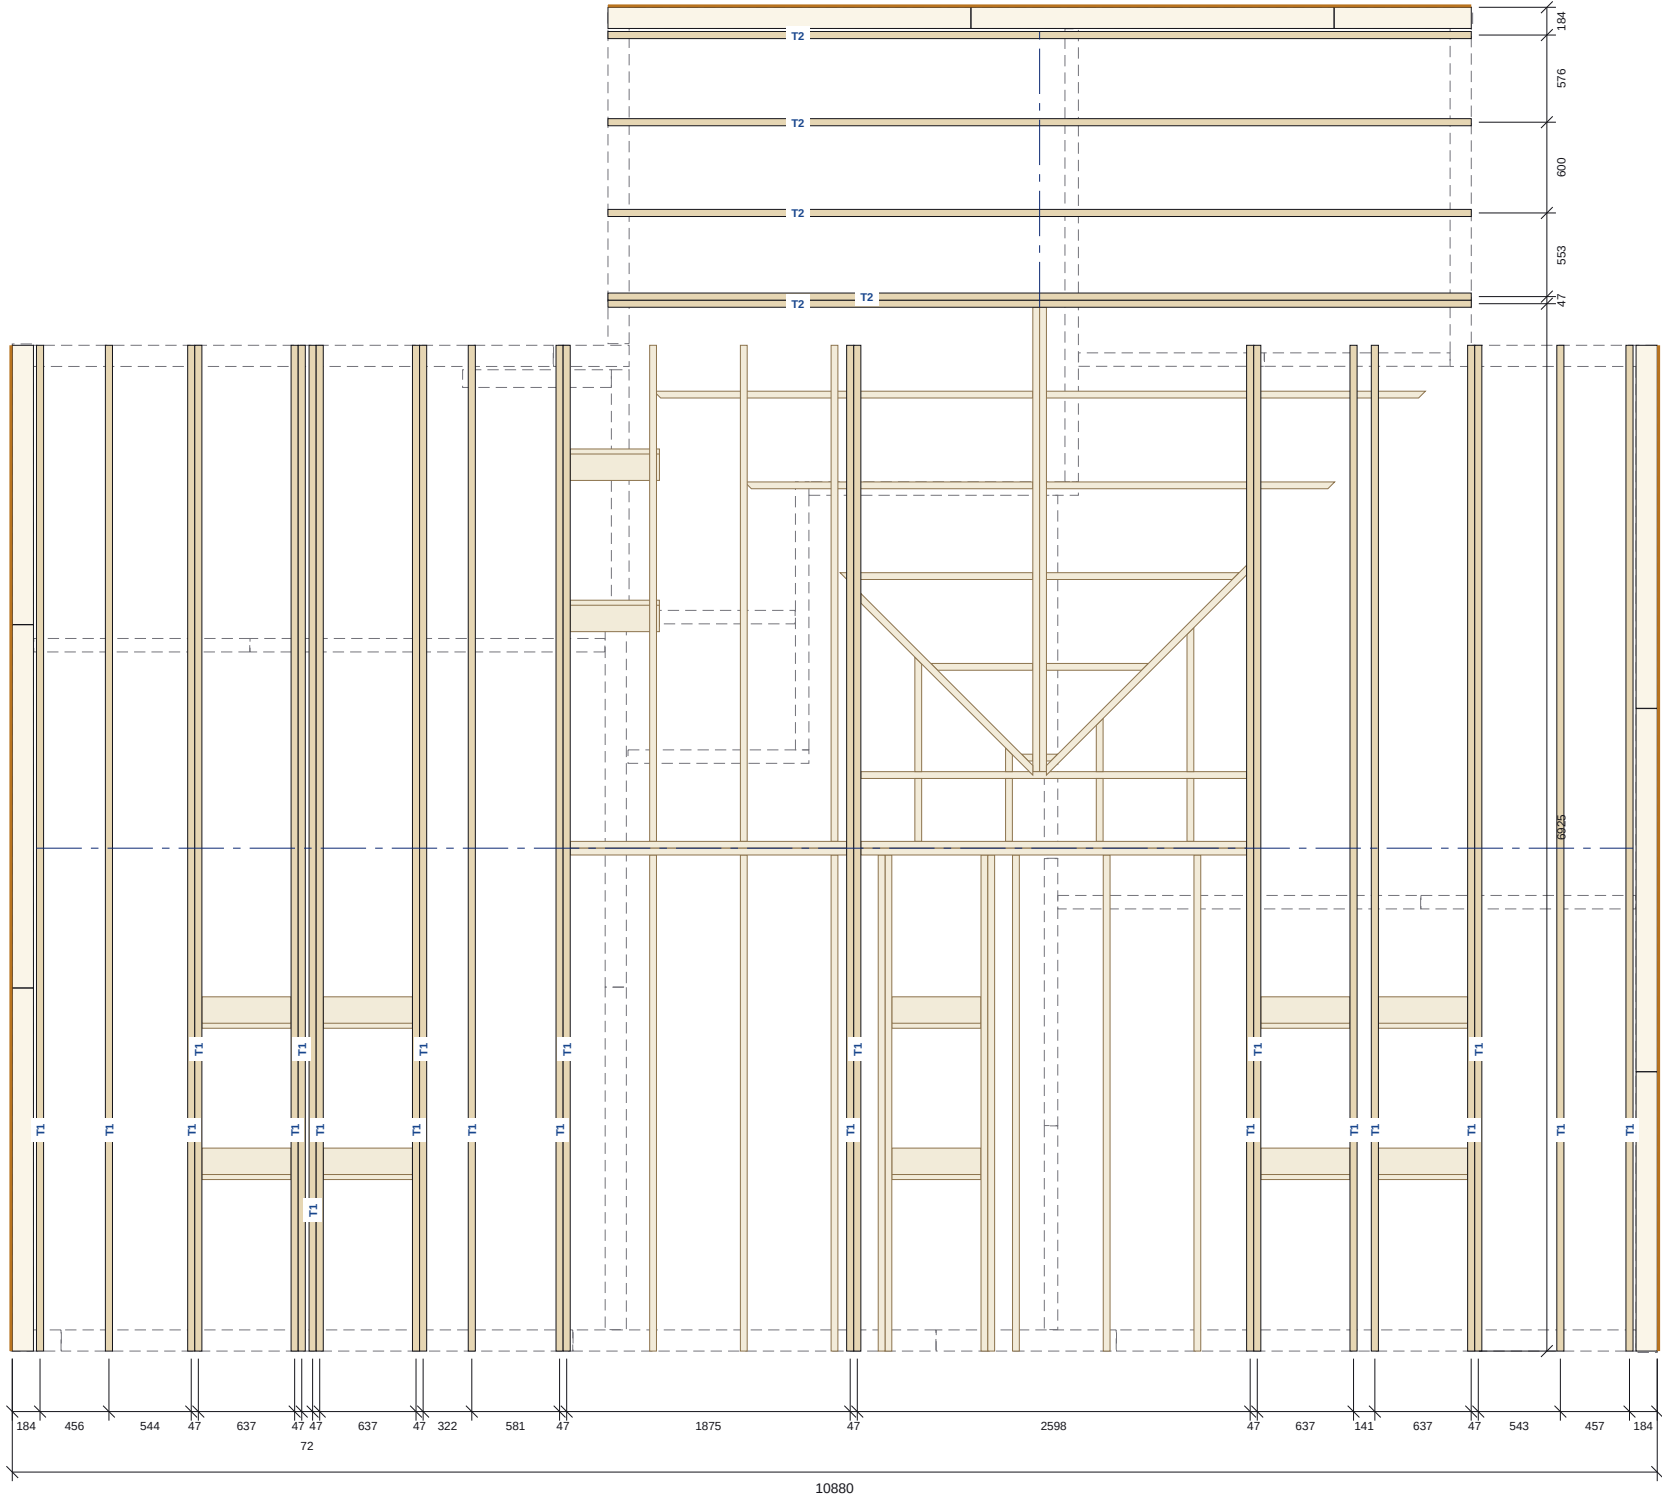

ROOF SCHEDULE

ATTIC TRUSSES

Type	No.	Span	Height	Doubles
T1	23	6650	3588	8
T2	5	5710	3118	1

Span over external frame faces; height from underside of bottom chord.

CUT ROOF MEMBERS

Item	No.
Valley / rafter / ridge / purlin members (above ceiling)	64

Indicative, at the pop-out junction.

NOTES

- Attic trusses T1 (main roof) and T2 (pop-out roof) at the centres dimensioned; doubles where shown.
- Cut roof members (valley, rafters, ridge and purlins) at the pop-out junction shown indicatively.
- Gable panels see P3-GA-03. Truss and roof member positions indicative; read with the truss manufacturer's layout and engineer's drawing 26-431-S-0001.

REVISIONS

REV	DATE	DESCRIPTION
C01	13.09.26	Construction issue



TLS TIMBER FRAME

Design & Manufacture

Scan: 3D model + drawings



CLIENT

MP Adams

PROJECT

MP Adams Plot 3, Eckington

DRAWING TITLE

ROOF - TRUSS LAYOUT

Attic trusses, cut roof members and set-out

SCALE	SIZE	DATE	DRAWN
1:50	A3	13.09.26	TS

STATUS

CONSTRUCTION


DRAWING No.

P3-RF-02

REV


C01

Do not scale. All dimensions in mm. Check all dimensions on site.

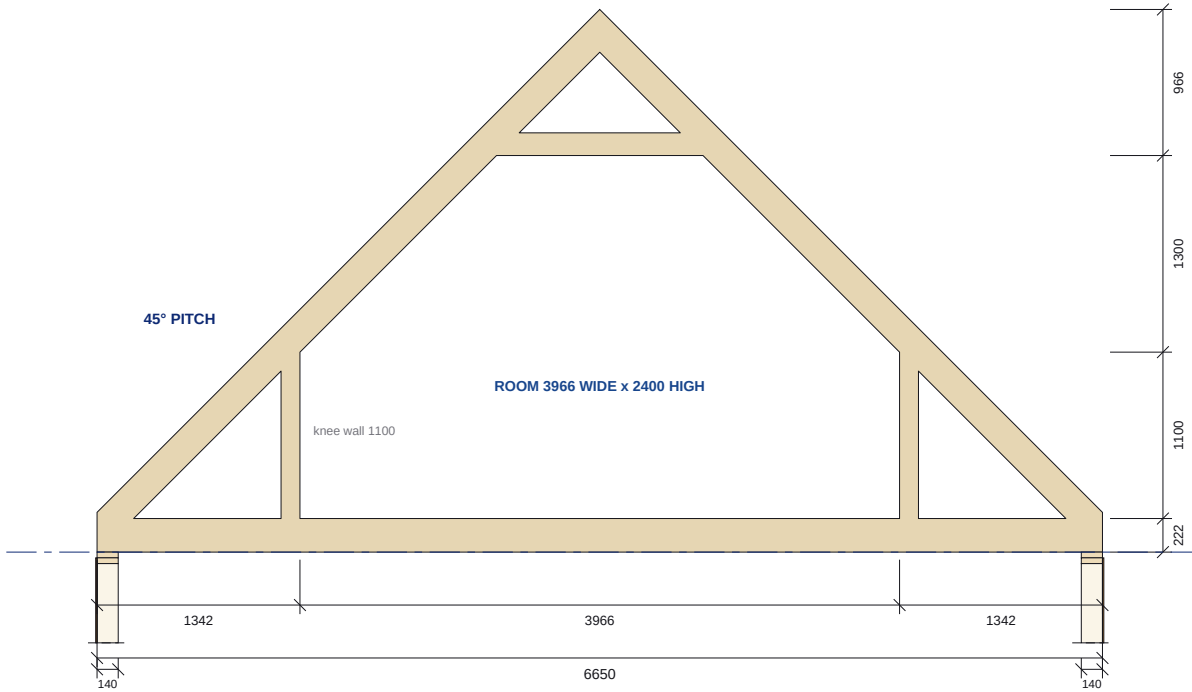

TRUSS T1 PROFILE (23 NO.)

Scale 1:50 | Main roof

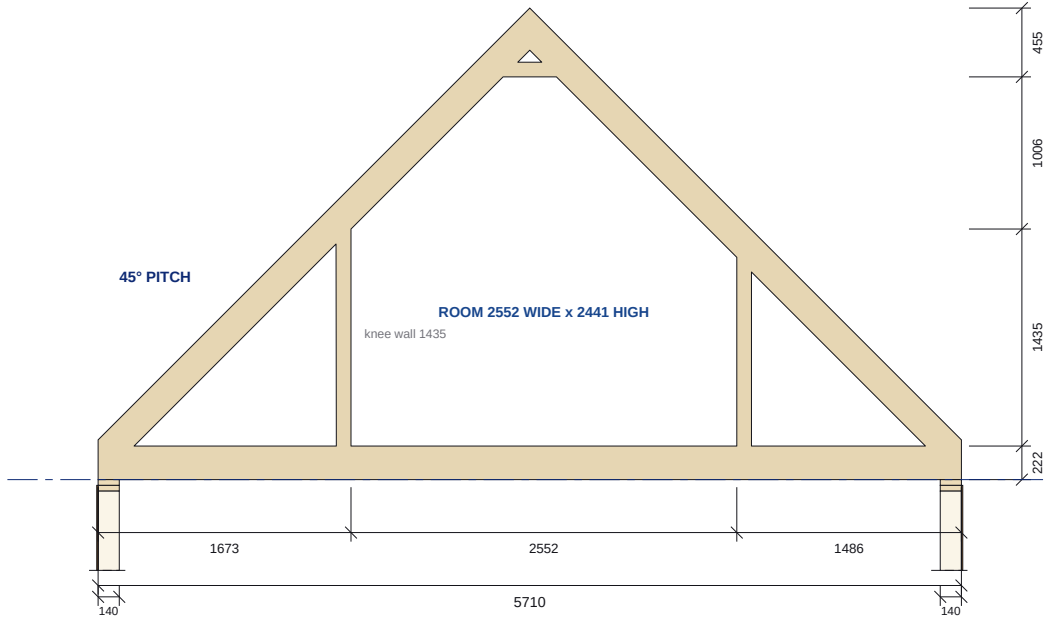

TRUSS T2 PROFILE (5 NO.)

Scale 1:50 | Pop-out roof

TRUSS SCHEDULE

ATTIC TRUSSES

Type	No.	Span	Height	Pitch	Room
T1	23	6650	3588	45	3966 x 2400
T2	5	5710	3118	45	2552 x 2441

Span over external frame faces; height from underside of bottom chord; pitch in degrees; room = clear width x height to the collar.

NOTES

- Attic truss profiles as modelled, for co-ordination. Member sizes, connections and bracing to the truss manufacturer's design.
- Heights from the underside of the bottom chord (+5115 above slab, top of first floor head binder). Trusses bear on the first floor external wall head binders shown below each profile.
- Room-in-roof clear sizes are between the inner faces of the attic studs and under the collar tie.

REVISIONS

REV	DATE	DESCRIPTION
C01	13.09.26	Construction issue



TLS TIMBER FRAME

Design & Manufacture

Scan: 3D model + drawings



CLIENT	PROJECT
MP Adams	MP Adams Plot 3, Eckington

DRAWING TITLE

ROOF - TRUSS PROFILES T1 / T2

Attic truss profiles with span, height and room dimensions


SCALE	SIZE	DATE	DRAWN
1:50	A3	13.09.26	TS

STATUS	DRAWING No.	REV
CONSTRUCTION	P3-RF-03	C01

Do not scale. All dimensions in mm. Check all dimensions on site.

SECTION A-A

Scale 1:50 @ A3 | Main building, looking east

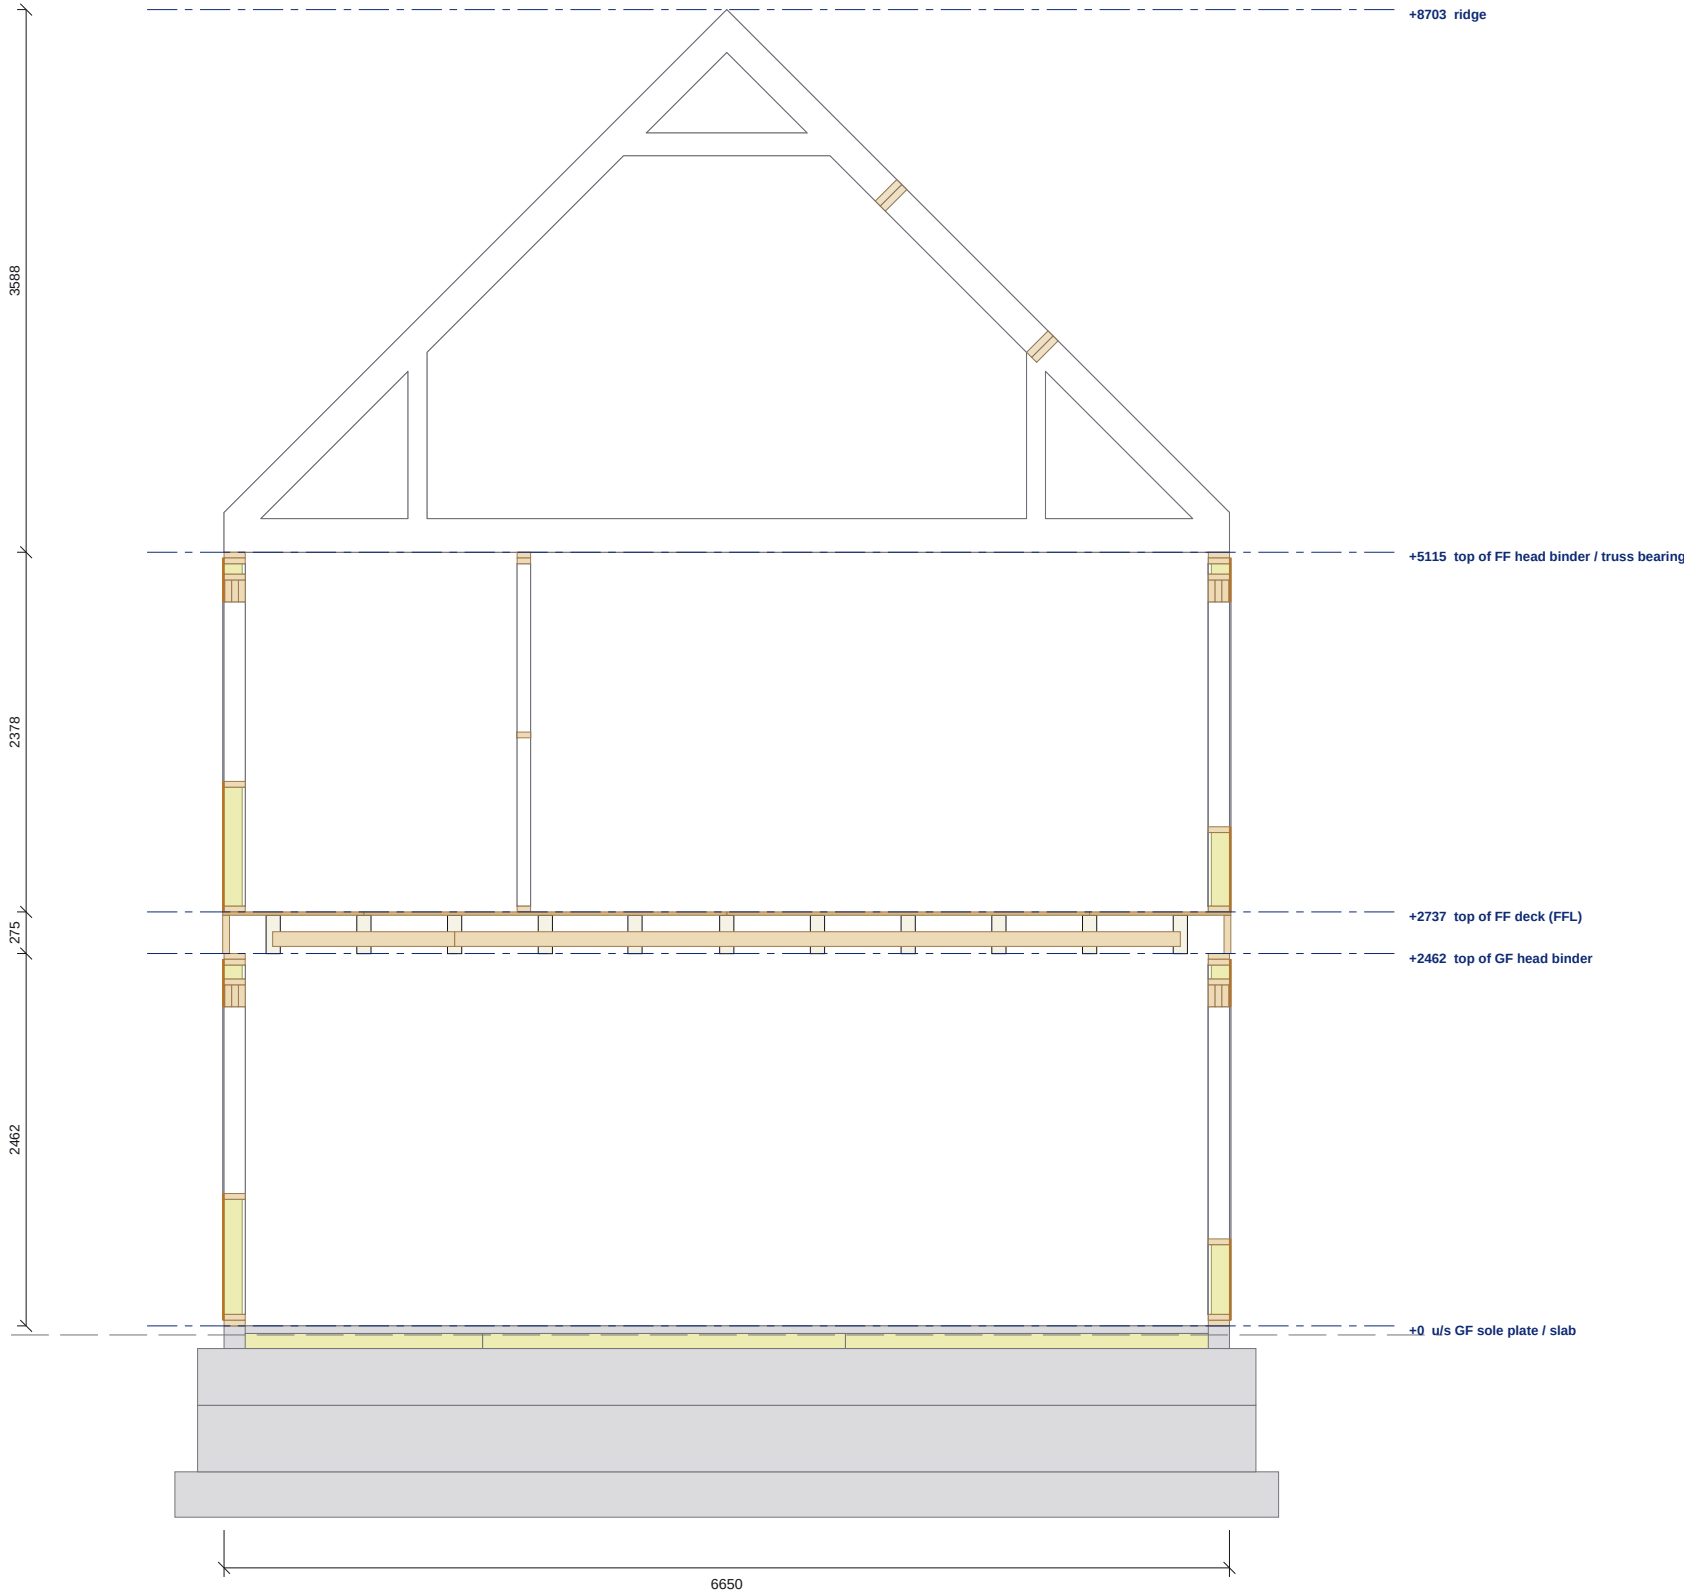

SECTION A-A SCHEDULE

LEVELS	
Level	mm
u/s GF sole plate / slab	+0
top of GF head binder	+2462
top of FF deck (FFL)	+2737
top of FF head binder / truss bearing	+5115
ridge	+8703

Above underside of the ground floor sole plate.

ELEMENTS CUT	
Element	Pieces cut
Sole plate / head binder	7
Panel framing	47
Substructure (by others)	24
Edgebinder	2
Metal-web joists (Acorn)	11
22mm deck	4
Cut roof members	4

- NOTES
- Section A-A after architect's drawing 17.007-303, cut through the timber frame model; members up to 700mm beyond the cut shown in outline.
 - Timber frame: 38x140 C16 external walls with 9mm OSB/3 and 120mm PIR; 254 metal-web first floor (Acorn); attic trusses over.
 - Levels are above the underside of the ground floor sole plate (+0). Substructure by others, shown for reference only.

REVISIONS		
REV	DATE	DESCRIPTION
C01	13.09.26	Construction issue



TLS
TIMBER FRAME DESIGN SUITE

TLS TIMBER FRAME
Design & Manufacture
Scan: 3D model + drawings



CLIENT	PROJECT
MP Adams	MP Adams Plot 3, Eckington

DRAWING TITLE			
SECTION A-A			
Main building, looking east			


SCALE	SIZE	DATE	DRAWN
1:50	A3	13.09.26	TS

STATUS	DRAWING No.	REV
CONSTRUCTION	P3-SE-01	C01

Do not scale. All dimensions in mm. Check all dimensions on site.

SECTION B-B

Scale 1:50 @ A3 | Pop-out, looking south

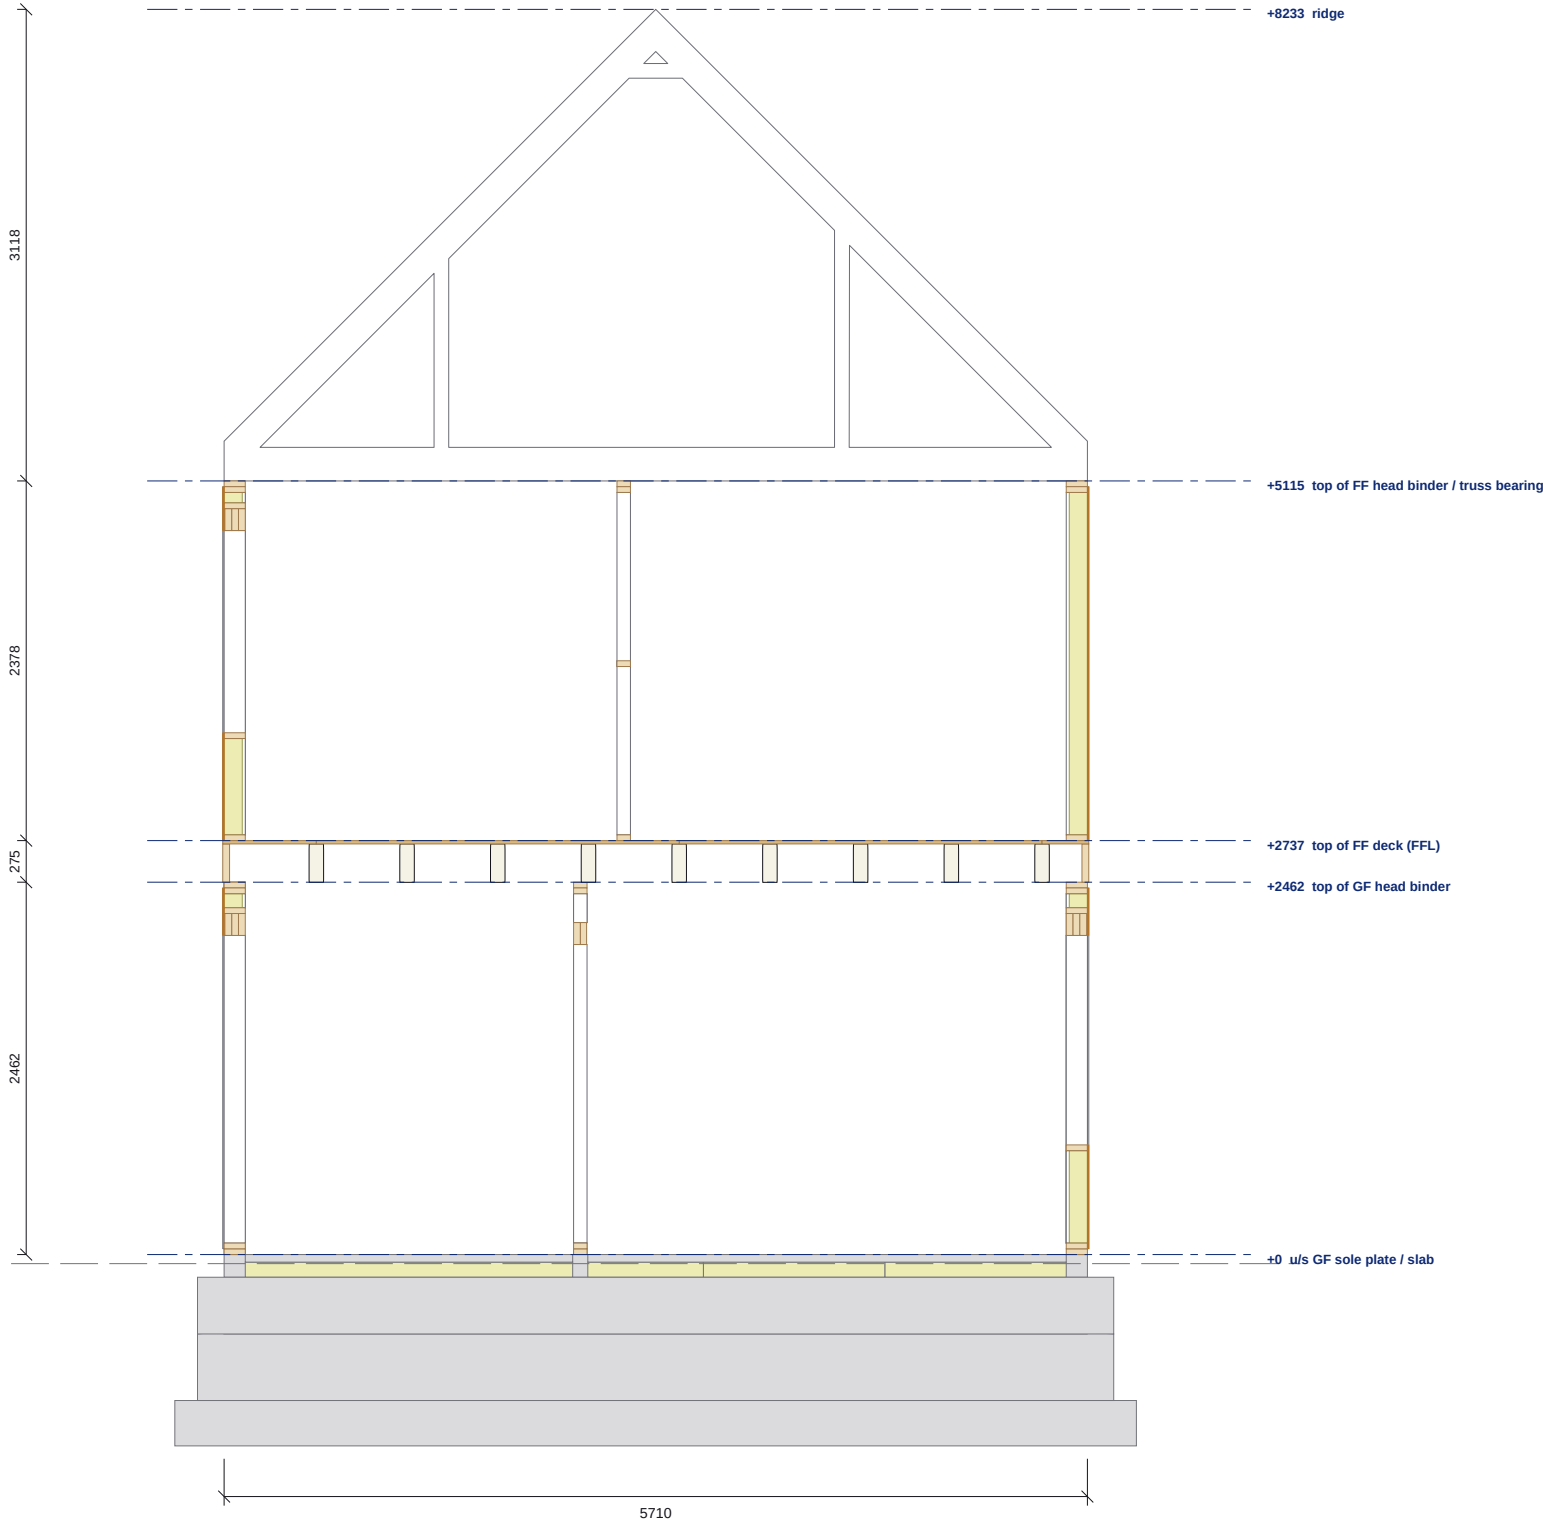

SECTION B-B SCHEDULE

LEVELS	
Level	mm
u/s GF sole plate / slab	+0
top of GF head binder	+2462
top of FF deck (FFL)	+2737
top of FF head binder / truss bearing	+5115
ridge	+8233

Above underside of the ground floor sole plate.

ELEMENTS CUT	
Element	Pieces cut
Sole plate / head binder	9
Panel framing	41
Substructure (by others)	14
Edgebinder	2
Metal-web joists (Acorn)	9
22mm deck	4

- NOTES
- Section B-B after architect's drawing 17.007-303, cut through the timber frame model; members up to 700mm beyond the cut shown in outline.
 - Timber frame: 38x140 C16 external walls with 9mm OSB/3 and 120mm PIR; 254 metal-web first floor (Acorn); attic trusses over.
 - Levels are above the underside of the ground floor sole plate (+0). Substructure by others, shown for reference only.

REVISIONS		
REV	DATE	DESCRIPTION
C01	13.09.26	Construction issue



TLS TIMBER FRAME
Design & Manufacture
Scan: 3D model + drawings



CLIENT	PROJECT
MP Adams	MP Adams Plot 3, Eckington

DRAWING TITLE			
SECTION B-B			
Pop-out, looking south			

SCALE	SIZE	DATE	DRAWN
1:50	A3	13.09.26	TS

STATUS	DRAWING No.	REV
CONSTRUCTION	P3-SE-02	C01

Do not scale. All dimensions in mm. Check all dimensions on site.

FRONT ELEVATION (SOUTH)

Scale 1:50 @ A3 | Levels right: storey levels + visible ridges; left: sills and heads on this face



FRONT ELEVATION (SOUTH) SCHEDULE

LEVELS ON THIS FACE

Level	mm
u/s GF sole plate	+0
top of GF head binder	+2462
top of FF deck (FFL)	+2737
top of FF head binder	+5115
ridge	+8703

Above underside of the ground floor sole plate.

OPENINGS ON THIS FACE

Label	Level	Width	Height	Sill	Head
D1	GF	1500	2110	0	2110
W1	GF	1120	1535	575	2110
W2	GF	1120	1235	875	2110
W11	FF	1120	1487	3300	4787
W12	FF	910	1487	3300	4787
W13	FF	1120	1337	3450	4787

Sill and head levels above underside of the GF sole plate.

NOTES

- Construction elevation of the timber frame: OSB/3 face of external and gable panels, sole plates, head binders and edgebinders. Cladding, roof covering and windows by others, not shown.
- Level lines shown are only those relevant to this face: storey levels, visible ridges and the sill / head levels of the openings on this face.
- Levels above the underside of the ground floor sole plate (+0). Openings are structural openings; see P3-GA-01 / P3-GA-02 / P3-GA-03.

REVISIONS

REV	DATE	DESCRIPTION
C01	13.09.26	Construction issue



TLS TIMBER FRAME
Design & Manufacture
Scan: 3D model + drawings



CLIENT MP Adams	PROJECT MP Adams Plot 3, Eckington
--------------------	---------------------------------------


DRAWING TITLE FRONT ELEVATION (SOUTH) Timber frame construction elevation			
SCALE 1:50	SIZE A3	DATE 13.09.26	DRAWN TS

SCALE :50	SIZE A3	DATE 13.09.26	DRAWN TS
STATUS CONSTRUCTION	DRAWING No. P3-EL-01		REV C01

Do not scale. All dimensions in mm. Check all dimensions on site.

SIDE ELEVATION (EAST)

Scale 1:50 @ A3 | Levels right: storey levels + visible ridges; left: sills and heads on this face

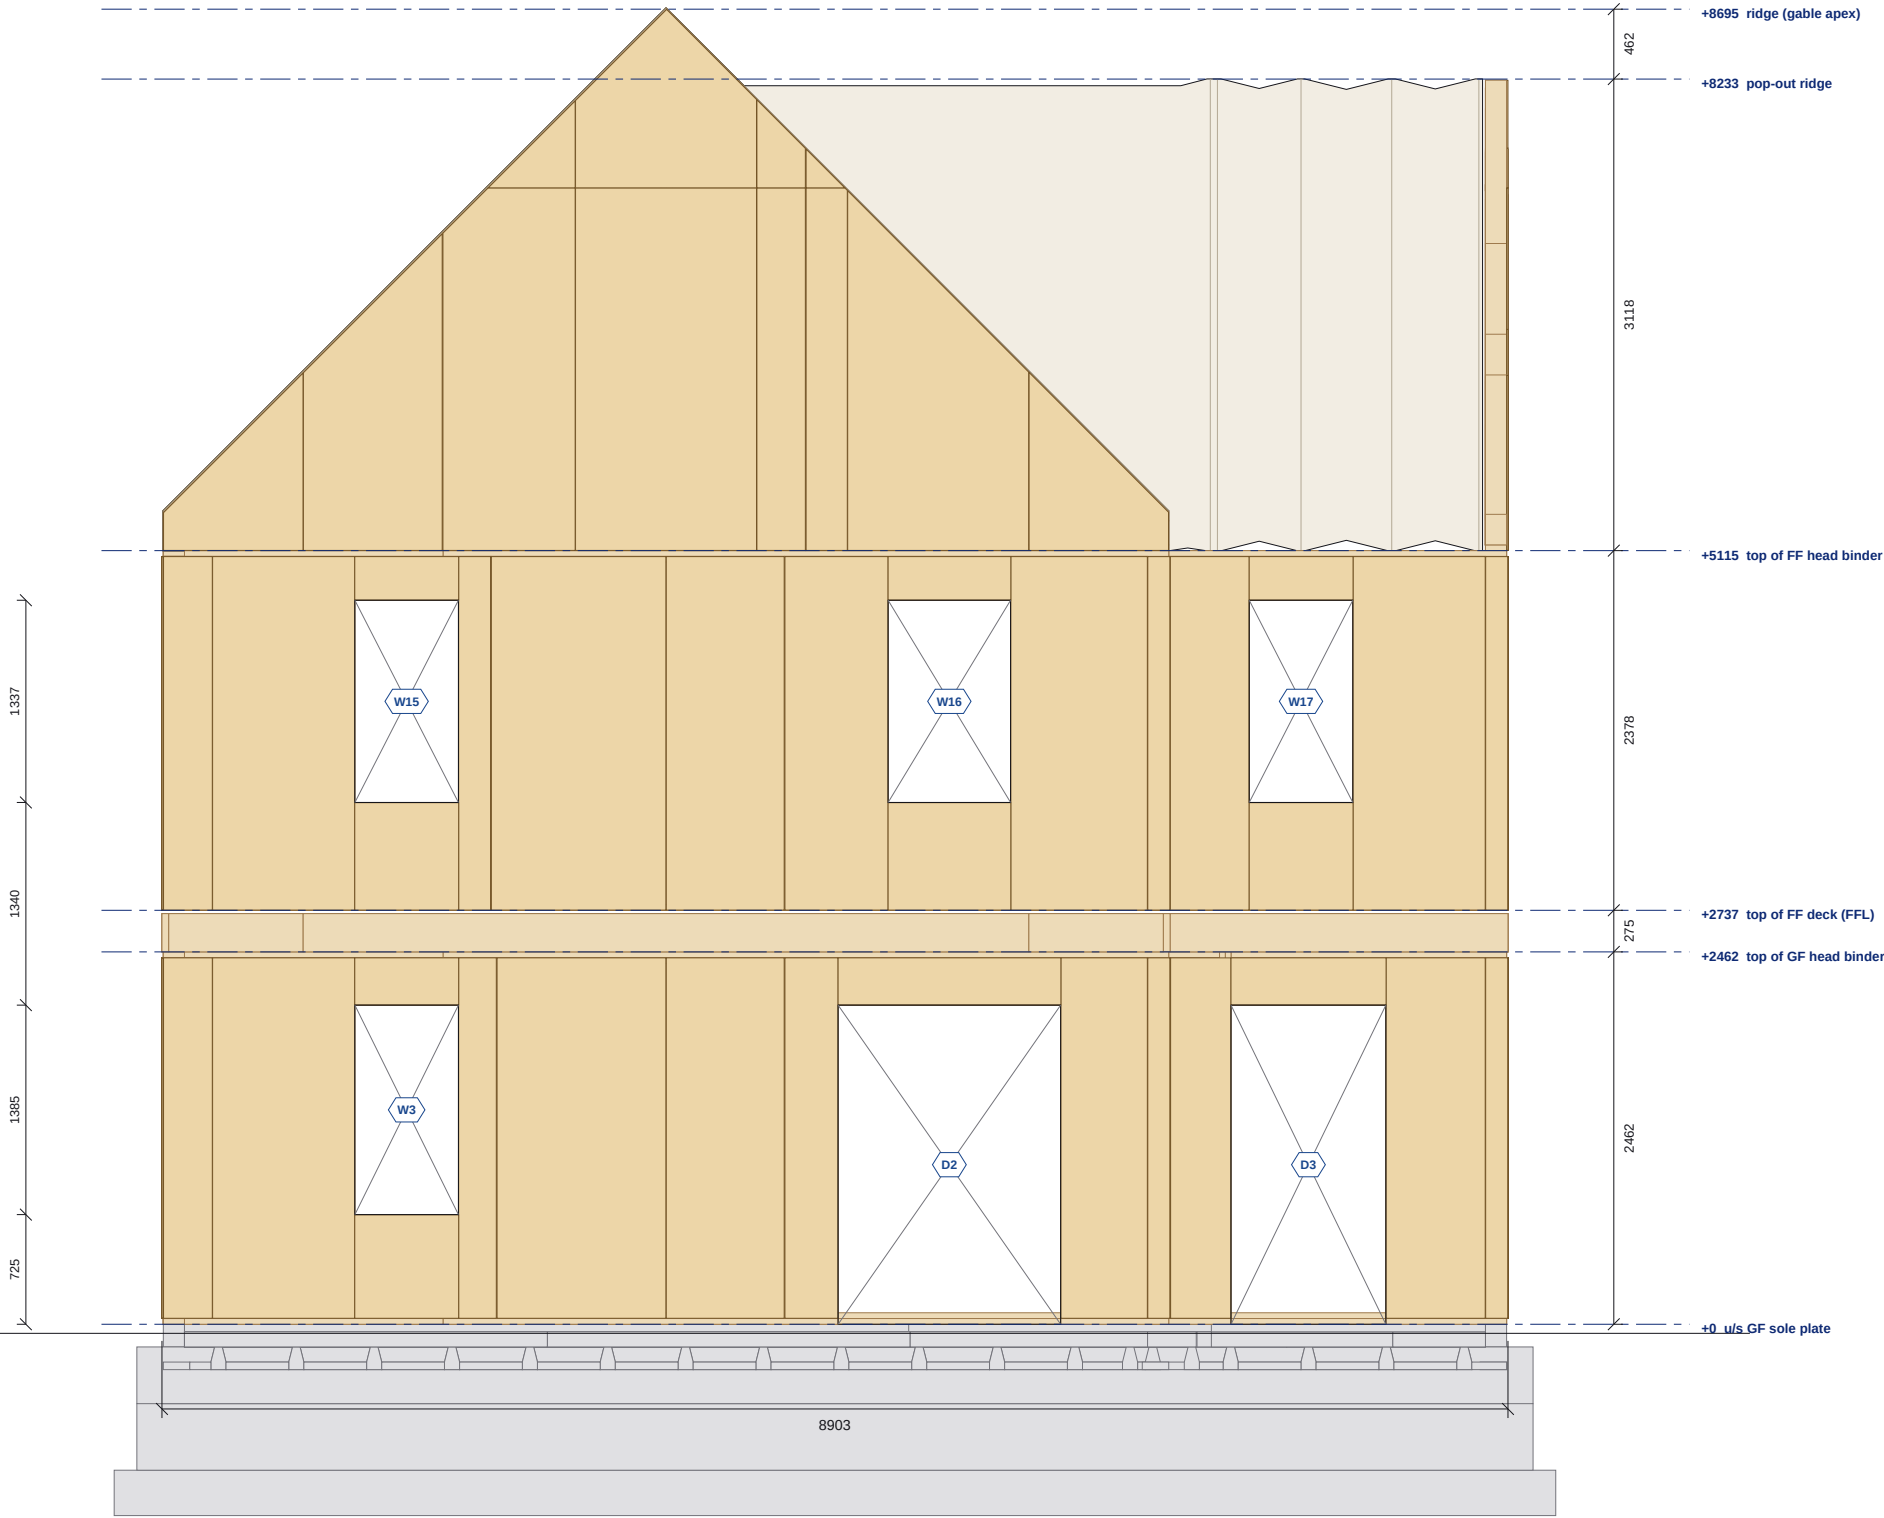

SIDE ELEVATION (EAST) SCHEDULE

LEVELS ON THIS FACE

Level	mm
u/s GF sole plate	+0
top of GF head binder	+2462
top of FF deck (FFL)	+2737
top of FF head binder	+5115
pop-out ridge	+8233
ridge (gable apex)	+8695

Above underside of the ground floor sole plate.

OPENINGS ON THIS FACE

Label	Level	Width	Height	Sill	Head
D2	GF	1472	2110	0	2110
D3	GF	1024	2110	0	2110
W3	GF	685	1385	725	2110
W15	FF	685	1337	3450	4787
W16	FF	810	1337	3450	4787
W17	FF	685	1337	3450	4787

Sill and head levels above underside of the GF sole plate.

NOTES

- Construction elevation of the timber frame: OSB/3 face of external and gable panels, sole plates, head binders and edgebinders. Cladding, roof covering and windows by others, not shown.
- Level lines shown are only those relevant to this face: storey levels, visible ridges and the sill / head levels of the openings on this face.
- Levels above the underside of the ground floor sole plate (+0). Openings are structural openings; see P3-GA-01 / P3-GA-02 / P3-GA-03.

REVISIONS

REV	DATE	DESCRIPTION
C01	13.09.26	Construction issue



TLS TIMBER FRAME

Design & Manufacture

Scan: 3D model + drawings



CLIENT	PROJECT
MP Adams	MP Adams Plot 3, Eckington

DRAWING TITLE			
SIDE ELEVATION (EAST)			
Timber frame construction elevation			

SCALE	SIZE	DATE	DRAWN
1:50	A3	13.09.26	TS

STATUS	DRAWING No.	REV
CONSTRUCTION	P3-EL-02	C01

Do not scale. All dimensions in mm. Check all dimensions on site.

REAR ELEVATION (NORTH)

Scale 1:50 @ A3 | Levels right: storey levels + visible ridges; left: sills and heads on this face



REAR ELEVATION (NORTH) SCHEDULE

LEVELS ON THIS FACE

Level	mm
u/s GF sole plate	+0
top of GF head binder	+2462
top of FF deck (FFL)	+2737
top of FF head binder	+5115
pop-out ridge (gable apex)	+8226
ridge	+8703

Above underside of the ground floor sole plate.

OPENINGS ON THIS FACE

Label	Level	Width	Height	Sill	Head
W4	GF	685	1235	875	2110
W5	GF	810	1535	575	2110
W7	GF	1120	1235	875	2110
W18	FF	810	1337	3450	4787
W19	FF	1120	1187	3600	4787

Sill and head levels above underside of the GF sole plate.

NOTES

- Construction elevation of the timber frame: OSB/3 face of external and gable panels, sole plates, head binders and edgebinders. Cladding, roof covering and windows by others, not shown.
- Level lines shown are only those relevant to this face: storey levels, visible ridges and the sill / head levels of the openings on this face.
- Levels above the underside of the ground floor sole plate (+0). Openings are structural openings; see P3-GA-01 / P3-GA-02 / P3-GA-03.

REVISIONS

REV	DATE	DESCRIPTION
C01	13.09.26	Construction issue



TLS TIMBER FRAME
Design & Manufacture
Scan: 3D model + drawings



CLIENT MP Adams	PROJECT MP Adams Plot 3, Eckington
--------------------	---------------------------------------

DRAWING TITLE REAR ELEVATION (NORTH)			
---	--	--	--

Timber frame construction elevation


SCALE 1:50	SIZE A3	DATE 13.09.26	DRAWN TS
---------------	------------	------------------	-------------

STATUS CONSTRUCTION	DRAWING No. P3-EL-03	REV C01
------------------------	-------------------------	------------

Do not scale. All dimensions in mm. Check all dimensions on site.

SIDE ELEVATION (WEST)

Scale 1:50 @ A3 | Levels right: storey levels + visible ridges; left: sills and heads on this face

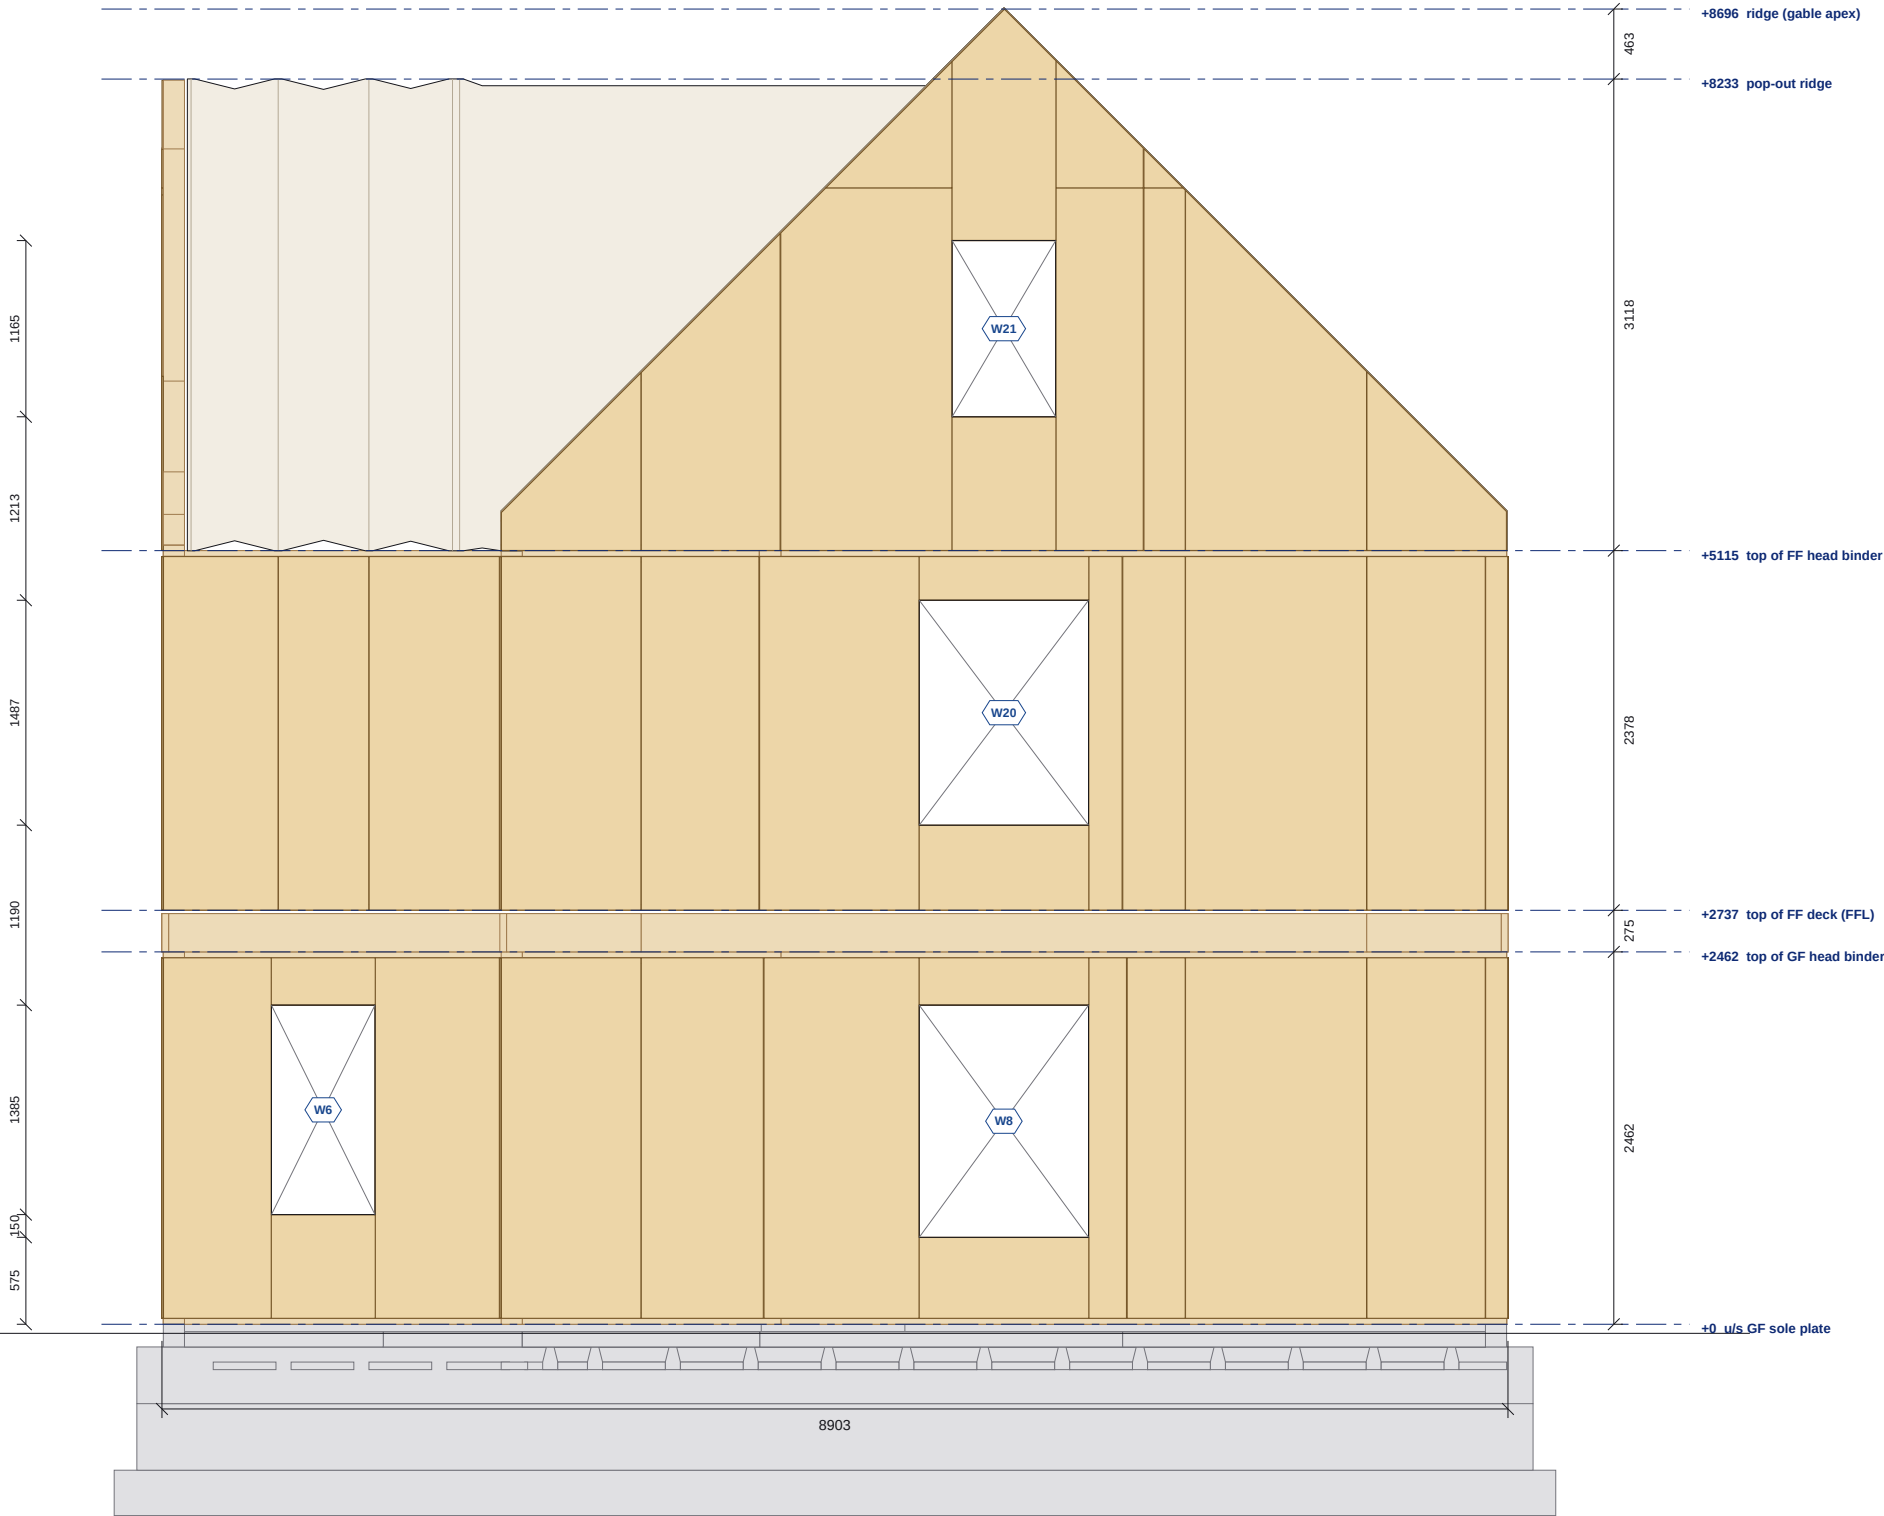

SIDE ELEVATION (WEST) SCHEDULE

LEVELS ON THIS FACE

Level	mm
u/s GF sole plate	+0
top of GF head binder	+2462
top of FF deck (FFL)	+2737
top of FF head binder	+5115
pop-out ridge	+8233
ridge (gable apex)	+8696

Above underside of the ground floor sole plate.

OPENINGS ON THIS FACE

Label	Level	Width	Height	Sill	Head
W6	GF	685	1385	725	2110
W8	GF	1120	1535	575	2110
W20	FF	1120	1487	3300	4787
W21	GB	685	1165	6000	7165

Sill and head levels above underside of the GF sole plate.

NOTES

- Construction elevation of the timber frame: OSB/3 face of external and gable panels, sole plates, head binders and edgebinders. Cladding, roof covering and windows by others, not shown.
- Level lines shown are only those relevant to this face: storey levels, visible ridges and the sill / head levels of the openings on this face.
- Levels above the underside of the ground floor sole plate (+0). Openings are structural openings; see P3-GA-01 / P3-GA-02 / P3-GA-03.

REVISIONS

REV	DATE	DESCRIPTION
C01	13.09.26	Construction issue



TLS TIMBER FRAME
Design & Manufacture
Scan: 3D model + drawings



CLIENT MP Adams	PROJECT MP Adams Plot 3, Eckington
--------------------	---------------------------------------

DRAWING TITLE
SIDE ELEVATION (WEST)

Timber frame construction elevation

SCALE 1:50	SIZE A3	DATE 13.09.26	DRAWN TS
---------------	------------	------------------	-------------

STATUS CONSTRUCTION	DRAWING No. P3-EL-04	REV C01
------------------------	-------------------------	------------
