



Nailing: OSB/Ply racking: 150mm perimeter / 300mm field nails (EC5 §9.2.4, 2:1 panel h:b)

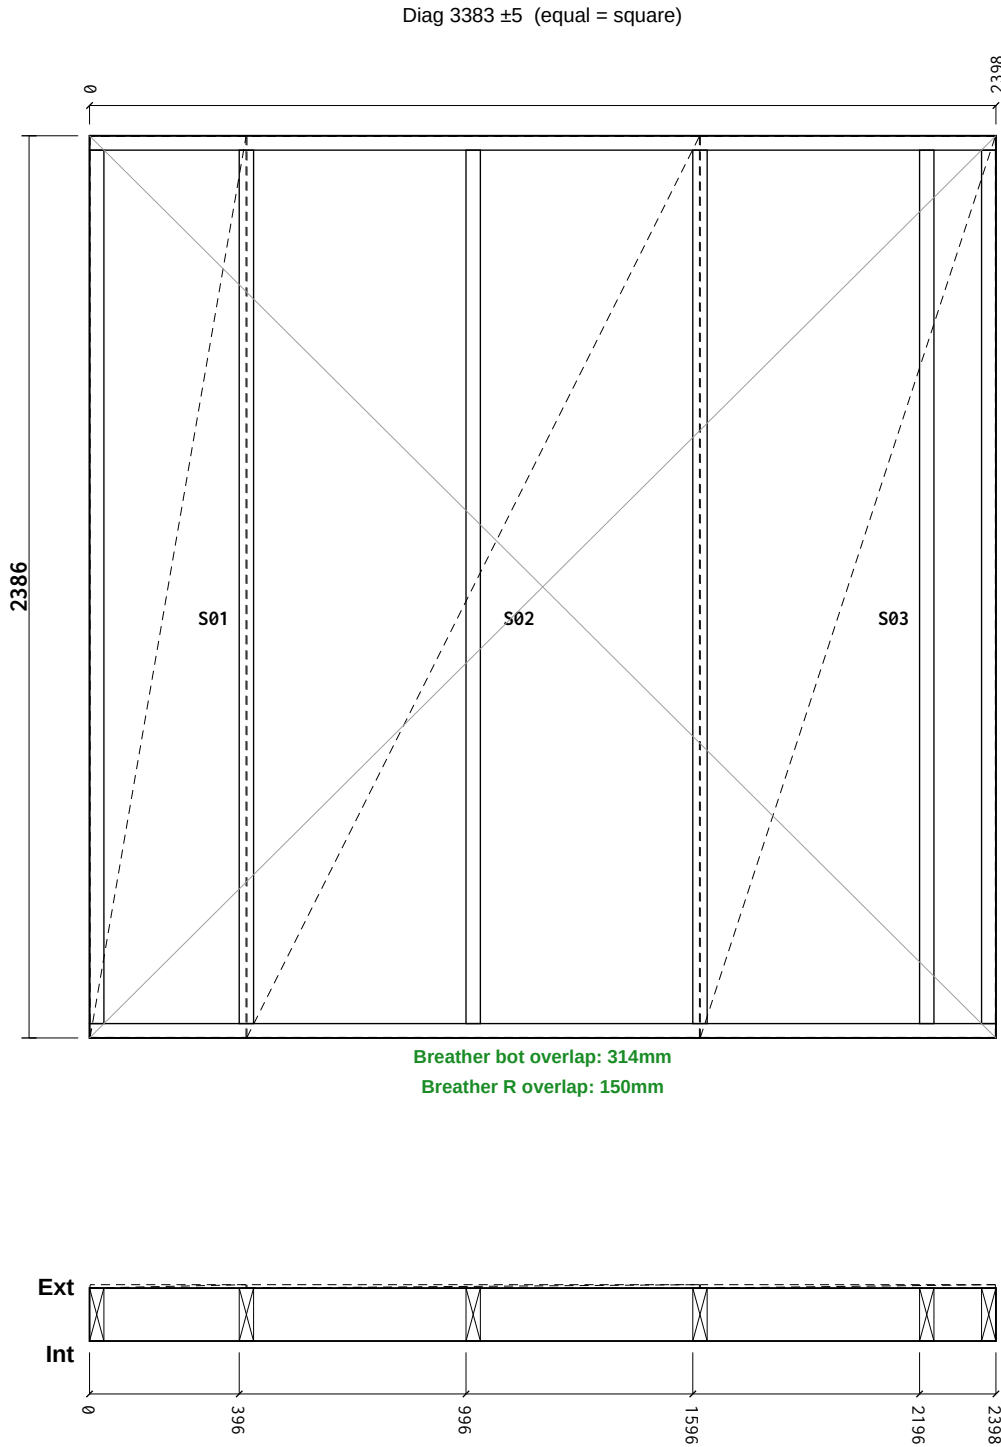

### Cut List

| Item                   | Section    | Len  | Bot° | Top° | Qty |
|------------------------|------------|------|------|------|-----|
| BR1 Bottom Rail        | 38×140 C16 | 2398 | 0    | 0    | 1   |
| TR1 Top Rail           | 38×140 C16 | 2398 | 0    | 0    | 1   |
| ES1 End Stud           | 38×140 C16 | 2310 | 0    | 0    | 1   |
| ES2 End Stud           | 38×140 C16 | 2310 | 0    | 0    | 1   |
| VS1 Vertical Stud      | 38×140 C16 | 2310 | 0    | 0    | 4   |
| Total: 8 pcs / 18.66 m |            |      |      |      |     |

### Sheathing & Insulation

| Material | W    | H    | Label |
|----------|------|------|-------|
| OSB 9mm  | 413  | 2383 | S01   |
| OSB 9mm  | 1197 | 2383 | S02   |
| OSB 9mm  | 780  | 2383 | S03   |

#### General Notes:

**Frame Nailing:**  
140mm Frames Nail Using 3no, 3.1×90mm length field galvanised twisted strip nails  
90mm Frames Nail Using 2no, 3.1×90mm length field galvanised twisted strip nails

**Sheathing Nails:**  
Components ≤ 100mm should be +/- 1mm  
Components > 100mm should be +/- 1.5mm  
Stepped check should be +/- 1.5mm  
Sloped Opening sizes are +/-2mm


**Nailing:**  
30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.

**Manufacturing Tolerances:**  
Length ±3 · Height ±2 · Diagonals ±5 · Openings 0/+5 (mm).  
Do not scale — work to figured dimensions. All dims in mm.

**Breather Membrane:**  
Laps 100mm horizontal / 150mm vertical, upper lapping lower.




**Panel Changes:**  
When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.

#### KEY PLAN



|                                |                                      |                            |      |             |              |          |  |
|--------------------------------|--------------------------------------|----------------------------|------|-------------|--------------|----------|--|
| Revisions (Rev · Date · Note): |                                      | C01 - Construction issue   |      |             |              |          |  |
| Date:                          | 2026-09-13                           | Scale:                     | 1:20 | Drawn:      | TS           | Checked: |  |
| Project Name:                  |                                      | MP Adams Plot 3, Eckington |      |             |              |          |  |
| Site:                          | Eckington                            |                            |      | Client:     | MP Adams     |          |  |
| Title:                         | Panel Fabrication — 38 x 140 C16 CLS |                            |      |             |              |          |  |
| Project Number:                | P3                                   |                            |      | Revision:   | C01          |          |  |
| Panel No:                      | GF-IL1                               |                            |      | Drawing No: | P3-MF-GF-IL1 |          |  |
| Panel L×H×T:                   | 2398×2386×149                        |                            |      | Weight:     | 73 kg        |          |  |
| Status:                        | CONSTRUCTION                         |                            |      | Sheet:      | 1 / 1        |          |  |

Nailing: OSB/Ply racking: 150mm perimeter / 300mm field nails (EC5 §9.2.4, 2:1 panel h:b)

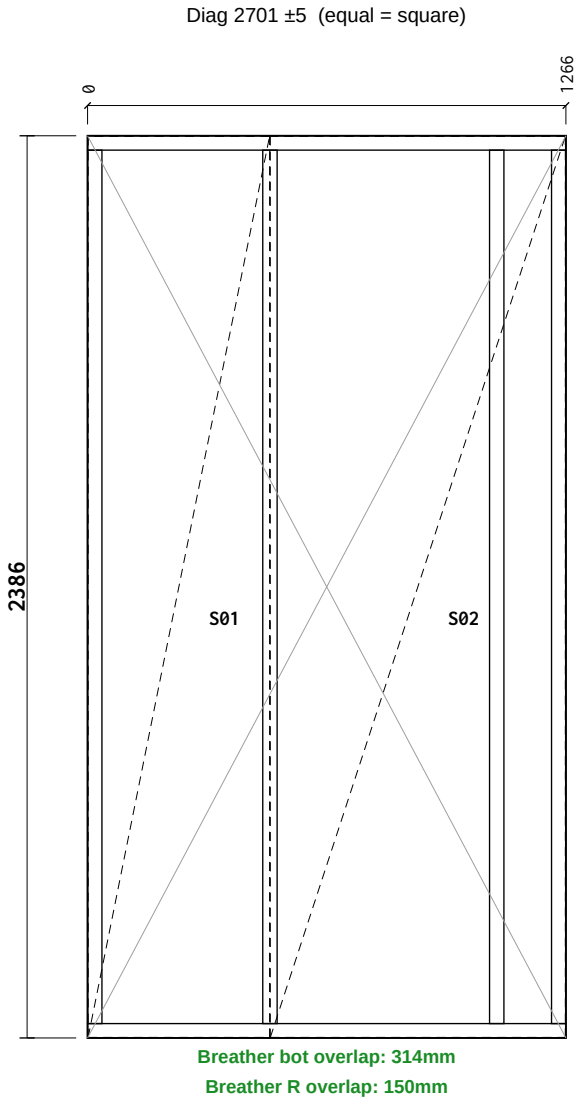

### Cut List

| Item                   | Section    | Len  | Bot° | Top°  | Qty |
|------------------------|------------|------|------|-------|-----|
| BR1 Bottom Rail        | 38×140 C16 | 1265 | 0    | 0     | 1   |
| TR1 Top Rail           | 38×140 C16 | 1265 | 0    | 0     | 1   |
| ES1 End Stud           | 38×140 C16 | 2310 | 0    | 0     | 1   |
| ES2 End Stud           | 38×140 C16 | 2310 | 0    | 0     | 1   |
| VS1 Vertical Stud      | 38×140 C16 | 2310 | 0    | 0     | 2   |
| Total: 6 pcs / 11.77 m |            |      |      |       |     |
| Sheathing & Insulation |            |      |      |       |     |
| Material               |            | W    | H    | Label |     |
| OSB 9mm                |            | 480  | 2383 | S01   |     |
| OSB 9mm                |            | 780  | 2383 | S02   |     |

#### General Notes:

**Frame Nailing:**  
140mm Frames Nail Using 3no, 3.1×90mm length field galvanised twisted strip nails  
90mm Frames Nail Using 2no, 3.1×90mm length field galvanised twisted strip nails

**Sheathing Nails:**  
Components ≤ 100mm should be +/- 1mm  
Components > 100mm should be +/- 1.5mm  
Stepped check should be +/- 1.5mm  
Sloped Opening sizes are +/-2mm


**Nailing:**  
30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.

**Manufacturing Tolerances:**  
Length ±3 · Height ±2 · Diagonals ±5 · Openings 0/+5 (mm).  
Do not scale — work to figured dimensions. All dims in mm.

**Breather Membrane:**  
Laps 100mm horizontal / 150mm vertical, upper lapping lower.

**Panel Changes:**  
When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.

#### KEY PLAN






Revisions (Rev · Date · Note):

C01 - Construction issue

|                 |            |                                      |      |             |              |          |  |
|-----------------|------------|--------------------------------------|------|-------------|--------------|----------|--|
| Date:           | 2026-09-13 | Scale:                               | 1:20 | Drawn:      | TS           | Checked: |  |
| Project Name:   |            | MP Adams Plot 3, Eckington           |      |             |              |          |  |
| Site:           | Eckington  |                                      |      | Client:     | MP Adams     |          |  |
| Title:          |            | Panel Fabrication — 38 x 140 C16 CLS |      |             |              |          |  |
| Project Number: |            | P3                                   |      | Revision:   | C01          |          |  |
| Panel No:       |            | GF-IL2                               |      | Drawing No: | P3-MF-GF-IL2 |          |  |
| Panel L×H×T:    |            | 1265×2386×149                        |      | Weight:     | 43 kg        |          |  |
| Status:         |            | CONSTRUCTION                         |      | Sheet:      | 1 / 1        |          |  |

Nailing: OSB/Ply racking: 150mm perimeter / 300mm field nails (EC5 §9.2.4, 2:1 panel h:b)

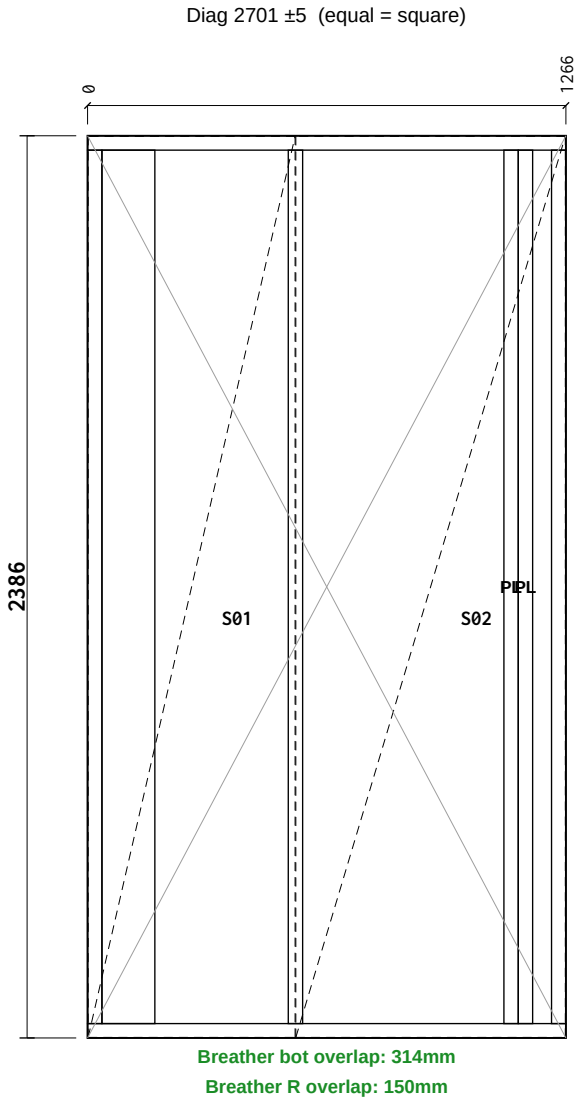

### Cut List

| Item                   | Section    | Len  | Bot° | Top° | Qty |
|------------------------|------------|------|------|------|-----|
| BR1 Bottom Rail        | 38×140 C16 | 1265 | 0    | 0    | 1   |
| TR1 Top Rail           | 38×140 C16 | 1265 | 0    | 0    | 1   |
| ES1 End Stud           | 38×140 C16 | 2310 | 0    | 0    | 1   |
| ES2 End Stud           | 38×140 C16 | 2310 | 0    | 0    | 1   |
| VS1 Vertical Stud      | 38×140 C16 | 2310 | 0    | 0    | 1   |
| JS1 Junction Stud      | 38×140 C16 | 2310 | 0    | 0    | 1   |
| Total: 6 pcs / 11.77 m |            |      |      |      |     |

### Sheathing & Insulation

| Material | W   | H    | Label |
|----------|-----|------|-------|
| OSB 9mm  | 548 | 2383 | S01   |
| OSB 9mm  | 713 | 2383 | S02   |

#### General Notes:

**Frame Nailing:**  
140mm Frames Nail Using 3no, 3.1×90mm length field galvanised twisted strip nails  
90mm Frames Nail Using 2no, 3.1×90mm length field galvanised twisted strip nails

**Sheathing Nails:**  
Components ≤ 100mm should be +/- 1mm  
Components > 100mm should be +/- 1.5mm  
Stepped check should be +/- 1.5mm  
Sloped Opening sizes are +/-2mm


**Nailing:**  
30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.

**Manufacturing Tolerances:**  
Length ±3 · Height ±2 · Diagonals ±5 · Openings 0/+5 (mm).  
Do not scale — work to figured dimensions. All dims in mm.

**Breather Membrane:**  
Laps 100mm horizontal / 150mm vertical, upper lapping lower.




**Panel Changes:**  
When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.

#### KEY PLAN



|                                |                                      |                            |      |             |              |          |  |
|--------------------------------|--------------------------------------|----------------------------|------|-------------|--------------|----------|--|
| Revisions (Rev · Date · Note): |                                      | C01 - Construction issue   |      |             |              |          |  |
| Date:                          | 2026-09-13                           | Scale:                     | 1:20 | Drawn:      | TS           | Checked: |  |
| Project Name:                  |                                      | MP Adams Plot 3, Eckington |      |             |              |          |  |
| Site:                          | Eckington                            |                            |      | Client:     | MP Adams     |          |  |
| Title:                         | Panel Fabrication — 38 x 140 C16 CLS |                            |      |             |              |          |  |
| Project Number:                | P3                                   |                            |      | Revision:   | C01          |          |  |
| Panel No:                      | GF-IL3                               |                            |      | Drawing No: | P3-MF-GF-IL3 |          |  |
| Panel L×H×T:                   | 1265×2386×149                        |                            |      | Weight:     | 43 kg        |          |  |
| Status:                        | CONSTRUCTION                         |                            |      | Sheet:      | 1 / 1        |          |  |

Nailing: OSB/Ply racking: 150mm perimeter / 300mm field nails (EC5 §9.2.4, 2:1 panel h:b)

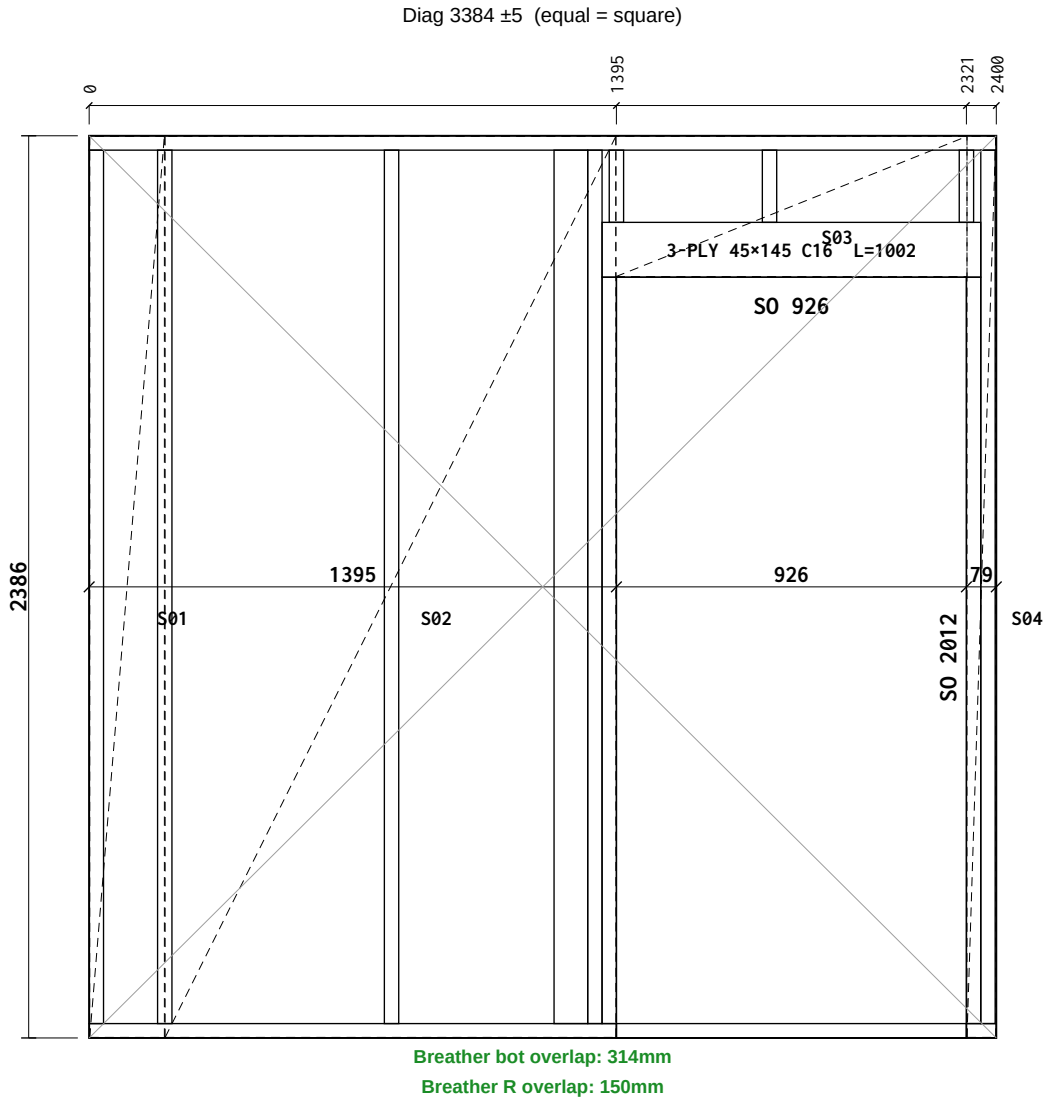

Cut List

| Item                    | Section     | Len  | Bot° | Top° | Qty |
|-------------------------|-------------|------|------|------|-----|
| BR1 Bottom Rail         | 38×140 C16  | 1395 | 0    | 0    | 1   |
| BR2 Bottom Rail         | 38×140 C16  | 926  | 0    | 0    | 1   |
| BR3 Bottom Rail         | 38×140 C16  | 79   | 0    | 0    | 1   |
| TR1 Top Rail            | 38×140 C16  | 2400 | 0    | 0    | 1   |
| ES1 End Stud            | 38×140 C16  | 2310 | 0    | 0    | 1   |
| ES2 End Stud            | 38×140 C16  | 191  | 0    | 0    | 1   |
| KS1 Vertical Stud       | 38×140 C16  | 2310 | 0    | 0    | 2   |
| CS1 Cripple Stud        | 38×140 C16  | 1974 | 0    | 0    | 2   |
| LP1 Lintel Ply          | 1002×45 C16 | 1002 | 0    | 0    | 3   |
| OS1 OSB Support         | 38×140 C16  | 191  | 0    | 0    | 2   |
| VS1 Vertical Stud       | 38×140 C16  | 2310 | 0    | 0    | 2   |
| JS1 Junction Stud       | 38×89 C16   | 2310 | 0    | 0    | 1   |
| Total: 18 pcs / 26.19 m |             |      |      |      |     |

Sheathing & Insulation

| Material | W    | H    | Label |
|----------|------|------|-------|
| OSB 9mm  | 198  | 2383 | S01   |
| OSB 9mm  | 1192 | 2383 | S02   |
| OSB 9mm  | 929  | 371  | S03   |
| OSB 9mm  | 76   | 2383 | S04   |

General Notes:

**Frame Nailing:**  
140mm Frames Nail Using 3no, 3.1×90mm length field galvanised twisted strip nails  
90mm Frames Nail Using 2no, 3.1×90mm length field galvanised twisted strip nails

**Sheathing Nails:**  
Components ≤ 100mm should be +/- 1mm  
Components > 100mm should be +/- 1.5mm  
Stepped check should be +/- 1.5mm  
Sloped Opening sizes are +/-2mm


**Nailing:**  
30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.

**Manufacturing Tolerances:**  
Length ±3 · Height ±2 · Diagonals ±5 · Openings 0/+5 (mm).  
Do not scale — work to figured dimensions. All dims in mm.

**Breather Membrane:**  
Laps 100mm horizontal / 150mm vertical, upper lapping lower.

**Panel Changes:**  
When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.

KEY PLAN



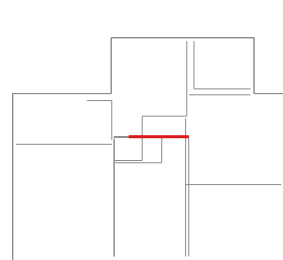


Revisions (Rev · Date · Note):

C01 - Construction issue

|                 |            |                                      |      |             |    |              |  |
|-----------------|------------|--------------------------------------|------|-------------|----|--------------|--|
| Date:           | 2026-09-13 | Scale:                               | 1:20 | Drawn:      | TS | Checked:     |  |
| Project Name:   |            | MP Adams Plot 3, Eckington           |      |             |    |              |  |
| Site:           |            | Eckington                            |      | Client:     |    | MP Adams     |  |
| Title:          |            | Panel Fabrication — 38 x 140 C16 CLS |      |             |    |              |  |
| Project Number: |            | P3                                   |      | Revision:   |    | C01          |  |
| Panel No:       |            | GF-IL4                               |      | Drawing No: |    | P3-MF-GF-IL4 |  |
| Panel L×H×T:    |            | 2400×2386×149                        |      | Weight:     |    | 79 kg        |  |
| Status:         |            | CONSTRUCTION                         |      | Sheet:      |    | 1 / 1        |  |

Nailing: OSB/Ply racking: 150mm perimeter / 300mm field nails (EC5 §9.2.4, 2:1 panel h:b)

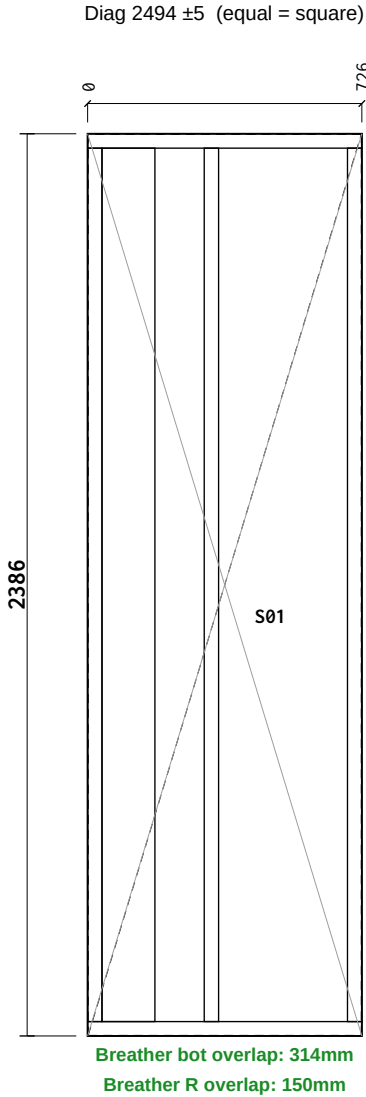

### Cut List

| Item                   | Section    | Len  | Bot° | Top° | Qty |
|------------------------|------------|------|------|------|-----|
| BR1 Bottom Rail        | 38×140 C16 | 725  | 0    | 0    | 1   |
| TR1 Top Rail           | 38×140 C16 | 725  | 0    | 0    | 1   |
| ES1 End Stud           | 38×140 C16 | 2310 | 0    | 0    | 1   |
| ES2 End Stud           | 38×140 C16 | 2310 | 0    | 0    | 1   |
| VS1 Vertical Stud      | 38×140 C16 | 2310 | 0    | 0    | 1   |
| JS1 Junction Stud      | 38×140 C16 | 2310 | 0    | 0    | 1   |
| Total: 6 pcs / 10.69 m |            |      |      |      |     |

### Sheathing & Insulation

| Material | W   | H    | Label |
|----------|-----|------|-------|
| OSB 9mm  | 722 | 2383 | S01   |

#### General Notes:

**Frame Nailing:**  
140mm Frames Nail Using 3no, 3.1×90mm length field galvanised twisted strip nails  
90mm Frames Nail Using 2no, 3.1×90mm length field galvanised twisted strip nails

**Sheathing Nails:**  
Components ≤ 100mm should be +/- 1mm  
Components > 100mm should be +/- 1.5mm  
Stepped check should be +/- 1.5mm  
Sloped Opening sizes are +/-2mm


**Nailing:**  
30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.

**Manufacturing Tolerances:**  
Length ±3 · Height ±2 · Diagonals ±5 · Openings 0/+5 (mm).  
Do not scale — work to figured dimensions. All dims in mm.

**Breather Membrane:**  
Laps 100mm horizontal / 150mm vertical, upper lapping lower.


**Panel Changes:**  
When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.

#### KEY PLAN



|                                |                                      |                            |      |                          |              |          |  |
|--------------------------------|--------------------------------------|----------------------------|------|--------------------------|--------------|----------|--|
| Revisions (Rev · Date · Note): |                                      |                            |      | C01 - Construction issue |              |          |  |
| Date:                          | 2026-09-13                           | Scale:                     | 1:20 | Drawn:                   | TS           | Checked: |  |
| Project Name:                  |                                      | MP Adams Plot 3, Eckington |      |                          |              |          |  |
| Site:                          | Eckington                            |                            |      | Client:                  | MP Adams     |          |  |
| Title:                         | Panel Fabrication — 38 x 140 C16 CLS |                            |      |                          |              |          |  |
| Project Number:                | P3                                   |                            |      | Revision:                | C01          |          |  |
| Panel No:                      | GF-IL5                               |                            |      | Drawing No:              | P3-MF-GF-IL5 |          |  |
| Panel L×H×T:                   | 725×2386×149                         |                            |      | Weight:                  | 33 kg        |          |  |
| Status:                        | CONSTRUCTION                         |                            |      | Sheet:                   | 1 / 1        |          |  |




Technical drawing of a rectangular panel with dimensions and internal structure. The overall width is 3384 mm and the height is 2386 mm. The panel is divided into three vertical sections labeled S01, S02, and S03. The width of S01 is 1195 mm, S02 is 1095 mm, and S03 is 1094 mm. The total width is 3384 mm. The height is 2386 mm. The drawing shows a grid of lines representing the internal structure, including a central vertical line and two diagonal lines. The text 'Diag 3384 ±5 (equal = square)' is at the top. The text 'Breather bot overlap: 314mm' and 'Breather R overlap: 150mm' is at the bottom.



| Item                              | Section    | Len      | Bot°          | Top° Qty   |
|-----------------------------------|------------|----------|---------------|------------|
| BR1 Bottom Rail                   | 38×140 C16 | 2400     | 0             | 0 1        |
| TR1 Top Rail                      | 38×140 C16 | 2400     | 0             | 0 0        |
| ES1 End Stud                      | 38×140 C16 | 2310     | 0             | 0 1        |
| ES2 End Stud                      | 38×140 C16 | 2310     | 0             | 0 1        |
| VS1 Vertical Stud                 | 38×140 C16 | 2310     | 0             | 0 4        |
| JS1 Junction Stud                 | 38×89 C16  | 2310     | 0             | 0 1        |
| <b>Total: 9 pcs / 20.97 m</b>     |            |          |               |            |
| <b>Sheathing &amp; Insulation</b> |            |          |               |            |
| <b>Material</b>                   |            | <b>W</b> | <b>HLabel</b> |            |
| OSB 9mm                           |            | 787      | 2383          | <b>S01</b> |
| OSB 9mm                           |            | 1197     | 2383          | <b>S02</b> |
| OSB 9mm                           |            | 408      | 2383          | <b>S03</b> |

|                                |  |             |  |                                      |  |          |  |
|--------------------------------|--|-------------|--|--------------------------------------|--|----------|--|
| Revisions (Rev - Date - Note): |  |             |  | C01 - Construction issue             |  |          |  |
| Date: 2026-09-13               |  | Scale: 1:20 |  | Drawn: TS                            |  | Checked: |  |
| Project Name:                  |  |             |  | MP Adams Plot 3, Eckington           |  |          |  |
| Site: Eckington                |  |             |  | Client: MP Adams                     |  |          |  |
| Title:                         |  |             |  | Panel Fabrication — 38 x 140 C16 CLS |  |          |  |
| Project Number: P3             |  |             |  | Revision: C01                        |  |          |  |
| Panel No: GF-IL6               |  |             |  | Drawing No: P3-MF-GF-IL6             |  |          |  |
| Panel L×H×T: 2400×2386×149     |  |             |  | Weight: 76 kg                        |  |          |  |
| Status: CONSTRUCTION           |  |             |  | Sheet: 1 / 1                         |  |          |  |

Nailing: OSB/Ply racking: 150mm perimeter / 300mm field nails (EC5 §9.2.4, 2:1 panel h:b)

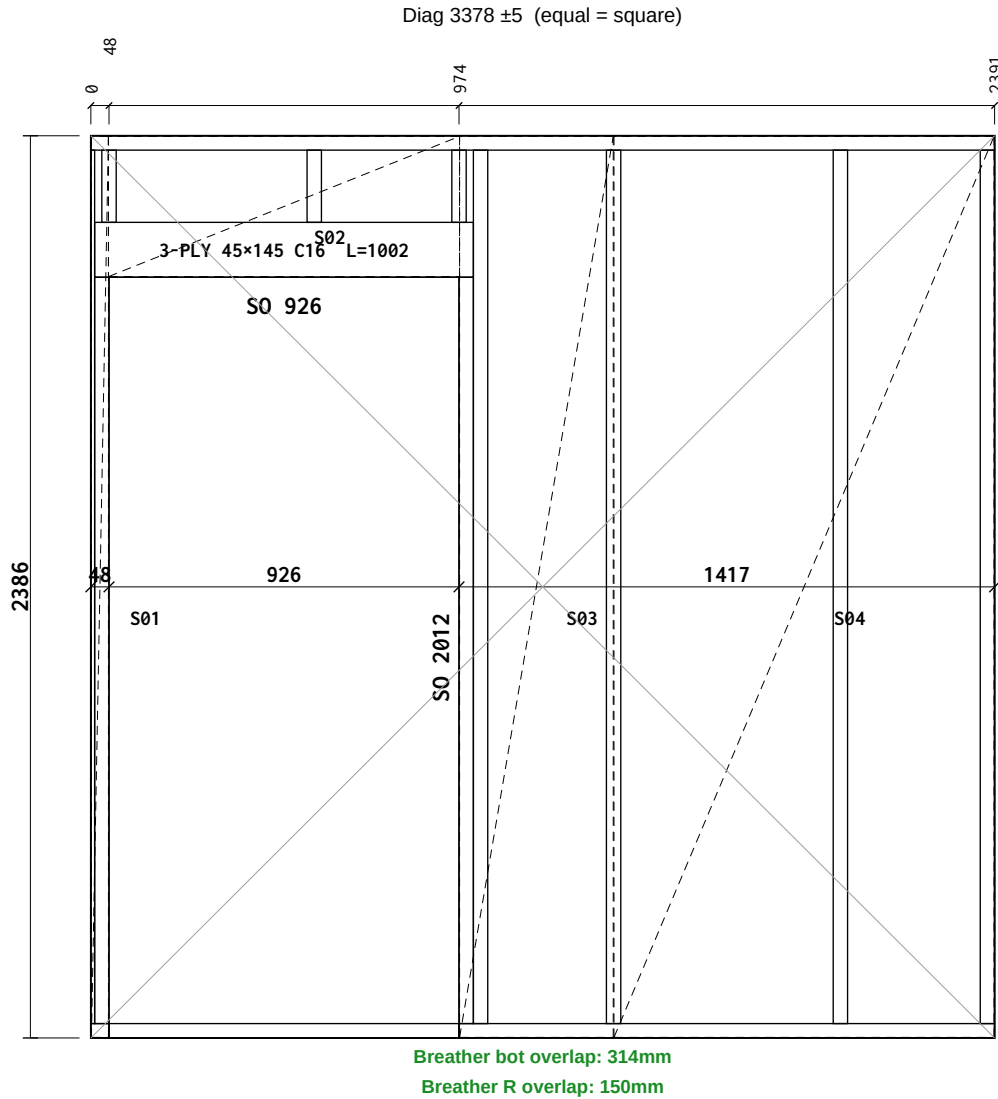

## Cut List

| Item              | Section     | Len  | Bot° | Top° | Qty |
|-------------------|-------------|------|------|------|-----|
| BR1 Bottom Rail   | 38×140 C16  | 1417 | 0    | 0    | 1   |
| BR2 Bottom Rail   | 38×140 C16  | 926  | 0    | 0    | 1   |
| BR3 Bottom Rail   | 38×140 C16  | 48   | 0    | 0    | 1   |
| TR1 Top Rail      | 38×140 C16  | 2391 | 0    | 0    | 1   |
| ES1 End Stud      | 38×140 C16  | 191  | 0    | 0    | 1   |
| ES2 End Stud      | 38×140 C16  | 2310 | 0    | 0    | 1   |
| KS1 Vertical Stud | 38×140 C16  | 2310 | 0    | 0    | 1   |
| KS2 Vertical Stud | 10×140 C16  | 2310 | 0    | 0    | 1   |
| CS1 Cripple Stud  | 38×140 C16  | 1974 | 0    | 0    | 2   |
| LP1 Lintel Ply    | 1002×45 C16 | 1002 | 0    | 0    | 3   |
| OS1 OSB Support   | 38×140 C16  | 191  | 0    | 0    | 2   |
| VS1 Vertical Stud | 38×140 C16  | 2310 | 0    | 0    | 2   |

Total: 17 pcs / 23.86 m

## Sheathing & Insulation

| Material | W    | H    | Label |
|----------|------|------|-------|
| OSB 9mm  | 45   | 2383 | S01   |
| OSB 9mm  | 929  | 371  | S02   |
| OSB 9mm  | 406  | 2383 | S03   |
| OSB 9mm  | 1006 | 2383 | S04   |

### General Notes:

**Frame Nailing:**  
140mm Frames Nail Using 3no, 3.1×90mm length field galvanised twisted strip nails  
90mm Frames Nail Using 2no, 3.1×90mm length field galvanised twisted strip nails

**Sheathing Nails:**  
Components ≤ 100mm should be +/- 1mm  
Components > 100mm should be +/- 1.5mm  
Stepped check should be +/- 1.5mm  
Sloped Opening sizes are +/-2mm


**Nailing:**  
30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.

**Manufacturing Tolerances:**  
Length ±3 · Height ±2 · Diagonals ±5 · Openings 0/+5 (mm).  
Do not scale — work to figured dimensions. All dims in mm.

**Breather Membrane:**  
Laps 100mm horizontal / 150mm vertical, upper lapping lower.

**Panel Changes:**  
When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.

### KEY PLAN



Revisions (Rev · Date · Note):

### C01 - Construction issue

|                 |                                      |        |      |             |              |          |  |
|-----------------|--------------------------------------|--------|------|-------------|--------------|----------|--|
| Date:           | 2026-09-13                           | Scale: | 1:20 | Drawn:      | TS           | Checked: |  |
| Project Name:   | MP Adams Plot 3, Eckington           |        |      |             |              |          |  |
| Site:           | Eckington                            |        |      | Client:     | MP Adams     |          |  |
| Title:          | Panel Fabrication — 38 x 140 C16 CLS |        |      |             |              |          |  |
| Project Number: | P3                                   |        |      | Revision:   | C01          |          |  |
| Panel No:       | GF-IL7                               |        |      | Drawing No: | P3-MF-GF-IL7 |          |  |
| Panel L×H×T:    | 2391×2386×149                        |        |      | Weight:     | 72 kg        |          |  |
| Status:         | CONSTRUCTION                         |        |      | Sheet:      | 1 / 1        |          |  |
