

Technical drawing of a roof plan and section.

Roof Plan:

- Overall dimensions: 2400mm (width) x 2659mm (depth).
- Slope: 45°.
- Structural supports: S01, S02, S03, S04, S05, S06.
- Roof panels: P01, P02, P03, P04, P05, P06.
- Dimensions: 256, 856, 1456, 2056, 667.
- Labels: Breather bot overlap: 150mm, Breather R overlap: 150mm.

Section View:

- Labels: Ext, Int.
- Dimensions: 0, 256, 856, 1456, 2056, 2400.

Item	Section	Len	Bot°	Top°	Qty
BR1 Bottom Rail	38×140 C16	2400	0	0	1
TR1 Top Rail	38×140 C16	2400	0	0	1
TR2 Top Rail	38×140 C16	0	0	0	1
ES1 End Stud	38×140 C16	2568	0	45.0	1
ES2 End Stud	38×140 C16	205	0	45.0	1
VS1 Vertical Stud	38×140 C16	2311	0	45.0	1
VS2 Vertical Stud	38×140 C16	1711	0	45.0	1
VS3 Vertical Stud	38×140 C16	1111	0	45.0	1
VS4 Vertical Stud	38×140 C16	511	0	45.0	1
NG1 Noggin	38×140 C16	186	0	0	

Total: 10 pcs / 13.40 m			
Sheathing & Insulation			
Material	W	H	Label
OSB 9mm	258	258	S01
OSB 9mm	273	2397	S02
OSB 9mm	1197	2380	S03
OSB 9mm	922	1180	S04
PIR 120mm	148	148	P01
PIR 120mm	217	2342	P02
PIR 120mm	561	2272	P03
PIR 120mm	561	1672	P04
PIR 120mm	561	1072	P05
PIR 120mm	267	472	P06

Frame Nailing:
140mm Frames Nail Using 3no, 3.1×90mm length field galvanised twisted strip nails
90mm Frames Nail Using 2no, 3.1×90mm length field galvanised twisted strip nails

Components $\leq 100\text{mm}$ should be $\pm 1\text{mm}$
 Components $> 100\text{mm}$ should be $\pm 1.5\text{mm}$
 Stepped check should be $\pm 1.5\text{mm}$
 Sloped Opening sizes are $\pm 2\text{mm}$

30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.

Length ± 3 · Height ± 2 · Diagonals ± 5 · Openings 0/+5 (mm).
Do not scale — work to figured dimensions. All dims in mm.


Laps 100mm horizontal / 150mm vertical, upper lapping lower.

When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.

C01 - Construction issue


Date:	2026-09-13	Scale:	1:20	Drawn:	TS	Checked:	
Project Name:		MP Adams Plot 3, Eckington					
Site:	Eckington			Client:	MP Adams		
Title:	Panel Fabrication — 38 x 140 C16 CLS						
Project Number:	P3			Revision:	C01		
Panel No:	GB-EX1			Drawing No:	P3-MF-GB-EX1		
Panel LxHxT:	2400x2659x149			Weight:	411 kg		
Status:	CONSTRUCTION			Sheet:	1 / 1		

Nailing: OSB/Ply racking: 150mm perimeter / 300mm field nails (EC5 §9.2.4, 2:1 panel h:b)

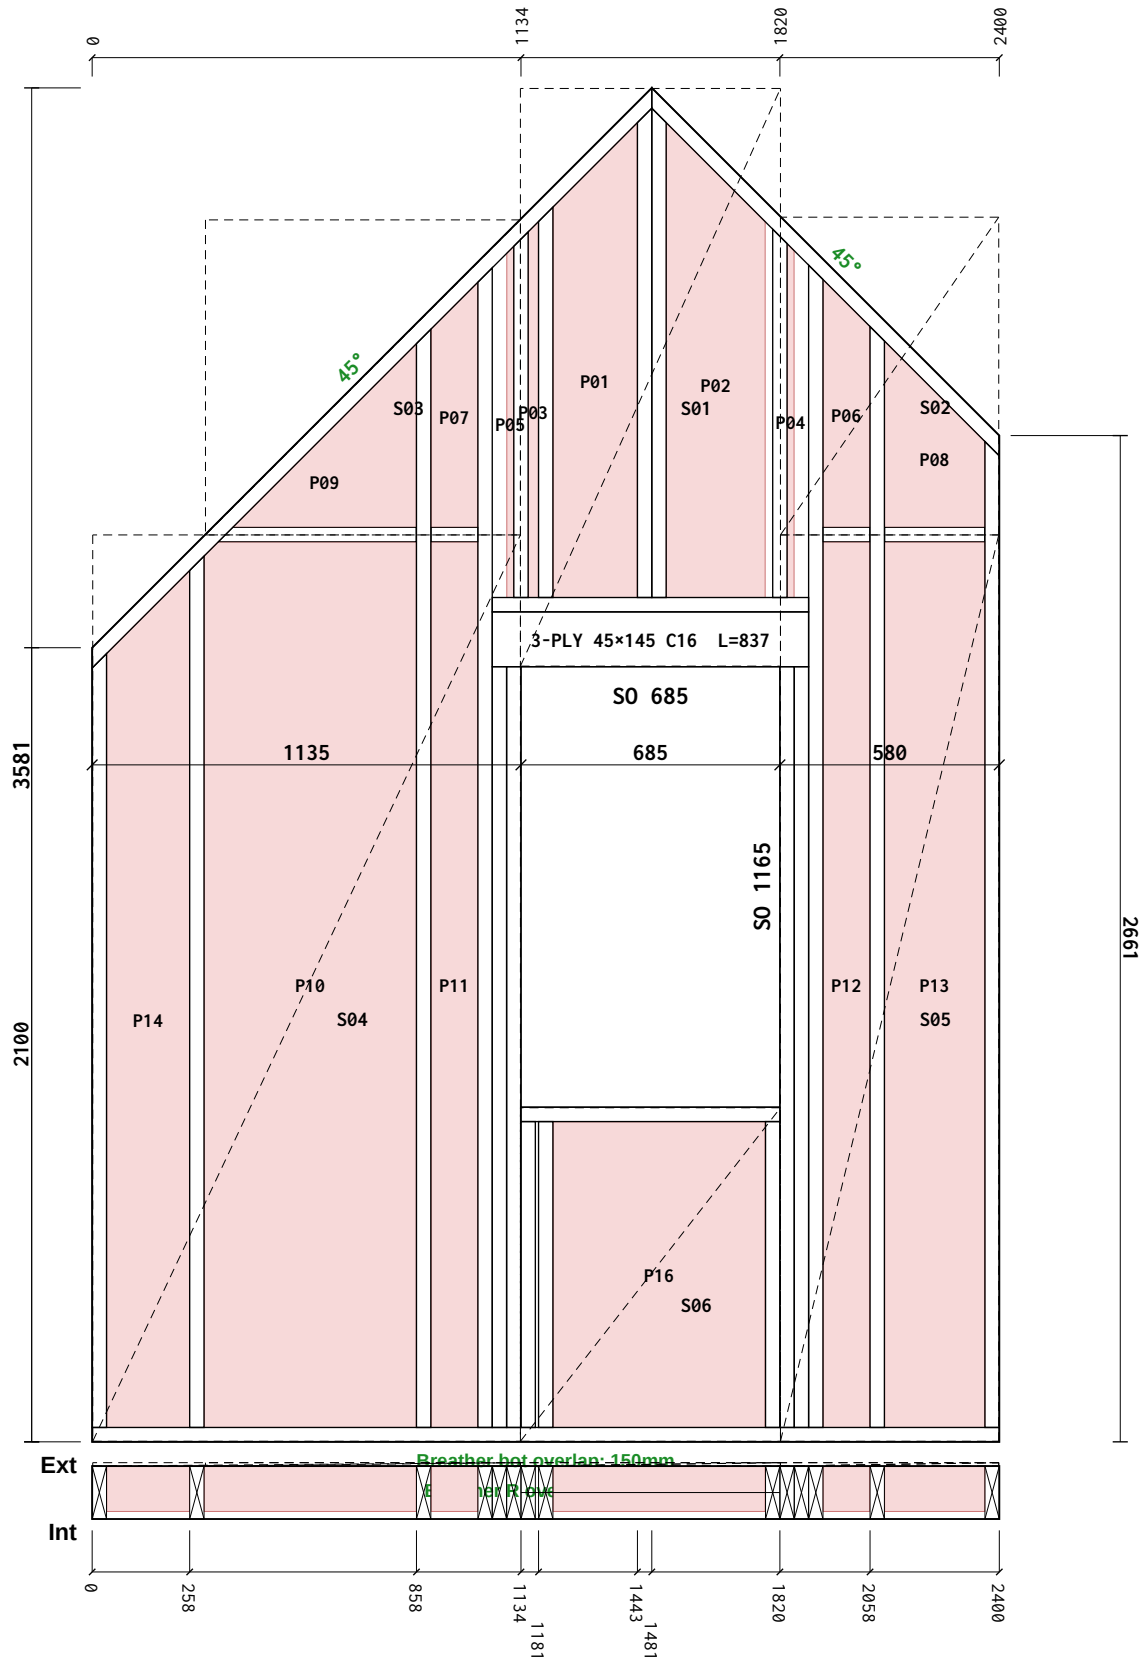

Section A-A

Ext Int



Cut List

Item	Section	Len	Bot°	Top°	Qty
BR1 Bottom Rail	38x140 C16	2400	0	0	1
TR1 Top Rail	38x140 C16	1481	0	0	1
TR2 Top Rail	38x140 C16	919	0	0	1
TR3 Top Rail	38x140 C16	837	0	0	1
ES1 End Stud	38x140 C16	2046	0	-45.0	1
ES2 End Stud	38x140 C16	2608	0	45.0	1
KS1 Vertical Stud	38x140 C16	3074	0	45.0	1
KS2 Vertical Stud	38x140 C16	3067	0	-45.0	1
CS1 Cripple Stud	38x140 C16	2012	0	0	4
SP1 Sill Plate	38x140 C16	685	0	0	1
LP1 Lintel Ply	837x45 C16	837	0	0	3
SS1 Sill Support	38x140 C16	809	0	0	2
OS1 OSB Support	38x140 C16	974	0	45.0	1
OS2 OSB Support	38x140 C16	967	0	-45.0	1
VS1 Vertical Stud	38x140 C16	2912	0	45.0	1
VS2 Vertical Stud	38x140 C16	2904	0	-45.0	1
VS3 Vertical Stud	38x140 C16	2304	0	-45.0	1
VS4 Vertical Stud	38x140 C16	1294	0	45.0	1
VS5 Vertical Stud	38x140 C16	1294	0	-45.0	1
VS6 Vertical Stud	38x140 C16	1032	0	-45.0	1
VS7 Vertical Stud	38x140 C16	809	0	0	1
NG1 Noggin	38x140 C16	523	0	0	1
NG2 Noggin	38x140 C16	264	0	0	1
NG3 Noggin	38x140 C16	124	0	0	1
NG4 Noggin	38x140 C16	123	0	0	1

Total: 31 pcs / 44.82 m

Sheathing & Insulation

Material	W	H	Label
OSB 9mm	688	1528	S01
OSB 9mm	578	840	S02
OSB 9mm	833	833	S03
OSB 9mm	1131	2397	S04
OSB 9mm	578	2397	S05
OSB 9mm	688	882	S06
PIR 120mm	223	1255	P01
PIR 120mm	261	1255	P02
PIR 120mm	27	993	P03
PIR 120mm	18	935	P04
PIR 120mm	18	928	P05
PIR 120mm	123	655	P06
PIR 120mm	123	647	P07
PIR 120mm	265	492	P08
PIR 120mm	485	485	P09
PIR 120mm	561	2342	P10
PIR 120mm	123	2342	P11
PIR 120mm	123	2342	P12
PIR 120mm	265	2342	P13
PIR 120mm	219	2265	P14
PIR 120mm	8	808	P15
PIR 120mm	561	808	P16

General Notes:

Frame Nailing:
140mm Frames Nail Using 3no, 3.1x90mm length field galvanised twisted strip nails
90mm Frames Nail Using 2no, 3.1x90mm length field galvanised twisted strip nails

Sheathing Nails:
Components ≤ 100mm should be +/- 1mm
Components > 100mm should be +/- 1.5mm
Stepped check should be +/- 1.5mm
Sloped Opening sizes are +/-2mm


Nailing:
30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.

Manufacturing Tolerances:
Length ±3 · Height ±2 · Diagonals ±5 · Openings 0/+5 (mm).
Do not scale — work to figured dimensions. All dims in mm.

Breather Membrane:
Laps 100mm horizontal / 150mm vertical, upper lapping lower.

Panel Changes:
When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.

KEY PLAN

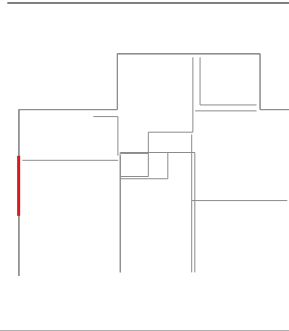


Revisions (Rev · Date · Note):

C01 - Construction issue


Date:	2026-09-13	Scale:	1:20	Drawn:	TS	Checked:	
Project Name:	MP Adams Plot 3, Eckington						
Site:	Eckington			Client:	MP Adams		
Title:	Panel Fabrication — 38 x 140 C16 CLS						
Project Number:	P3			Revision:	C01		
Panel No:	GB-EX2			Drawing No:	P3-MF-GB-EX2		
Panel LxHxT:	2400x3581x149			Weight:	340 kg		
Status:	CONSTRUCTION			Sheet:	1 / 1		

Nailing: OSB/Ply racking: 150mm perimeter / 300mm field nails (EC5 §9.2.4, 2:1 panel h:b)

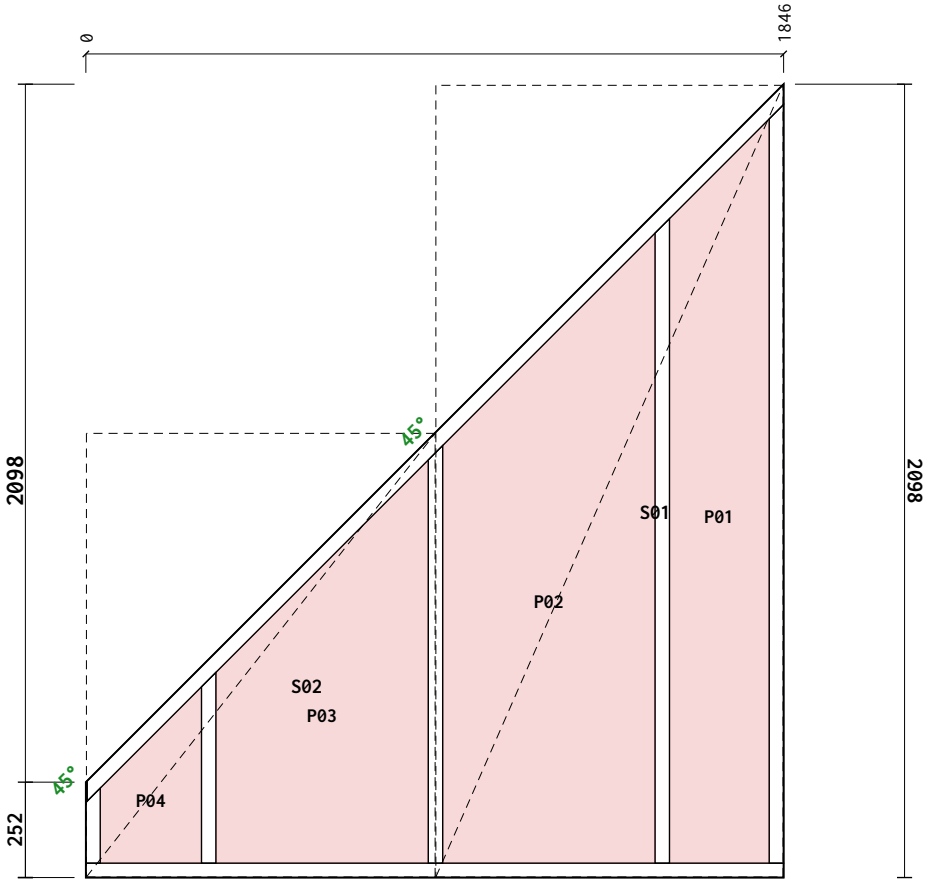

Breather bot overlap: 602mm

Breather R overlap: 150mm



Section A-A

Ext Int

2098

0

Cut List

Item	Section	Len	Bot°	Top°	Qty
BR1 Bottom Rail	38×140 C16	1846	0	0	1
TR1 Top Rail	38×140 C16	1843	0	0	1
TR2 Top Rail	38×140 C16	3	0	0	1
ES1 End Stud	38×140 C16	199	0	-45.0	1
ES2 End Stud	38×140 C16	2006	0	-45.0	1
VS1 Vertical Stud	38×140 C16	1704	0	-45.0	1
VS2 Vertical Stud	38×140 C16	1105	0	-45.0	1
VS3 Vertical Stud	38×140 C16	505	0	-45.0	1
Total: 8 pcs / 9.21 m					

Sheathing & Insulation

Material	W	H	Label
OSB 9mm	918	2094	S01
OSB 9mm	923	1173	S02
PIR 120mm	263	1967	P01
PIR 120mm	561	1665	P02
PIR 120mm	561	1066	P03
PIR 120mm	267	466	P04

General Notes:

Frame Nailing:
140mm Frames Nail Using 3no, 3.1×90mm length field galvanised twisted strip nails
90mm Frames Nail Using 2no, 3.1×90mm length field galvanised twisted strip nails

Sheathing Nails:
Components ≤ 100mm should be +/- 1mm
Components > 100mm should be +/- 1.5mm
Stepped check should be +/- 1.5mm
Sloped Opening sizes are +/-2mm


Nailing:
30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.

Manufacturing Tolerances:
Length ±3 · Height ±2 · Diagonals ±5 · Openings 0/+5 (mm).
Do not scale — work to figured dimensions. All dims in mm.

Breather Membrane:
Laps 100mm horizontal / 150mm vertical, upper lapping lower.

Panel Changes:
When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.

KEY PLAN



Revisions (Rev · Date · Note):

C01 - Construction issue

Date:	2026-09-13	Scale:	1:20	Drawn:	TS	Checked:	
-------	------------	--------	------	--------	----	----------	--

Project Name:	MP Adams Plot 3, Eckington					
---------------	----------------------------	--	--	--	--	--

Site:	Eckington	Client:	MP Adams			
-------	-----------	---------	----------	--	--	--

Title:	Panel Fabrication — 38 x 140 C16 CLS					
--------	--------------------------------------	--	--	--	--	--



Project Number:	P3	Revision:	C01			
-----------------	----	-----------	-----	--	--	--

Panel No:	GB-EX3	Drawing No:	P3-MF-GB-EX3			
-----------	--------	-------------	--------------	--	--	--

Panel L×H×T:	1846×2098×149	Weight:	248 kg			
--------------	---------------	---------	--------	--	--	--

Status:	CONSTRUCTION	Sheet:	1 / 1			
---------	--------------	--------	-------	--	--	--

Nailing: OSB/Ply racking: 150mm perimeter / 300mm field nails (EC5 §9.2.4, 2:1 panel h:b)

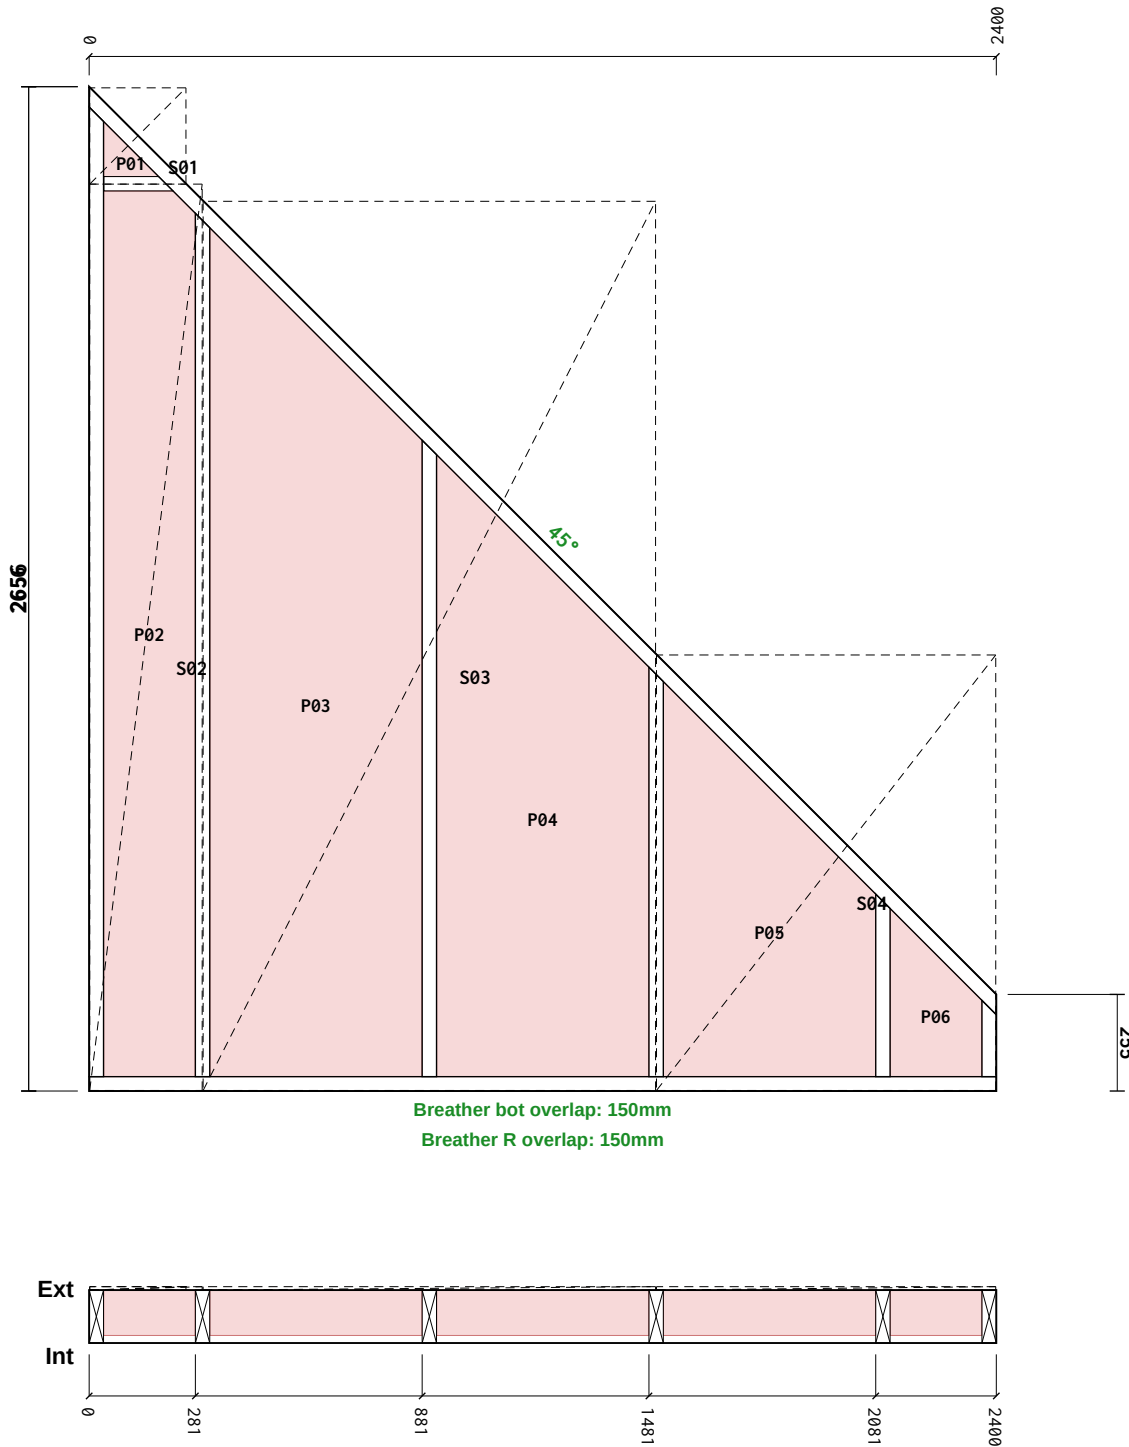

Cut List

Item	Section	Len	Bot°	Top°	Qty
BR1 Bottom Rail	38×140 C16	2400	0	0	1
TR1 Top Rail	38×140 C16	2400	0	0	1
ES1 End Stud	38×140 C16	2564	0	45.0	1
ES2 End Stud	38×140 C16	202	0	45.0	1
VS1 Vertical Stud	38×140 C16	2283	0	45.0	1
VS2 Vertical Stud	38×140 C16	1683	0	45.0	1
VS3 Vertical Stud	38×140 C16	1083	0	45.0	1
VS4 Vertical Stud	38×140 C16	483	0	45.0	1
NG1 Noggin	38×140 C16	183	0	0	1
Total: 9 pcs / 13.28 m					

Sheathing & Insulation

Material	W	H	Label
OSB 9mm	255	255	S01
OSB 9mm	297	2397	S02
OSB 9mm	1197	2352	S03
OSB 9mm	898	1152	S04
PIR 120mm	145	145	P01
PIR 120mm	242	2342	P02
PIR 120mm	561	2244	P03
PIR 120mm	561	1644	P04
PIR 120mm	561	1044	P05
PIR 120mm	242	444	P06

General Notes:

Frame Nailing:
140mm Frames Nail Using 3no, 3.1×90mm length field galvanised twisted strip nails
90mm Frames Nail Using 2no, 3.1×90mm length field galvanised twisted strip nails

Sheathing Nails:
Components ≤ 100mm should be +/- 1mm
Components > 100mm should be +/- 1.5mm
Stepped check should be +/- 1.5mm
Sloped Opening sizes are +/-2mm


Nailing:
30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.

Manufacturing Tolerances:
Length ±3 · Height ±2 · Diagonals ±5 · Openings 0/+5 (mm).
Do not scale — work to figured dimensions. All dims in mm.

Breather Membrane:
Laps 100mm horizontal / 150mm vertical, upper lapping lower.


Panel Changes:
When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.

KEY PLAN




Revisions (Rev · Date · Note):		C01 - Construction issue					
Date:	2026-09-13	Scale:	1:20	Drawn:	TS	Checked:	
Project Name:		MP Adams Plot 3, Eckington					
Site:	Eckington			Client:	MP Adams		
Title:	Panel Fabrication — 38 x 140 C16 CLS						
Project Number:	P3			Revision:	C01		
Panel No:	GB-EX4			Drawing No:	P3-MF-GB-EX4		
Panel L×H×T:	2400×2656×149			Weight:	411 kg		
Status:	CONSTRUCTION			Sheet:	1 / 1		

Nailing: OSB/Ply racking: 150mm perimeter / 300mm field nails (EC5 §9.2.4, 2:1 panel h:b)

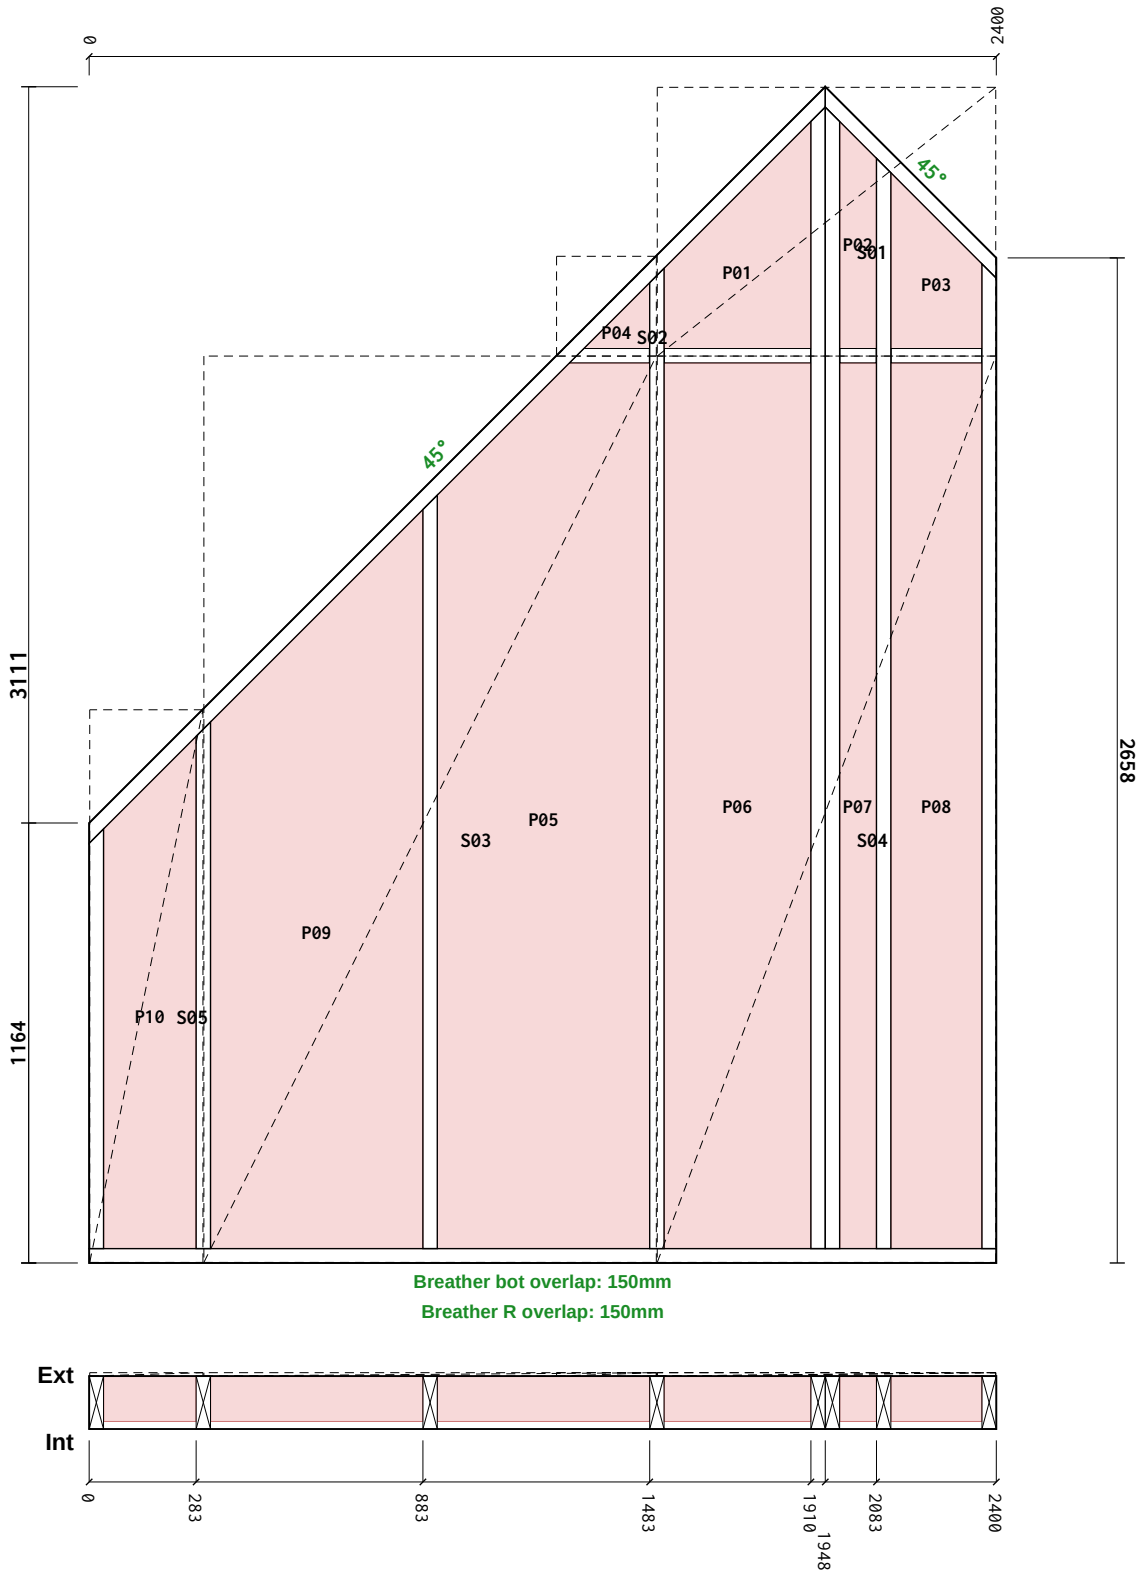

Section A-A



Cut List

Item	Section	Len	Bot°	Top°	Qty
BR1 Bottom Rail	38×140 C16	2400	0	0	1
TR1 Top Rail	38×140 C16	1947	0	0	1
TR2 Top Rail	38×140 C16	453	0	0	1
ES1 End Stud	38×140 C16	1110	0	-45.0	1
ES2 End Stud	38×140 C16	2604	0	45.0	1
VS1 Vertical Stud	38×140 C16	3019	0	45.0	1
VS2 Vertical Stud	38×140 C16	3019	0	-45.0	1
VS3 Vertical Stud	38×140 C16	2883	0	45.0	1
VS4 Vertical Stud	38×140 C16	2593	0	-45.0	1
VS5 Vertical Stud	38×140 C16	1993	0	-45.0	1
VS6 Vertical Stud	38×140 C16	1393	0	-45.0	1
NG1 Noggin	38×140 C16	386	0	0	1
NG2 Noggin	38×140 C16	239	0	0	1
NG3 Noggin	38×140 C16	211	0	0	1
NG4 Noggin	38×140 C16	96	0	0	1

Total: 15 pcs / 24.35 m

Sheathing & Insulation

Material	W	H	Label
OSB 9mm	896	711	S01
OSB 9mm	264	264	S02
OSB 9mm	1197	2397	S03
OSB 9mm	896	2397	S04
OSB 9mm	299	1462	S05
PIR 120mm	387	600	P01
PIR 120mm	97	600	P02
PIR 120mm	240	464	P03
PIR 120mm	174	173	P04
PIR 120mm	561	2342	P05
PIR 120mm	387	2342	P06
PIR 120mm	97	2342	P07
PIR 120mm	240	2342	P08
PIR 120mm	561	1954	P09
PIR 120mm	244	1354	P10

General Notes:

Frame Nailing:
140mm Frames Nail Using 3no, 3.1×90mm length field galvanised twisted strip nails
90mm Frames Nail Using 2no, 3.1×90mm length field galvanised twisted strip nails

Sheathing Nails:
Components ≤ 100mm should be +/- 1mm
Components > 100mm should be +/- 1.5mm
Stepped check should be +/- 1.5mm
Sloped Opening sizes are +/-2mm


Nailing:
30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.

Manufacturing Tolerances:
Length ±3 · Height ±2 · Diagonals ±5 · Openings 0/+5 (mm).
Do not scale — work to figured dimensions. All dims in mm.

Breather Membrane:
Laps 100mm horizontal / 150mm vertical, upper lapping lower.

Panel Changes:
When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.

KEY PLAN



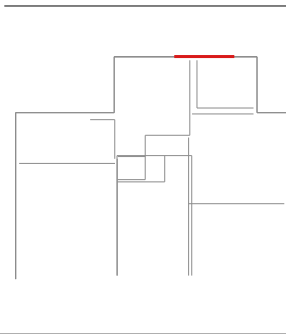


Revisions (Rev · Date · Note):

C01 - Construction issue

Date:	2026-09-13	Scale:	1:20	Drawn:	TS	Checked:	
Project Name:	MP Adams Plot 3, Eckington						
Site:	Eckington			Client:	MP Adams		
Title:	Panel Fabrication — 38 x 140 C16 CLS						
Project Number:	P3			Revision:	C01		
Panel No:	GB-EX5			Drawing No:	P3-MF-GB-EX5		
Panel L×H×T:	2400×3111×149			Weight:	346 kg		
Status:	CONSTRUCTION			Sheet:	1 / 1		

Nailing: OSB/Ply racking: 150mm perimeter / 300mm field nails (EC5 §9.2.4, 2:1 panel h:b)

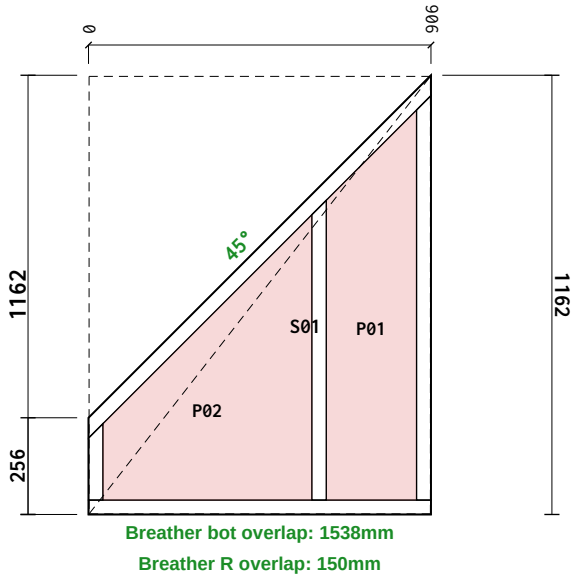

Cut List

Item	Section	Len	Bot°	Top°	Qty
BR1 Bottom Rail	38×140 C16	906	0	0	1
TR1 Top Rail	38×140 C16	906	0	0	1
ES1 End Stud	38×140 C16	202	0	-45.0	1
ES2 End Stud	38×140 C16	1070	0	-45.0	1
VS1 Vertical Stud	38×140 C16	793	0	-45.0	1
Total: 5 pcs / 3.88 m					

Sheathing & Insulation

Material	W	H	Label
OSB 9mm	903	1157	S01
PIR 120mm	238	1031	P01
PIR 120mm	552	754	P02

General Notes:

Frame Nailing:
140mm Frames Nail Using 3no, 3.1×90mm length field galvanised twisted strip nails
90mm Frames Nail Using 2no, 3.1×90mm length field galvanised twisted strip nails

Sheathing Nails:
Components ≤ 100mm should be +/- 1mm
Components > 100mm should be +/- 1.5mm
Stepped check should be +/- 1.5mm
Sloped Opening sizes are +/-2mm


Nailing:
30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.

Manufacturing Tolerances:
Length ±3 · Height ±2 · Diagonals ±5 · Openings 0/+5 (mm).
Do not scale — work to figured dimensions. All dims in mm.

Breather Membrane:
Laps 100mm horizontal / 150mm vertical, upper lapping lower.



Panel Changes:
When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.

KEY PLAN



Revisions (Rev · Date · Note):		C01 - Construction issue					
Date:	2026-09-13	Scale:	1:20	Drawn:	TS	Checked:	
Project Name:		MP Adams Plot 3, Eckington					
Site:	Eckington			Client:	MP Adams		
Title:	Panel Fabrication — 38 x 140 C16 CLS						
Project Number:	P3			Revision:	C01		
Panel No:	GB-EX6			Drawing No:	P3-MF-GB-EX6		
Panel L×H×T:	906×1162×149			Weight:	66 kg		
Status:	CONSTRUCTION			Sheet:	1 / 1		

Nailing: OSB/Ply racking: 150mm perimeter / 300mm field nails (EC5 §9.2.4, 2:1 panel h:b)

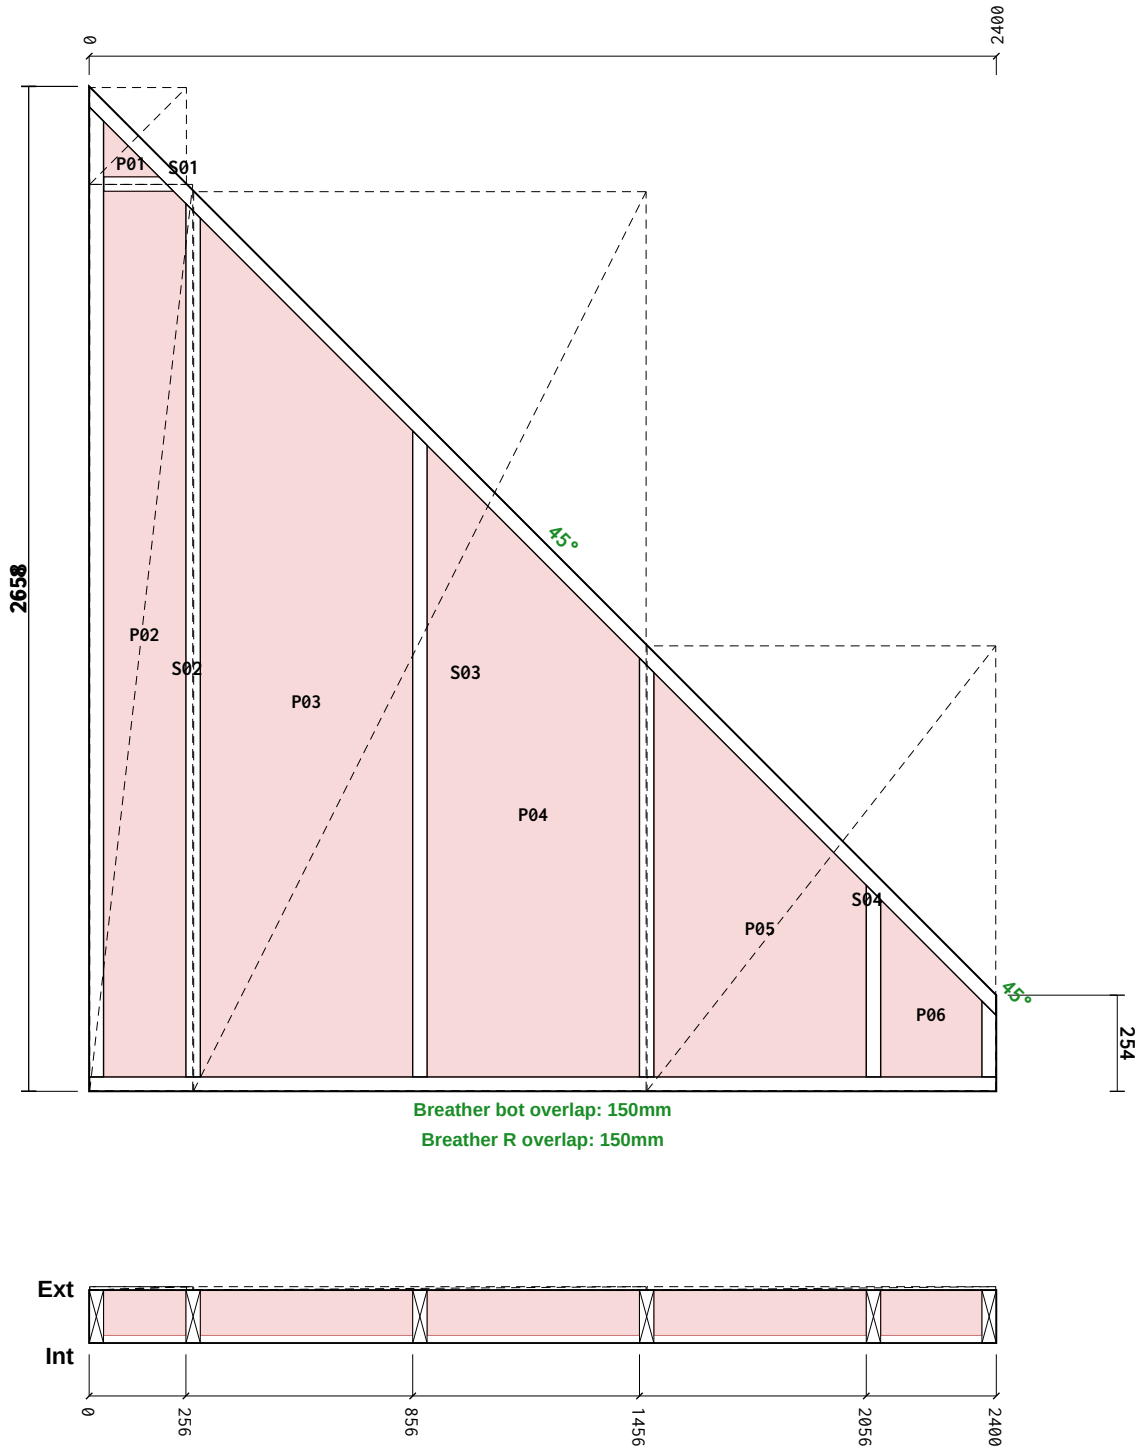

Cut List

Item	Section	Len	Bot°	Top°	Qty
BR1 Bottom Rail	38×140 C16	2400	0	0	1
TR1 Top Rail	38×140 C16	2398	0	0	1
TR2 Top Rail	38×140 C16	2	0	0	1
ES1 End Stud	38×140 C16	2566	0	45.0	1
ES2 End Stud	38×140 C16	201	0	45.0	1
VS1 Vertical Stud	38×140 C16	2310	0	45.0	1
VS2 Vertical Stud	38×140 C16	1709	0	45.0	1
VS3 Vertical Stud	38×140 C16	1108	0	45.0	1
VS4 Vertical Stud	38×140 C16	507	0	45.0	1
NG1 Noggin	38×140 C16	184	0	0	1

Total: 10 pcs / 13.38 m

Sheathing & Insulation

Material	W	HLabel
OSB 9mm	256	256 S01
OSB 9mm	272	2397 S02
OSB 9mm	1197	2378 S03
OSB 9mm	923	1177 S04
PIR 120mm	147	146 P01
PIR 120mm	217	2342 P02
PIR 120mm	561	2270 P03
PIR 120mm	561	1670 P04
PIR 120mm	561	1069 P05
PIR 120mm	267	468 P06

General Notes:

Frame Nailing:
140mm Frames Nail Using 3no, 3.1×90mm length field galvanised twisted strip nails
90mm Frames Nail Using 2no, 3.1×90mm length field galvanised twisted strip nails

Sheathing Nails:
Components ≤ 100mm should be +/- 1mm
Components > 100mm should be +/- 1.5mm
Stepped check should be +/- 1.5mm
Sloped Opening sizes are +/-2mm


Nailing:
30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.

Manufacturing Tolerances:
Length ±3 · Height ±2 · Diagonals ±5 · Openings 0/+5 (mm).
Do not scale — work to figured dimensions. All dims in mm.

Breather Membrane:
Laps 100mm horizontal / 150mm vertical, upper lapping lower.

Panel Changes:
When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.

KEY PLAN

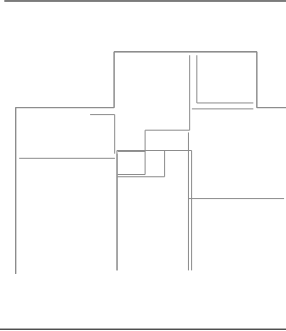


Revisions (Rev · Date · Note):


C01 - Construction issue

Date:	2026-09-13	Scale:	1:20	Drawn:	TS	Checked:	
Project Name:		MP Adams Plot 3, Eckington					
Site:	Eckington			Client:	MP Adams		
Title:		Panel Fabrication — 38 x 140 C16 CLS					
Project Number:		P3		Revision:	C01		
Panel No:		GB-EX7		Drawing No:	P3-MF-GB-EX7		
Panel L×H×T:		2400×2658×149		Weight:	411 kg		
Status:		CONSTRUCTION		Sheet:	1 / 1		

Nailing: OSB/Ply racking: 150mm perimeter / 300mm field nails (EC5 §9.2.4, 2:1 panel h:b)

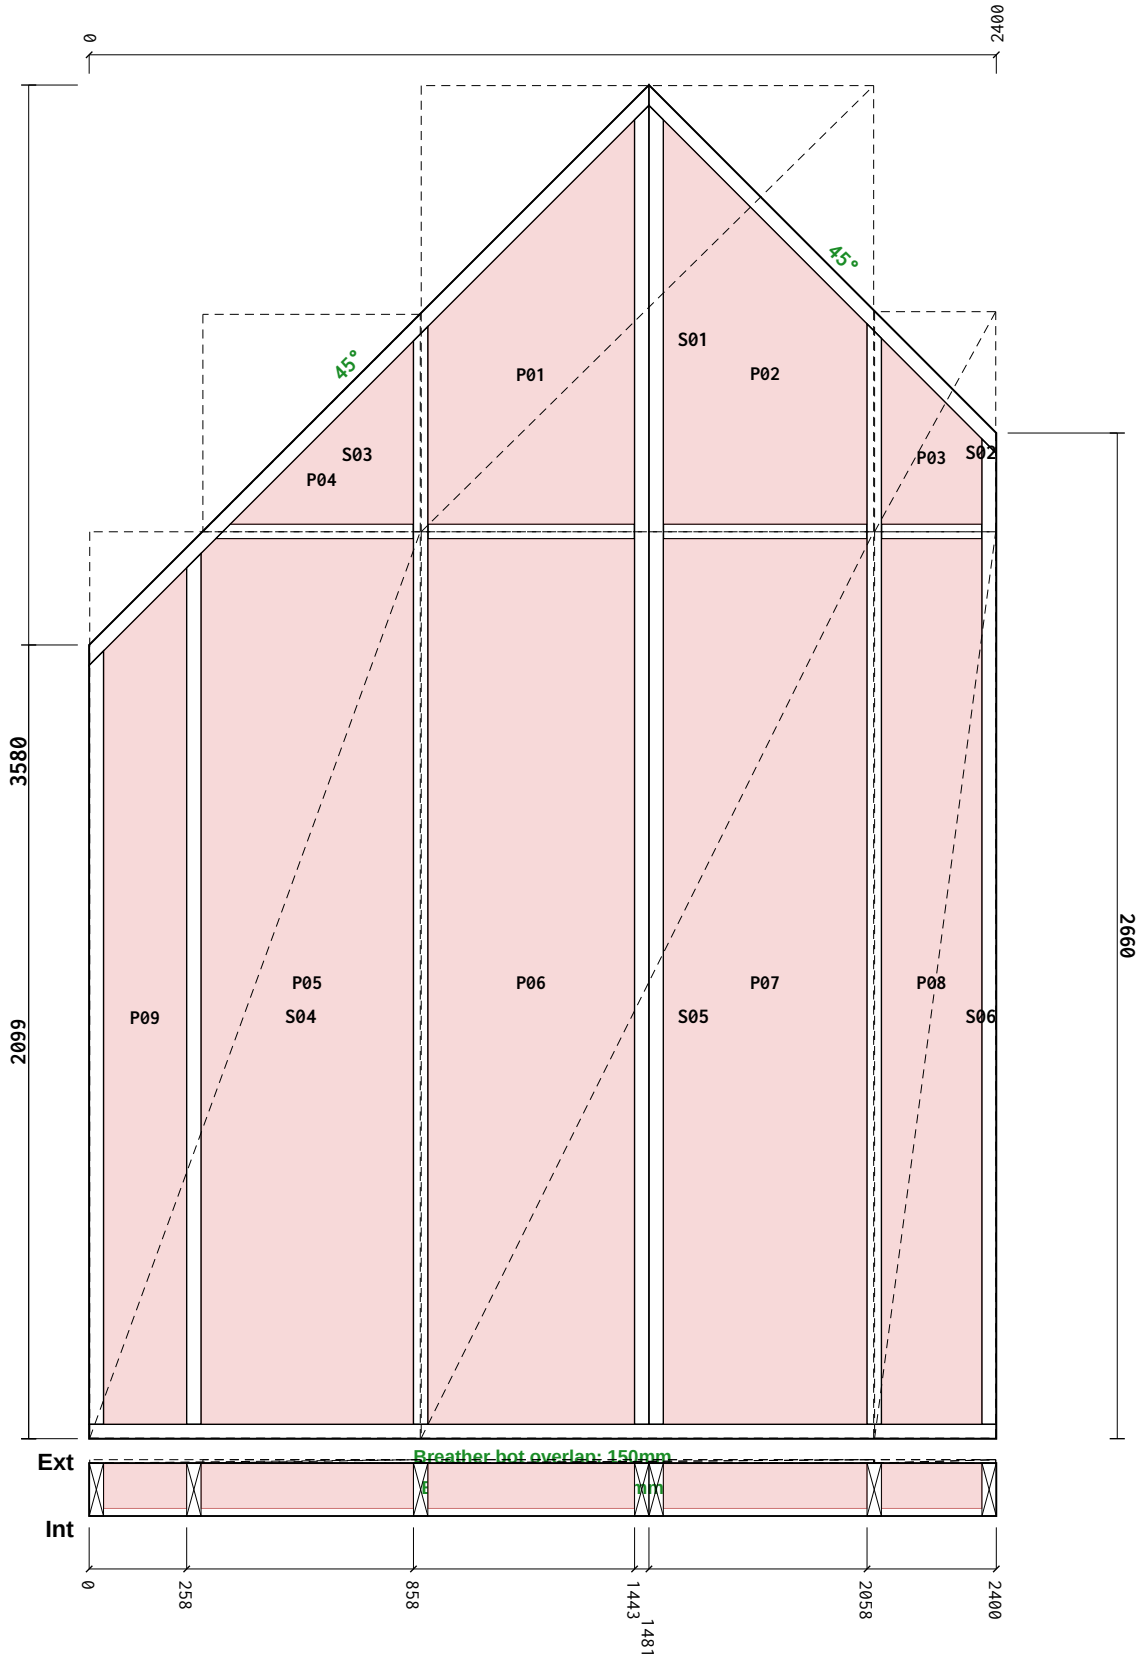

Section A-A



Cut List

Item	Section	Len	Bot°	Top°	Qty
BR1 Bottom Rail	38×140 C16	2400	0	0	1
TR1 Top Rail	38×140 C16	1481	0	0	1
TR2 Top Rail	38×140 C16	919	0	0	1
ES1 End Stud	38×140 C16	2045	0	-45.0	1
ES2 End Stud	38×140 C16	2606	0	45.0	1
VS1 Vertical Stud	38×140 C16	3488	0	45.0	1
VS2 Vertical Stud	38×140 C16	3488	0	-45.0	1
VS3 Vertical Stud	38×140 C16	2910	0	45.0	1
VS4 Vertical Stud	38×140 C16	2903	0	-45.0	1
VS5 Vertical Stud	38×140 C16	2303	0	-45.0	1
NG1 Noggin	38×140 C16	545	0	0	1
NG2 Noggin	38×140 C16	537	0	0	1
NG3 Noggin	38×140 C16	522	0	0	1
NG4 Noggin	38×140 C16	264	0	0	1

Total: 14 pcs / 26.41 m

Sheathing & Insulation

Material	W	H	Label
OSB 9mm	1197	1180	S01
OSB 9mm	321	582	S02
OSB 9mm	575	575	S03
OSB 9mm	874	2397	S04
OSB 9mm	1197	2397	S05
OSB 9mm	321	2397	S06
PIR 120mm	546	1069	P01
PIR 120mm	538	1069	P02
PIR 120mm	265	491	P03
PIR 120mm	484	484	P04
PIR 120mm	561	2342	P05
PIR 120mm	546	2342	P06
PIR 120mm	538	2342	P07
PIR 120mm	265	2342	P08
PIR 120mm	219	2264	P09

General Notes:

Frame Nailing:
140mm Frames Nail Using 3no, 3.1×90mm length field galvanised twisted strip nails
90mm Frames Nail Using 2no, 3.1×90mm length field galvanised twisted strip nails

Sheathing Nails:
Components ≤ 100mm should be +/- 1mm
Components > 100mm should be +/- 1.5mm
Stepped check should be +/- 1.5mm
Sloped Opening sizes are +/-2mm


Nailing:
30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.

Manufacturing Tolerances:
Length ±3 · Height ±2 · Diagonals ±5 · Openings 0/+5 (mm).
Do not scale — work to figured dimensions. All dims in mm.

Breather Membrane:
Laps 100mm horizontal / 150mm vertical, upper lapping lower.


Panel Changes:
When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.

KEY PLAN




Revisions (Rev · Date · Note):		C01 - Construction issue					
Date:	2026-09-13	Scale:	1:20	Drawn:	TS	Checked:	
Project Name:		MP Adams Plot 3, Eckington					
Site:	Eckington			Client:	MP Adams		
Title:		Panel Fabrication — 38 x 140 C16 CLS					
Project Number:		P3		Revision:		C01	
Panel No:		GB-EX8		Drawing No:		P3-MF-GB-EX8	
Panel L×H×T:		2400×3580×149		Weight:		309 kg	
Status:		CONSTRUCTION		Sheet:		1 / 1	

Nailing: OSB/Ply racking: 150mm perimeter / 300mm field nails (EC5 §9.2.4, 2:1 panel h:b)

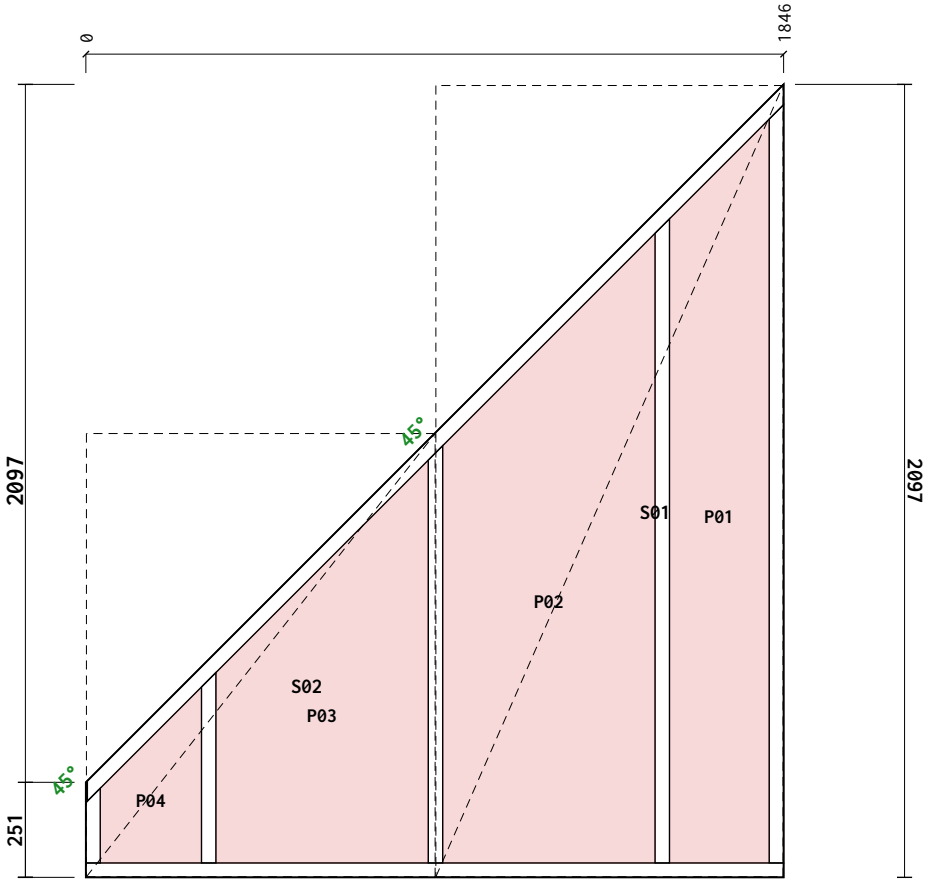


Breather bot overlap: 603mm

Breather R overlap: 150mm



Section A-A



Cut List

Item	Section	Len	Bot°	Top°	Qty
BR1 Bottom Rail	38×140 C16	1846	0	0	1
TR1 Top Rail	38×140 C16	1842	0	0	1
TR2 Top Rail	38×140 C16	4	0	0	1
ES1 End Stud	38×140 C16	198	0	-45.0	1
ES2 End Stud	38×140 C16	2005	0	-45.0	1
VS1 Vertical Stud	38×140 C16	1703	0	-45.0	1
VS2 Vertical Stud	38×140 C16	1104	0	-45.0	1
VS3 Vertical Stud	38×140 C16	504	0	-45.0	1
Total: 8 pcs / 9.21 m					

Sheathing & Insulation

Material	W	HLabel
OSB 9mm	919	2093 S01
OSB 9mm	922	1172 S02
PIR 120mm	263	1966 P01
PIR 120mm	561	1664 P02
PIR 120mm	561	1065 P03
PIR 120mm	267	465 P04

General Notes:

Frame Nailing:
140mm Frames Nail Using 3no, 3.1×90mm length field galvanised twisted strip nails
90mm Frames Nail Using 2no, 3.1×90mm length field galvanised twisted strip nails

Sheathing Nails:
Components ≤ 100mm should be +/- 1mm
Components > 100mm should be +/- 1.5mm
Stepped check should be +/- 1.5mm
Sloped Opening sizes are +/-2mm


Nailing:
30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.

Manufacturing Tolerances:
Length ±3 · Height ±2 · Diagonals ±5 · Openings 0/+5 (mm).
Do not scale — work to figured dimensions. All dims in mm.

Breather Membrane:
Laps 100mm horizontal / 150mm vertical, upper lapping lower.

Panel Changes:
When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.

KEY PLAN



Revisions (Rev · Date · Note):

C01 - Construction issue

Date:	2026-09-13	Scale:	1:20	Drawn:	TS	Checked:		
Project Name:		MP Adams Plot 3, Eckington						
Site:		Eckington			Client:			MP Adams
Title:		Panel Fabrication — 38 x 140 C16 CLS						
Project Number:		P3			Revision:			C01
Panel No:		GB-EX9			Drawing No:			P3-MF-GB-EX9
Panel L×H×T:		1846×2097×149			Weight:			247 kg
Status:		CONSTRUCTION			Sheet:			1 / 1
