



Nailing: OSB/Ply racking: 150mm perimeter / 300mm field nails (EC5 §9.2.4, 2:1 panel h:b)

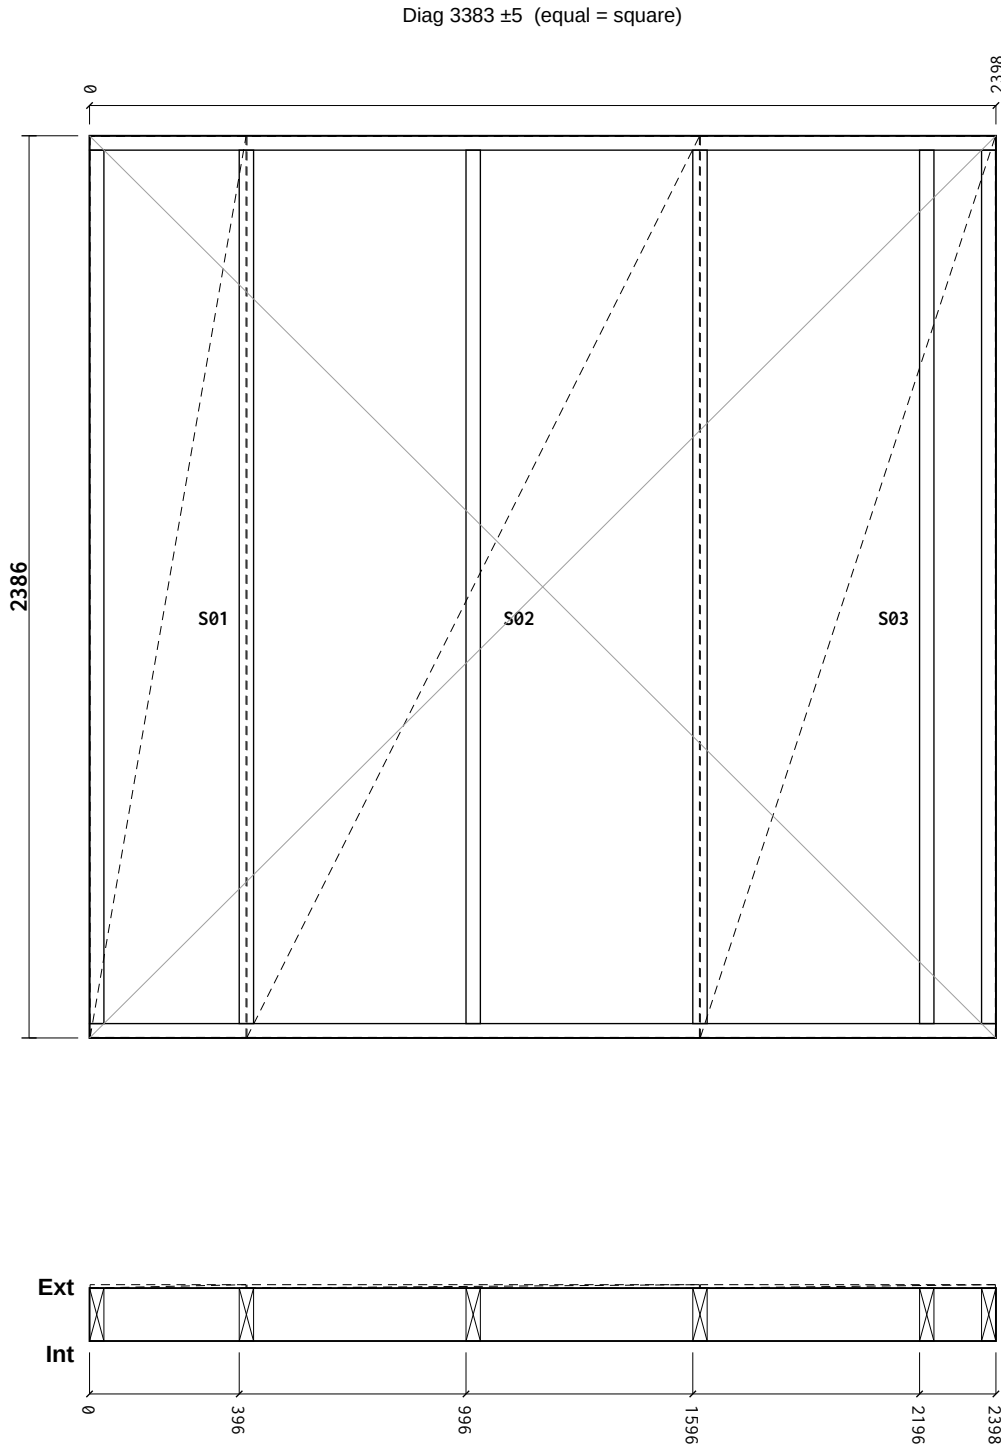

### Cut List

| Item                   | Section    | Len  | Bot° | Top° | Qty |
|------------------------|------------|------|------|------|-----|
| BR1 Bottom Rail        | 38×140 C16 | 2398 | 0    | 0    | 1   |
| TR1 Top Rail           | 38×140 C16 | 2398 | 0    | 0    | 1   |
| ES1 End Stud           | 38×140 C16 | 2310 | 0    | 0    | 1   |
| ES2 End Stud           | 38×140 C16 | 2310 | 0    | 0    | 1   |
| VS1 Vertical Stud      | 38×140 C16 | 2310 | 0    | 0    | 4   |
| Total: 8 pcs / 18.66 m |            |      |      |      |     |

### Sheathing & Insulation

| Material | W    | H    | Label |
|----------|------|------|-------|
| OSB 9mm  | 413  | 2383 | S01   |
| OSB 9mm  | 1197 | 2383 | S02   |
| OSB 9mm  | 780  | 2383 | S03   |

#### General Notes:

**Frame Nailing:**  
140mm Frames Nail Using 3no, 3.1×90mm length field galvanised twisted strip nails  
90mm Frames Nail Using 2no, 3.1×90mm length field galvanised twisted strip nails


**Sheathing Nails:**  
Components ≤ 100mm should be +/- 1mm  
Components > 100mm should be +/- 1.5mm  
Stepped check should be +/- 1.5mm  
Sloped Opening sizes are +/-2mm

**Nailing:**  
30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.

**Manufacturing Tolerances:**  
Length ±3 · Height ±2 · Diagonals ±5 · Openings 0/+5 (mm).  
Do not scale — work to figured dimensions. All dims in mm.

**Panel Changes:**  
When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.

#### KEY PLAN





Revisions (Rev · Date · Note):

C01 - Construction issue

|                 |            |                                      |      |             |    |              |  |
|-----------------|------------|--------------------------------------|------|-------------|----|--------------|--|
| Date:           | 2026-09-13 | Scale:                               | 1:20 | Drawn:      | TS | Checked:     |  |
| Project Name:   |            | MP Adams Plot 3, Eckington           |      |             |    |              |  |
| Site:           |            | Eckington                            |      | Client:     |    | MP Adams     |  |
| Title:          |            | Panel Fabrication — 38 x 140 C16 CLS |      |             |    |              |  |
| Project Number: |            | P3                                   |      | Revision:   |    | C01          |  |
| Panel No:       |            | GF-IL1                               |      | Drawing No: |    | P3-MF-GF-IL1 |  |
| Panel L×H×T:    |            | 2398×2386×149                        |      | Weight:     |    | 73 kg        |  |
| Status:         |            | CONSTRUCTION                         |      | Sheet:      |    | 1 / 1        |  |

Nailing: OSB/Ply racking: 150mm perimeter / 300mm field nails (EC5 §9.2.4, 2:1 panel h:b)

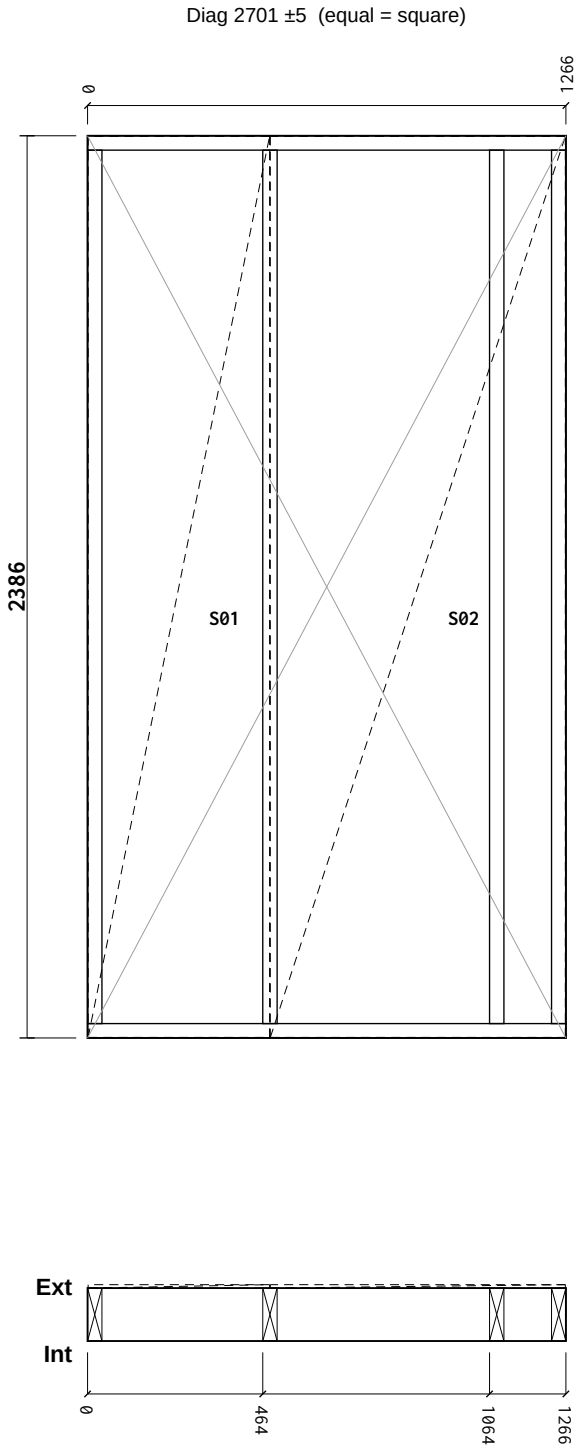

### Cut List

| Item                   | Section    | Len  | Bot° | Top° | Qty |
|------------------------|------------|------|------|------|-----|
| BR1 Bottom Rail        | 38×140 C16 | 1265 | 0    | 0    | 1   |
| TR1 Top Rail           | 38×140 C16 | 1265 | 0    | 0    | 1   |
| ES1 End Stud           | 38×140 C16 | 2310 | 0    | 0    | 1   |
| ES2 End Stud           | 38×140 C16 | 2310 | 0    | 0    | 1   |
| VS1 Vertical Stud      | 38×140 C16 | 2310 | 0    | 0    | 2   |
| Total: 6 pcs / 11.77 m |            |      |      |      |     |

### Sheathing & Insulation

| Material | W   | H    | Label |
|----------|-----|------|-------|
| OSB 9mm  | 480 | 2383 | S01   |
| OSB 9mm  | 780 | 2383 | S02   |

#### General Notes:

**Frame Nailing:**  
140mm Frames Nail Using 3no, 3.1×90mm length field galvanised twisted strip nails  
90mm Frames Nail Using 2no, 3.1×90mm length field galvanised twisted strip nails


**Sheathing Nails:**  
Components ≤ 100mm should be +/- 1mm  
Components > 100mm should be +/- 1.5mm  
Stepped check should be +/- 1.5mm  
Sloped Opening sizes are +/-2mm

**Nailing:**  
30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.

**Manufacturing Tolerances:**  
Length ±3 · Height ±2 · Diagonals ±5 · Openings 0/+5 (mm).  
Do not scale — work to figured dimensions. All dims in mm.

**Panel Changes:**  
When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.

#### KEY PLAN





Revisions (Rev · Date · Note):

C01 - Construction issue

|                 |            |                                      |      |             |              |          |  |
|-----------------|------------|--------------------------------------|------|-------------|--------------|----------|--|
| Date:           | 2026-09-13 | Scale:                               | 1:20 | Drawn:      | TS           | Checked: |  |
| Project Name:   |            | MP Adams Plot 3, Eckington           |      |             |              |          |  |
| Site:           | Eckington  |                                      |      | Client:     | MP Adams     |          |  |
| Title:          |            | Panel Fabrication — 38 x 140 C16 CLS |      |             |              |          |  |
| Project Number: |            | P3                                   |      | Revision:   | C01          |          |  |
| Panel No:       |            | GF-IL2                               |      | Drawing No: | P3-MF-GF-IL2 |          |  |
| Panel L×H×T:    |            | 1265×2386×149                        |      | Weight:     | 43 kg        |          |  |
| Status:         |            | CONSTRUCTION                         |      | Sheet:      | 1 / 1        |          |  |

Nailing: OSB/Ply racking: 150mm perimeter / 300mm field nails (EC5 §9.2.4, 2:1 panel h:b)

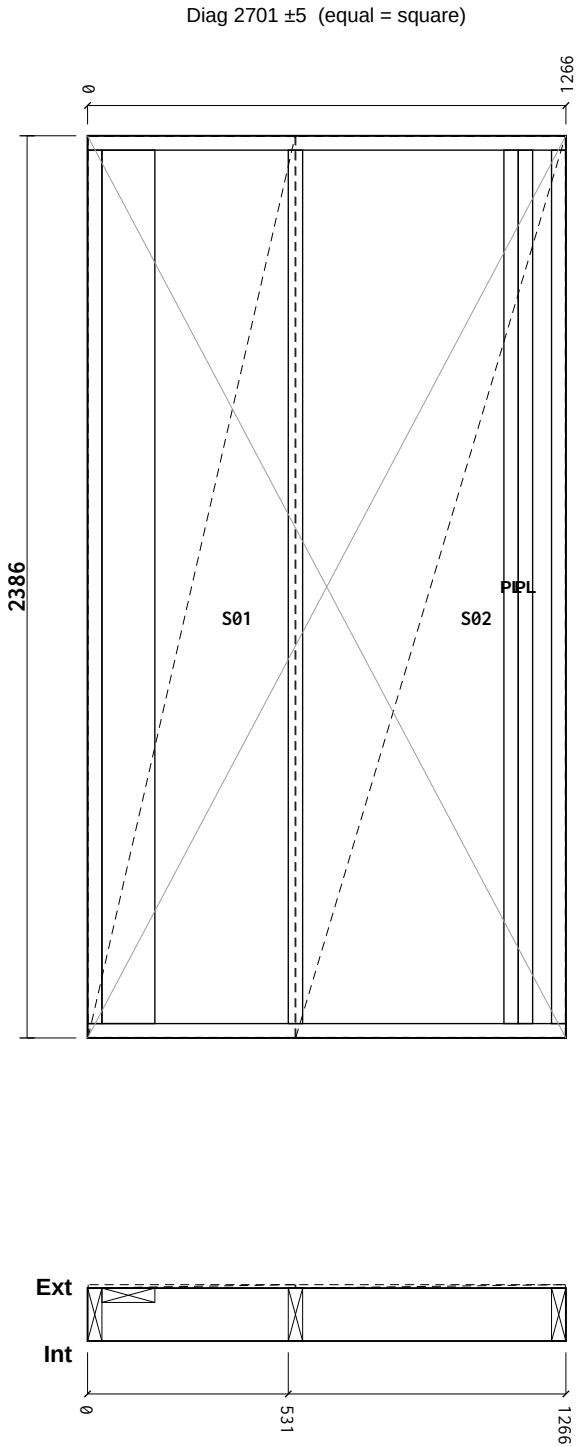

### Cut List

| Item                   | Section    | Len  | Bot° | Top° | Qty |
|------------------------|------------|------|------|------|-----|
| BR1 Bottom Rail        | 38×140 C16 | 1265 | 0    | 0    | 1   |
| TR1 Top Rail           | 38×140 C16 | 1265 | 0    | 0    | 1   |
| ES1 End Stud           | 38×140 C16 | 2310 | 0    | 0    | 1   |
| ES2 End Stud           | 38×140 C16 | 2310 | 0    | 0    | 1   |
| VS1 Vertical Stud      | 38×140 C16 | 2310 | 0    | 0    | 1   |
| JS1 Junction Stud      | 38×140 C16 | 2310 | 0    | 0    | 1   |
| Total: 6 pcs / 11.77 m |            |      |      |      |     |

### Sheathing & Insulation

| Material | W   | H    | Label |
|----------|-----|------|-------|
| OSB 9mm  | 548 | 2383 | S01   |
| OSB 9mm  | 713 | 2383 | S02   |

#### General Notes:

**Frame Nailing:**  
140mm Frames Nail Using 3no, 3.1×90mm length field galvanised twisted strip nails  
90mm Frames Nail Using 2no, 3.1×90mm length field galvanised twisted strip nails


**Sheathing Nails:**  
Components ≤ 100mm should be +/- 1mm  
Components > 100mm should be +/- 1.5mm  
Stepped check should be +/- 1.5mm  
Sloped Opening sizes are +/-2mm

**Nailing:**  
30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.

**Manufacturing Tolerances:**  
Length ±3 · Height ±2 · Diagonals ±5 · Openings 0/+5 (mm).  
Do not scale — work to figured dimensions. All dims in mm.

**Panel Changes:**  
When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.

#### KEY PLAN





Revisions (Rev · Date · Note):

#### C01 - Construction issue

|                 |            |                                      |      |        |             |          |              |
|-----------------|------------|--------------------------------------|------|--------|-------------|----------|--------------|
| Date:           | 2026-09-13 | Scale:                               | 1:20 | Drawn: | TS          | Checked: |              |
| Project Name:   |            | MP Adams Plot 3, Eckington           |      |        |             |          |              |
| Site:           |            | Eckington                            |      |        | Client:     |          | MP Adams     |
| Title:          |            | Panel Fabrication — 38 x 140 C16 CLS |      |        |             |          |              |
| Project Number: |            | P3                                   |      |        | Revision:   |          | C01          |
| Panel No:       |            | GF-IL3                               |      |        | Drawing No: |          | P3-MF-GF-IL3 |
| Panel L×H×T:    |            | 1265×2386×149                        |      |        | Weight:     |          | 43 kg        |
| Status:         |            | CONSTRUCTION                         |      |        | Sheet:      |          | 1 / 1        |

Nailing: OSB/Ply racking: 150mm perimeter / 300mm field nails (EC5 §9.2.4, 2:1 panel h:b)

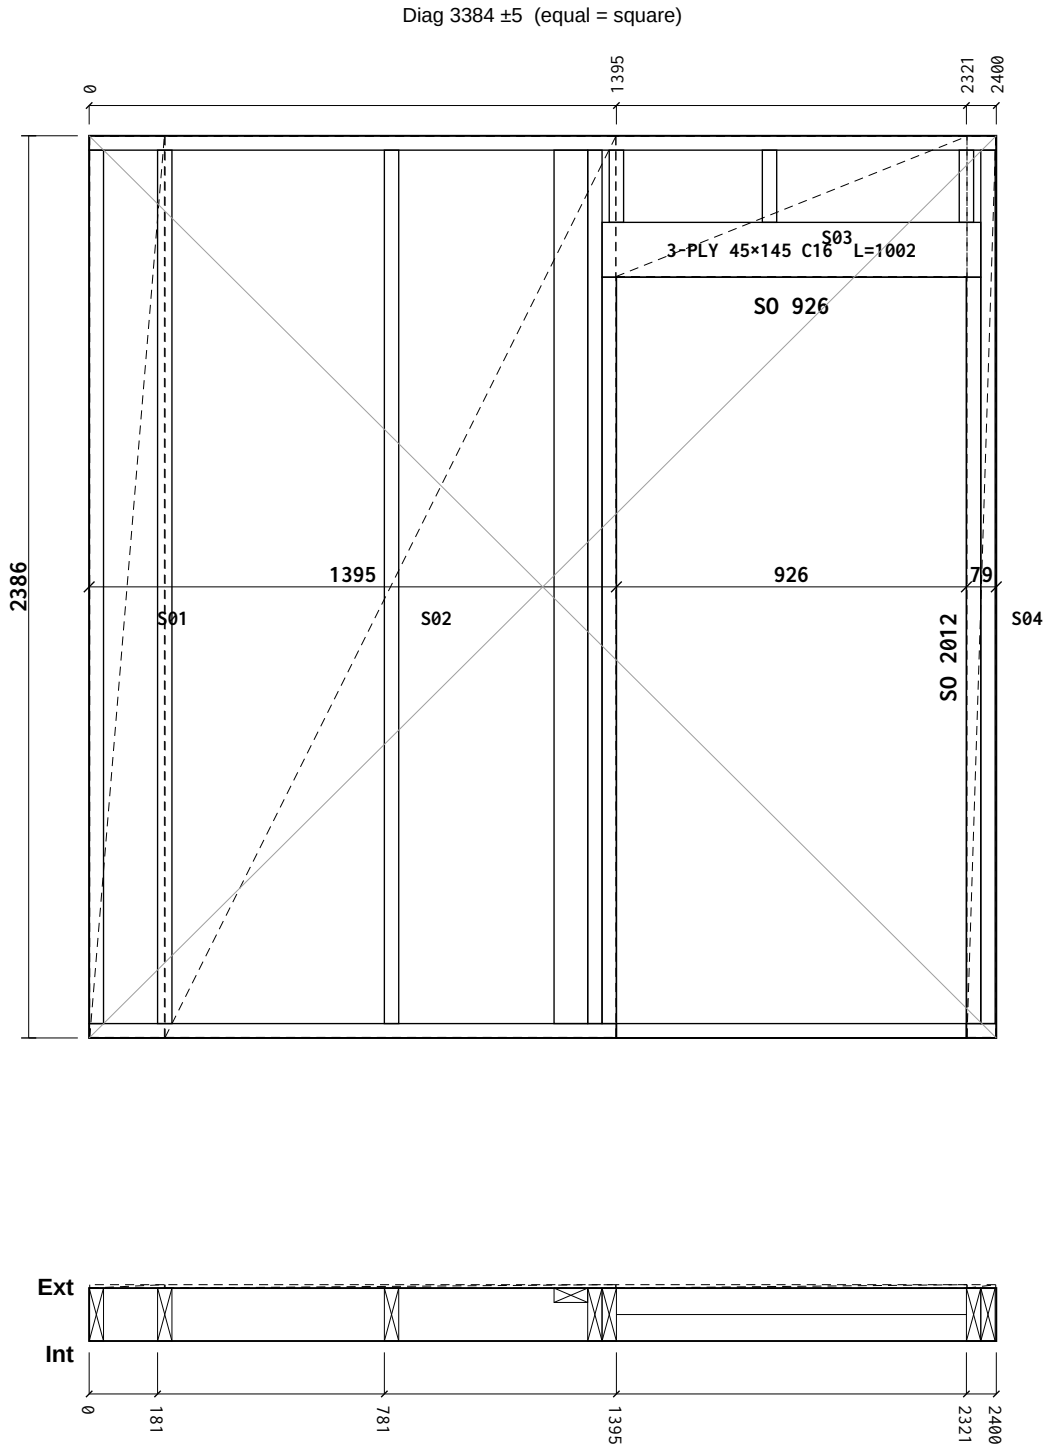

### Cut List

| Item                    | Section     | Len  | Bot° | Top° | Qty |
|-------------------------|-------------|------|------|------|-----|
| BR1 Bottom Rail         | 38×140 C16  | 1395 | 0    | 0    | 1   |
| BR2 Bottom Rail         | 38×140 C16  | 926  | 0    | 0    | 1   |
| BR3 Bottom Rail         | 38×140 C16  | 79   | 0    | 0    | 1   |
| TR1 Top Rail            | 38×140 C16  | 2400 | 0    | 0    | 1   |
| ES1 End Stud            | 38×140 C16  | 2310 | 0    | 0    | 1   |
| ES2 End Stud            | 38×140 C16  | 191  | 0    | 0    | 1   |
| KS1 Vertical Stud       | 38×140 C16  | 2310 | 0    | 0    | 2   |
| CS1 Cripple Stud        | 38×140 C16  | 1974 | 0    | 0    | 2   |
| LP1 Lintel Ply          | 1002×45 C16 | 1002 | 0    | 0    | 3   |
| OS1 OSB Support         | 38×140 C16  | 191  | 0    | 0    | 2   |
| VS1 Vertical Stud       | 38×140 C16  | 2310 | 0    | 0    | 2   |
| JS1 Junction Stud       | 38×89 C16   | 2310 | 0    | 0    | 1   |
| Total: 18 pcs / 26.19 m |             |      |      |      |     |

### Sheathing & Insulation

| Material | W    | H    | Label |
|----------|------|------|-------|
| OSB 9mm  | 198  | 2383 | S01   |
| OSB 9mm  | 1192 | 2383 | S02   |
| OSB 9mm  | 929  | 371  | S03   |
| OSB 9mm  | 76   | 2383 | S04   |

#### General Notes:

**Frame Nailing:**  
140mm Frames Nail Using 3no, 3.1×90mm length field galvanised twisted strip nails  
90mm Frames Nail Using 2no, 3.1×90mm length field galvanised twisted strip nails


**Sheathing Nails:**  
Components ≤ 100mm should be +/- 1mm  
Components > 100mm should be +/- 1.5mm  
Stepped check should be +/- 1.5mm  
Sloped Opening sizes are +/-2mm

**Nailing:**  
30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.

**Manufacturing Tolerances:**  
Length ±3 · Height ±2 · Diagonals ±5 · Openings 0/+5 (mm).  
Do not scale — work to figured dimensions. All dims in mm.

**Panel Changes:**  
When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.



#### KEY PLAN




|                                |                                      |                            |      |             |              |          |  |
|--------------------------------|--------------------------------------|----------------------------|------|-------------|--------------|----------|--|
| Revisions (Rev · Date · Note): |                                      | C01 - Construction issue   |      |             |              |          |  |
| Date:                          | 2026-09-13                           | Scale:                     | 1:20 | Drawn:      | TS           | Checked: |  |
| Project Name:                  |                                      | MP Adams Plot 3, Eckington |      |             |              |          |  |
| Site:                          | Eckington                            |                            |      | Client:     | MP Adams     |          |  |
| Title:                         | Panel Fabrication — 38 x 140 C16 CLS |                            |      |             |              |          |  |
| Project Number:                | P3                                   |                            |      | Revision:   | C01          |          |  |
| Panel No:                      | GF-IL4                               |                            |      | Drawing No: | P3-MF-GF-IL4 |          |  |
| Panel L×H×T:                   | 2400×2386×149                        |                            |      | Weight:     | 79 kg        |          |  |
| Status:                        | CONSTRUCTION                         |                            |      | Sheet:      | 1 / 1        |          |  |

Nailing: OSB/Ply racking: 150mm perimeter / 300mm field nails (EC5 §9.2.4, 2:1 panel h:b)

Diag 2494 ±5 (equal = square)

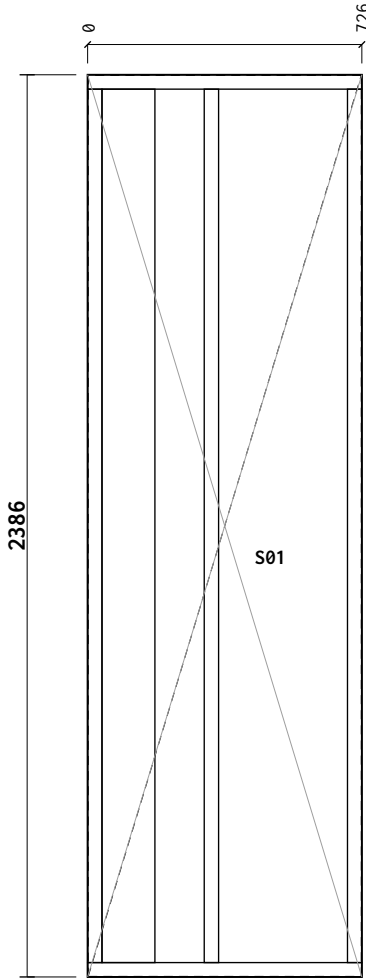

Section A-A



Cut List

| Item                   | Section    | Len  | Bot° | Top° | Qty |
|------------------------|------------|------|------|------|-----|
| BR1 Bottom Rail        | 38×140 C16 | 725  | 0    | 0    | 1   |
| TR1 Top Rail           | 38×140 C16 | 725  | 0    | 0    | 1   |
| ES1 End Stud           | 38×140 C16 | 2310 | 0    | 0    | 1   |
| ES2 End Stud           | 38×140 C16 | 2310 | 0    | 0    | 1   |
| VS1 Vertical Stud      | 38×140 C16 | 2310 | 0    | 0    | 1   |
| JS1 Junction Stud      | 38×140 C16 | 2310 | 0    | 0    | 1   |
| Total: 6 pcs / 10.69 m |            |      |      |      |     |

Sheathing & Insulation

| Material | W   | H    | Label |
|----------|-----|------|-------|
| OSB 9mm  | 722 | 2383 | S01   |

General Notes:


- Frame Nailing:**  
140mm Frames Nail Using 3no, 3.1×90mm length field galvanised twisted strip nails  
90mm Frames Nail Using 2no, 3.1×90mm length field galvanised twisted strip nails

**Sheathing Nails:**  
Components ≤ 100mm should be +/- 1mm  
Components > 100mm should be +/- 1.5mm  
Stepped check should be +/- 1.5mm  
Sloped Opening sizes are +/-2mm

**Nailing:**  
30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.



**Manufacturing Tolerances:**  
Length ±3 · Height ±2 · Diagonals ±5 · Openings 0/+5 (mm).  
Do not scale — work to figured dimensions. All dims in mm.
- Panel Changes:**  
When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.

KEY PLAN



|                                |            |                                      |      |                          |    |              |  |
|--------------------------------|------------|--------------------------------------|------|--------------------------|----|--------------|--|
| Revisions (Rev · Date · Note): |            |                                      |      | C01 - Construction issue |    |              |  |
| Date:                          | 2026-09-13 | Scale:                               | 1:20 | Drawn:                   | TS | Checked:     |  |
| Project Name:                  |            | MP Adams Plot 3, Eckington           |      |                          |    |              |  |
| Site:                          |            | Eckington                            |      | Client:                  |    | MP Adams     |  |
| Title:                         |            | Panel Fabrication — 38 x 140 C16 CLS |      |                          |    |              |  |
| Project Number:                |            | P3                                   |      | Revision:                |    | C01          |  |
| Panel No:                      |            | GF-IL5                               |      | Drawing No:              |    | P3-MF-GF-IL5 |  |
| Panel L×H×T:                   |            | 725×2386×149                         |      | Weight:                  |    | 33 kg        |  |
| Status:                        |            | CONSTRUCTION                         |      | Sheet:                   |    | 1 / 1        |  |

Nailing: OSB/Ply racking: 150mm perimeter / 300mm field nails (EC5 §9.2.4, 2:1 panel h:b)

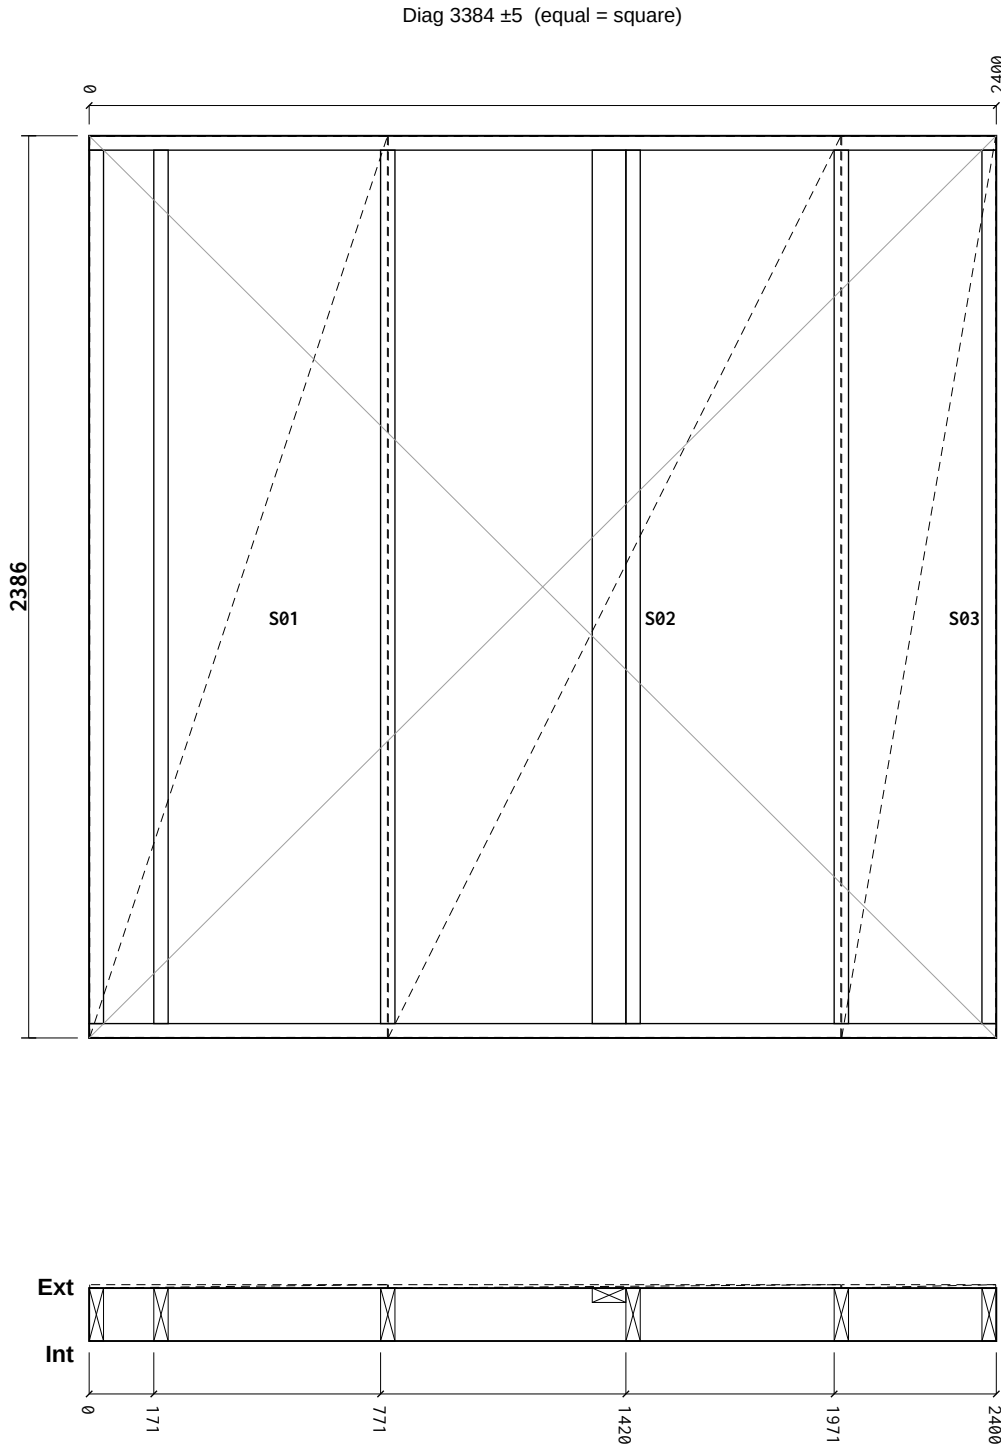

### Cut List

| Item                   | Section    | Len  | Bot° | Top° | Qty |
|------------------------|------------|------|------|------|-----|
| BR1 Bottom Rail        | 38×140 C16 | 2400 | 0    | 0    | 1   |
| TR1 Top Rail           | 38×140 C16 | 2400 | 0    | 0    | 1   |
| ES1 End Stud           | 38×140 C16 | 2310 | 0    | 0    | 1   |
| ES2 End Stud           | 38×140 C16 | 2310 | 0    | 0    | 1   |
| VS1 Vertical Stud      | 38×140 C16 | 2310 | 0    | 0    | 4   |
| JS1 Junction Stud      | 38×89 C16  | 2310 | 0    | 0    | 1   |
| Total: 9 pcs / 20.97 m |            |      |      |      |     |

### Sheathing & Insulation

| Material | W    | H    | Label |
|----------|------|------|-------|
| OSB 9mm  | 787  | 2383 | S01   |
| OSB 9mm  | 1197 | 2383 | S02   |
| OSB 9mm  | 408  | 2383 | S03   |

#### General Notes:

**Frame Nailing:**  
140mm Frames Nail Using 3no, 3.1×90mm length field galvanised twisted strip nails  
90mm Frames Nail Using 2no, 3.1×90mm length field galvanised twisted strip nails


**Sheathing Nails:**  
Components ≤ 100mm should be +/- 1mm  
Components > 100mm should be +/- 1.5mm  
Stepped check should be +/- 1.5mm  
Sloped Opening sizes are +/-2mm

**Nailing:**  
30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.

**Manufacturing Tolerances:**  
Length ±3 · Height ±2 · Diagonals ±5 · Openings 0/+5 (mm).  
Do not scale — work to figured dimensions. All dims in mm.



**Panel Changes:**  
When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.

#### KEY PLAN



|                                |                                      |                            |      |             |              |          |  |
|--------------------------------|--------------------------------------|----------------------------|------|-------------|--------------|----------|--|
| Revisions (Rev · Date · Note): |                                      | C01 - Construction issue   |      |             |              |          |  |
| Date:                          | 2026-09-13                           | Scale:                     | 1:20 | Drawn:      | TS           | Checked: |  |
| Project Name:                  |                                      | MP Adams Plot 3, Eckington |      |             |              |          |  |
| Site:                          | Eckington                            |                            |      | Client:     | MP Adams     |          |  |
| Title:                         | Panel Fabrication — 38 x 140 C16 CLS |                            |      |             |              |          |  |
| Project Number:                | P3                                   |                            |      | Revision:   | C01          |          |  |
| Panel No:                      | GF-IL6                               |                            |      | Drawing No: | P3-MF-GF-IL6 |          |  |
| Panel L×H×T:                   | 2400×2386×149                        |                            |      | Weight:     | 76 kg        |          |  |
| Status:                        | CONSTRUCTION                         |                            |      | Sheet:      | 1 / 1        |          |  |

Nailing: OSB/Ply racking: 150mm perimeter / 300mm field nails (EC5 §9.2.4, 2:1 panel h:b)

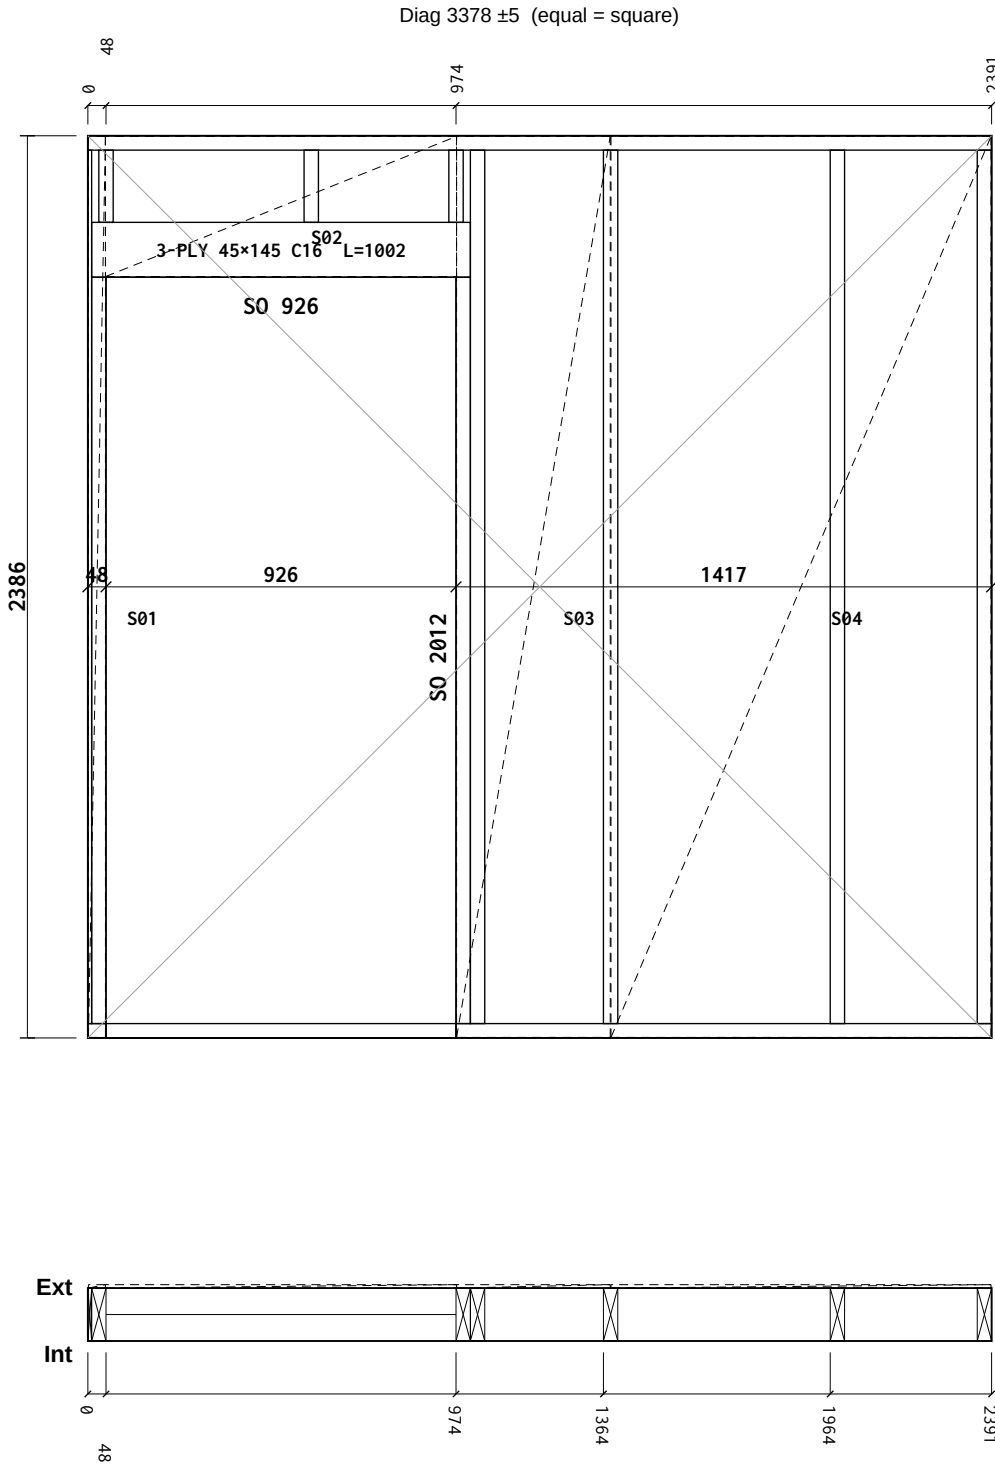

### Cut List

| Item              | Section     | Len  | Bot° | Top° | Qty |
|-------------------|-------------|------|------|------|-----|
| BR1 Bottom Rail   | 38×140 C16  | 1417 | 0    | 0    | 1   |
| BR2 Bottom Rail   | 38×140 C16  | 926  | 0    | 0    | 1   |
| BR3 Bottom Rail   | 38×140 C16  | 48   | 0    | 0    | 1   |
| TR1 Top Rail      | 38×140 C16  | 2391 | 0    | 0    | 1   |
| ES1 End Stud      | 38×140 C16  | 191  | 0    | 0    | 1   |
| ES2 End Stud      | 38×140 C16  | 2310 | 0    | 0    | 1   |
| KS1 Vertical Stud | 38×140 C16  | 2310 | 0    | 0    | 1   |
| KS2 Vertical Stud | 10×140 C16  | 2310 | 0    | 0    | 1   |
| CS1 Cripple Stud  | 38×140 C16  | 1974 | 0    | 0    | 2   |
| LP1 Lintel Ply    | 1002×45 C16 | 1002 | 0    | 0    | 3   |
| OS1 OSB Support   | 38×140 C16  | 191  | 0    | 0    | 2   |
| VS1 Vertical Stud | 38×140 C16  | 2310 | 0    | 0    | 2   |

Total: 17 pcs / 23.86 m

### Sheathing & Insulation

| Material | W    | H    | Label |
|----------|------|------|-------|
| OSB 9mm  | 45   | 2383 | S01   |
| OSB 9mm  | 929  | 371  | S02   |
| OSB 9mm  | 406  | 2383 | S03   |
| OSB 9mm  | 1006 | 2383 | S04   |

#### General Notes:

**Frame Nailing:**  
140mm Frames Nail Using 3no, 3.1×90mm length field galvanised twisted strip nails  
90mm Frames Nail Using 2no, 3.1×90mm length field galvanised twisted strip nails


**Sheathing Nails:**  
Components ≤ 100mm should be +/- 1mm  
Components > 100mm should be +/- 1.5mm  
Stepped check should be +/- 1.5mm  
Sloped Opening sizes are +/-2mm

**Nailing:**  
30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.

**Manufacturing Tolerances:**  
Length ±3 · Height ±2 · Diagonals ±5 · Openings 0/+5 (mm).  
Do not scale — work to figured dimensions. All dims in mm.

**Panel Changes:**  
When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.

#### KEY PLAN



|                                |                                      |                            |      |             |              |          |  |
|--------------------------------|--------------------------------------|----------------------------|------|-------------|--------------|----------|--|
| Revisions (Rev · Date · Note): |                                      | C01 - Construction issue   |      |             |              |          |  |
| Date:                          | 2026-09-13                           | Scale:                     | 1:20 | Drawn:      | TS           | Checked: |  |
| Project Name:                  |                                      | MP Adams Plot 3, Eckington |      |             |              |          |  |
| Site:                          | Eckington                            |                            |      | Client:     | MP Adams     |          |  |
| Title:                         | Panel Fabrication — 38 x 140 C16 CLS |                            |      |             |              |          |  |
| Project Number:                | P3                                   |                            |      | Revision:   | C01          |          |  |
| Panel No:                      | GF-IL7                               |                            |      | Drawing No: | P3-MF-GF-IL7 |          |  |
| Panel L×H×T:                   | 2391×2386×149                        |                            |      | Weight:     | 72 kg        |          |  |
| Status:                        | CONSTRUCTION                         |                            |      | Sheet:      | 1 / 1        |          |  |
