



DETAIL 1 - ETFSS HOLDING DOWN STRAP

Engineer's detail reproduced from Skyhooks 26-431-S-0001 P02 (not to scale)

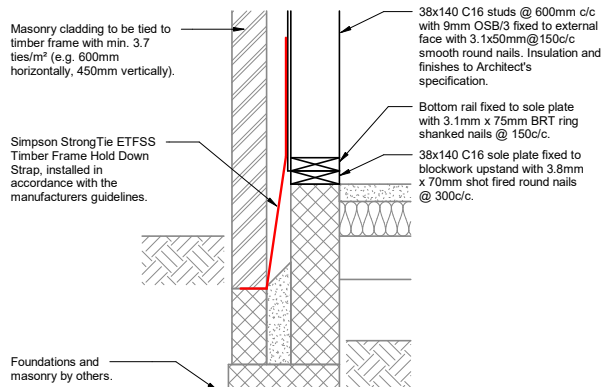

1 Plot 3 - Holding Down Strap Detail
1 : 10

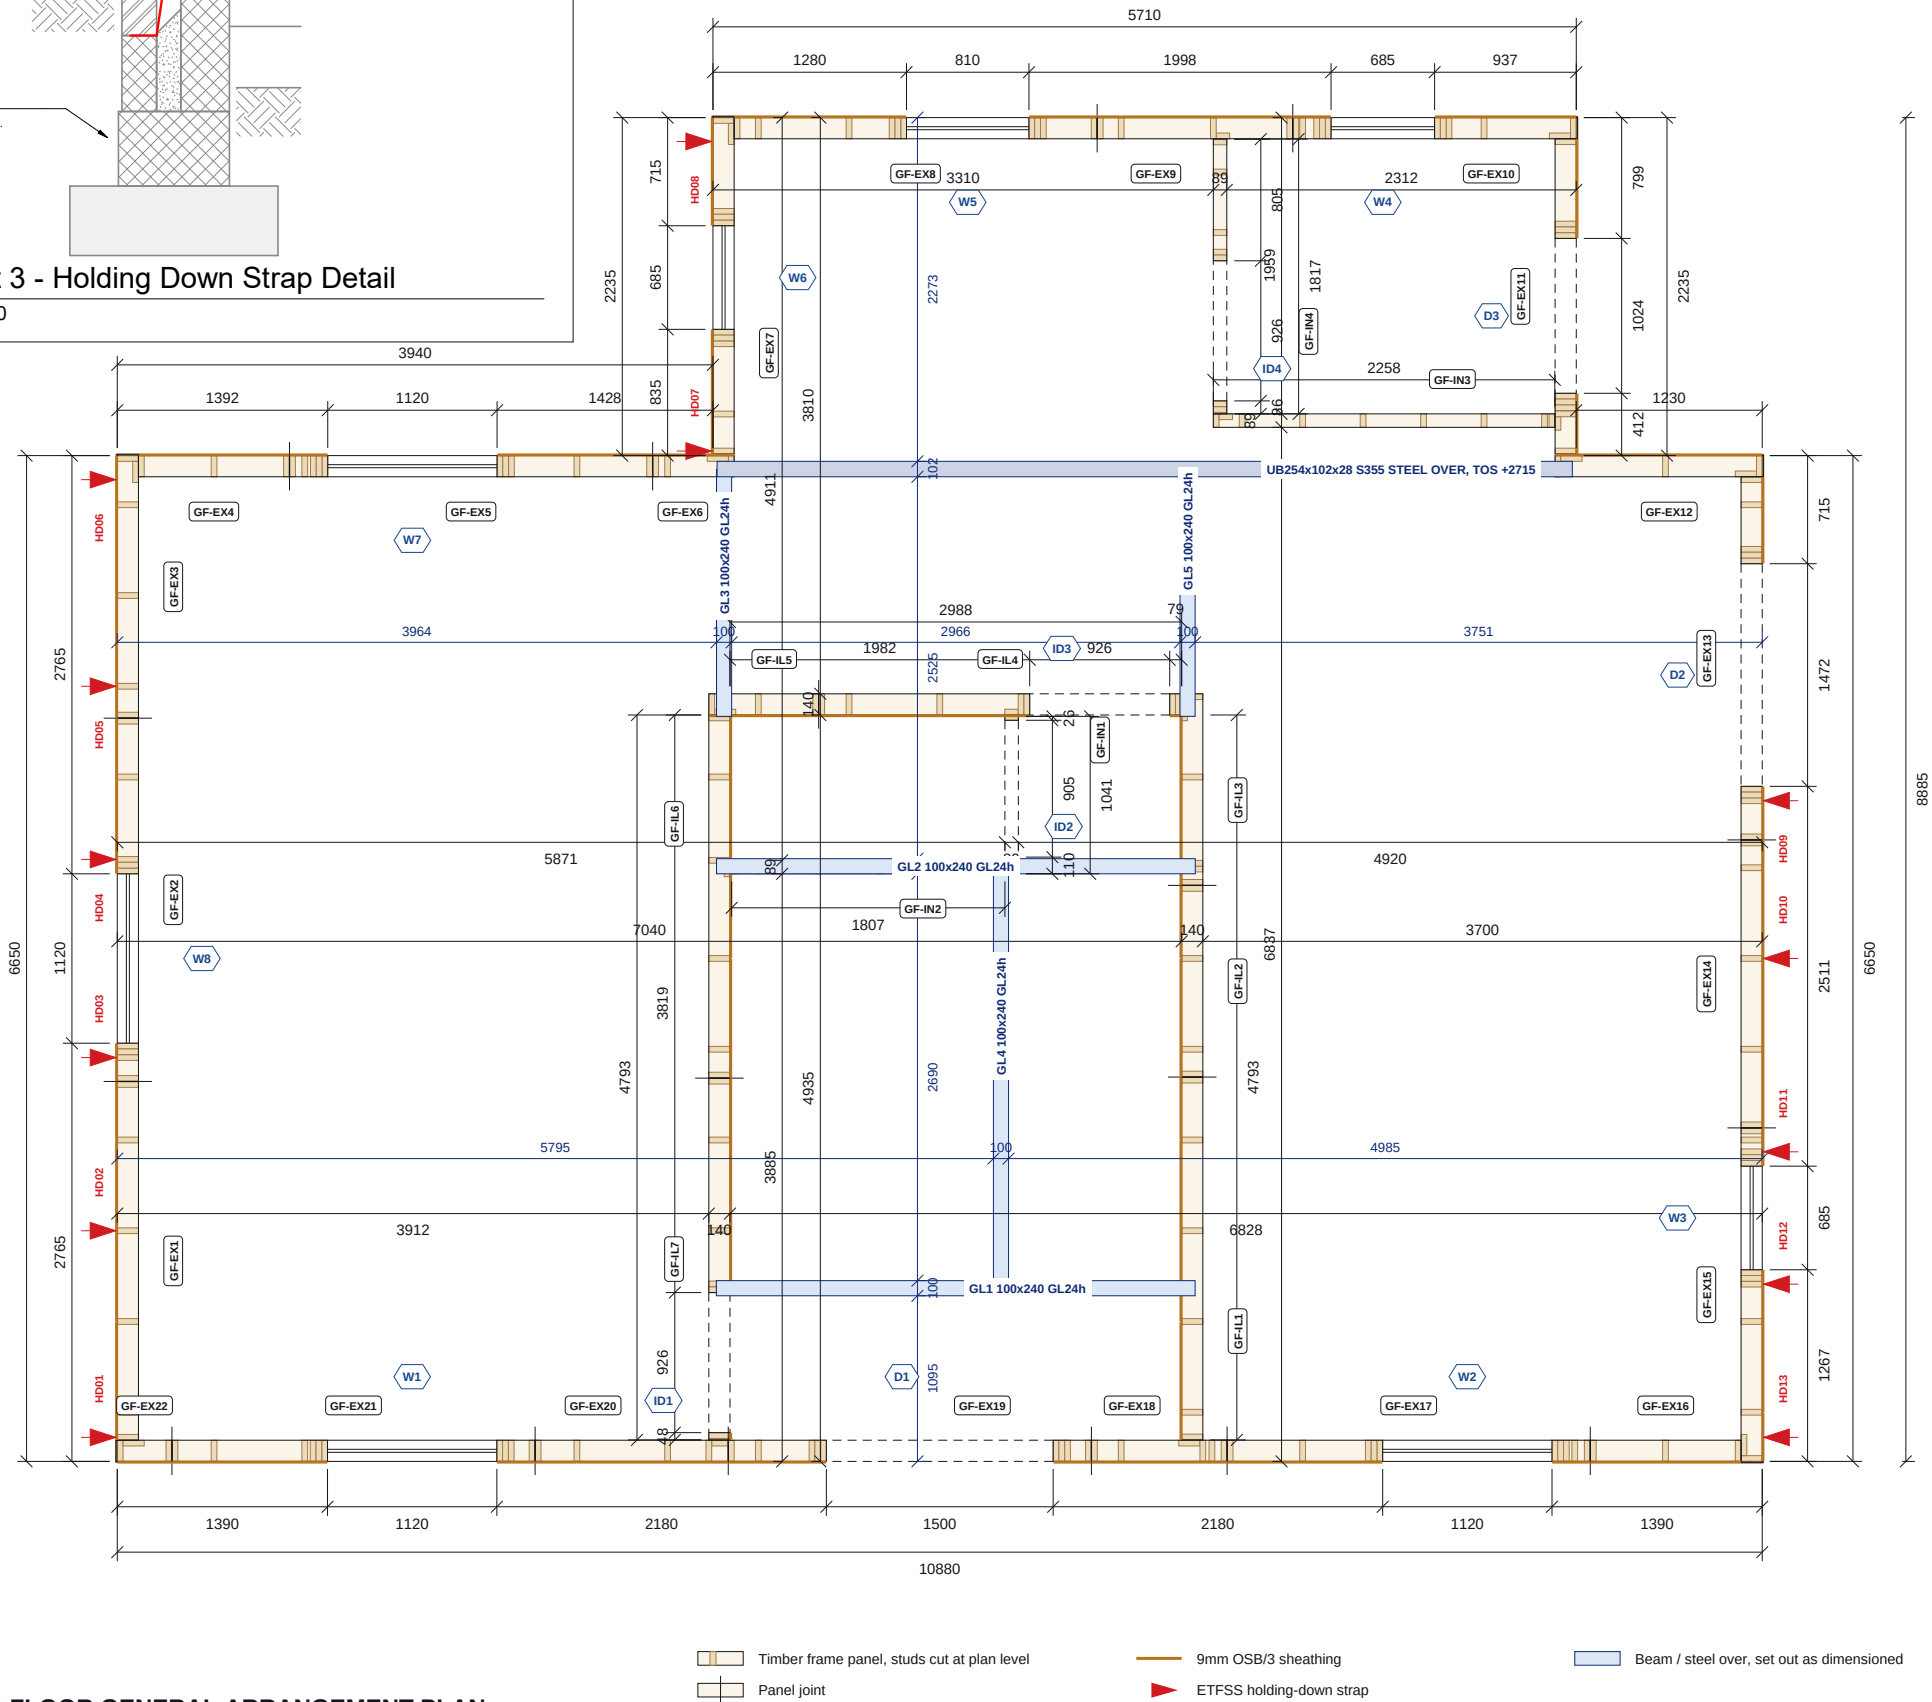

GROUND FLOOR GENERAL ARRANGEMENT PLAN

Scale 1:50 @ A3 | Plan cut at 1200 above slab

- Timber frame panel, studs cut at plan level
- 9mm OSB/3 sheathing
- Beam / steel over, set out as dimensioned
- Panel joint
- ETFSS holding-down strap



GROUND FLOOR SCHEDULES

HEAD BINDER

Section	Pieces	Run m	4.8m lengths
38x140 C16	18	51.7	12

External and load-bearing walls only. Cut-optimised 4.8m stock, 3mm kerf, +5%.

TEMPORARY BRACING (NOT SHOWN)

Item	No.	Order
Brace 4x1 treated rough-sawn, 2.7m	18	10 x 5.4m
Noggin 38x89 C16, 600	18	4 x 4.8m
M7.5x100 concrete screw (2 per noggin)	36	1 box of 100

One brace per panel joint on external / load-bearing walls (18 joints), 2 braces per 5.4m; +5%.

WINDOW BATTENS 38X43

Item	Qty	Order
Battens (head, sill, jambs)	41 / 55.0m	14 x 4.8m 38x43
Ripped from 38x89 C16 4.8m	2 per length	7 x 4.8m 38x89

External openings only. Head/sill = width + 76; jambs = height. Cut-optimised, 3mm kerf, +5%.

HOLDING-DOWN STRAPS (ETFSS)

Mark	Wall	At	On	Mark	Wall	At	On
HD01	W3/0	159	end stud	HD08	W3/2	2077	junction
HD02	W3/0	1525	stud	HD09	W3/6	2282	king D2
HD03	W3/0	2670	king W8	HD10	W3/6	3325	stud
HD04	W3/0	3980	king W8	HD11	W3/6	4603	king W3
HD05	W3/0	5125	stud	HD12	W3/6	5478	king W3
HD06	W3/0	6491	junction	HD13	W3/6	6491	junction
HD07	W3/2	30	end stud				

13 No. Simpson Strong-Tie ETFSS, engineer 26-431-S-0001 Detail 1. 'At' = from the wall's start corner along the external frame face.

OPENING SCHEDULE

Label	Width	Height	Head	Label	Width	Height	Head
W1	1120	1535	2110	D1	1500	2110	2110
W2	1120	1235	2110	D2	1472	2110	2110
W3	685	1385	2110	D3	1024	2110	2110
W4	685	1235	2110	ID1	926	2050	2050
W5	810	1535	2110	ID2	905	2050	2050
W6	685	1385	2110	ID3	926	2050	2050
W7	1120	1235	2110	ID4	926	2050	2050
W8	1120	1535	2110				

Structural opening sizes. W = window, D = external door, ID = internal door. Head level above underside of sole plate.

NOTES

- Panels: 38x140 C16 studs at 600 centres, 9mm OSB/3 to the external face (external and load-bearing walls); 38x89 C16 partitions. Panel marks refer to the manufacture drawings.
- Head binder 38x140 C16 over external and load-bearing walls only; joints staggered from panel joints.
- Temporary bracing (not shown): one 2.7m 4x1 treated brace at every panel joint of external and load-bearing walls, through a 600 38x89 noggin fixed with 2 No. M7.5x100 concrete screws.
- Window battens 38x43 to external openings: head and sill run over the jambs by 38; doors head and jambs.
- ETFSS holding-down straps (red) on the stud scheduled, to engineer's Detail 1 and Simpson guidance.
- Beams and steel over (dark blue) set out as dimensioned; TOS = top of steel above underside of sole plate. Dimensions to timber frame faces. Read with P3-SP-01, P3-FL-01 and engineer's drawing 26-431-S-0001.

REVISIONS

REV	DATE	DESCRIPTION
C01	13.09.26	Construction issue



TLS TIMBER FRAME

Design & Manufacture

Scan: 3D model + drawings

CLIENT

MP Adams

PROJECT

MP Adams Plot 3, Eckington

DRAWING TITLE

GROUND FLOOR GENERAL ARRANGEMENT

Panels, openings, holding-down straps, beams and steel over

SCALE	SIZE	DATE	DRAWN
1:50	A3	13.09.26	TS

STATUS

CONSTRUCTION

DRAWING No.

P3-GA-01

REV

C01
