



Nailing: OSB/Ply racking: 150mm perimeter / 300mm field nails (EC5 §9.2.4, 2:1 panel h:b)

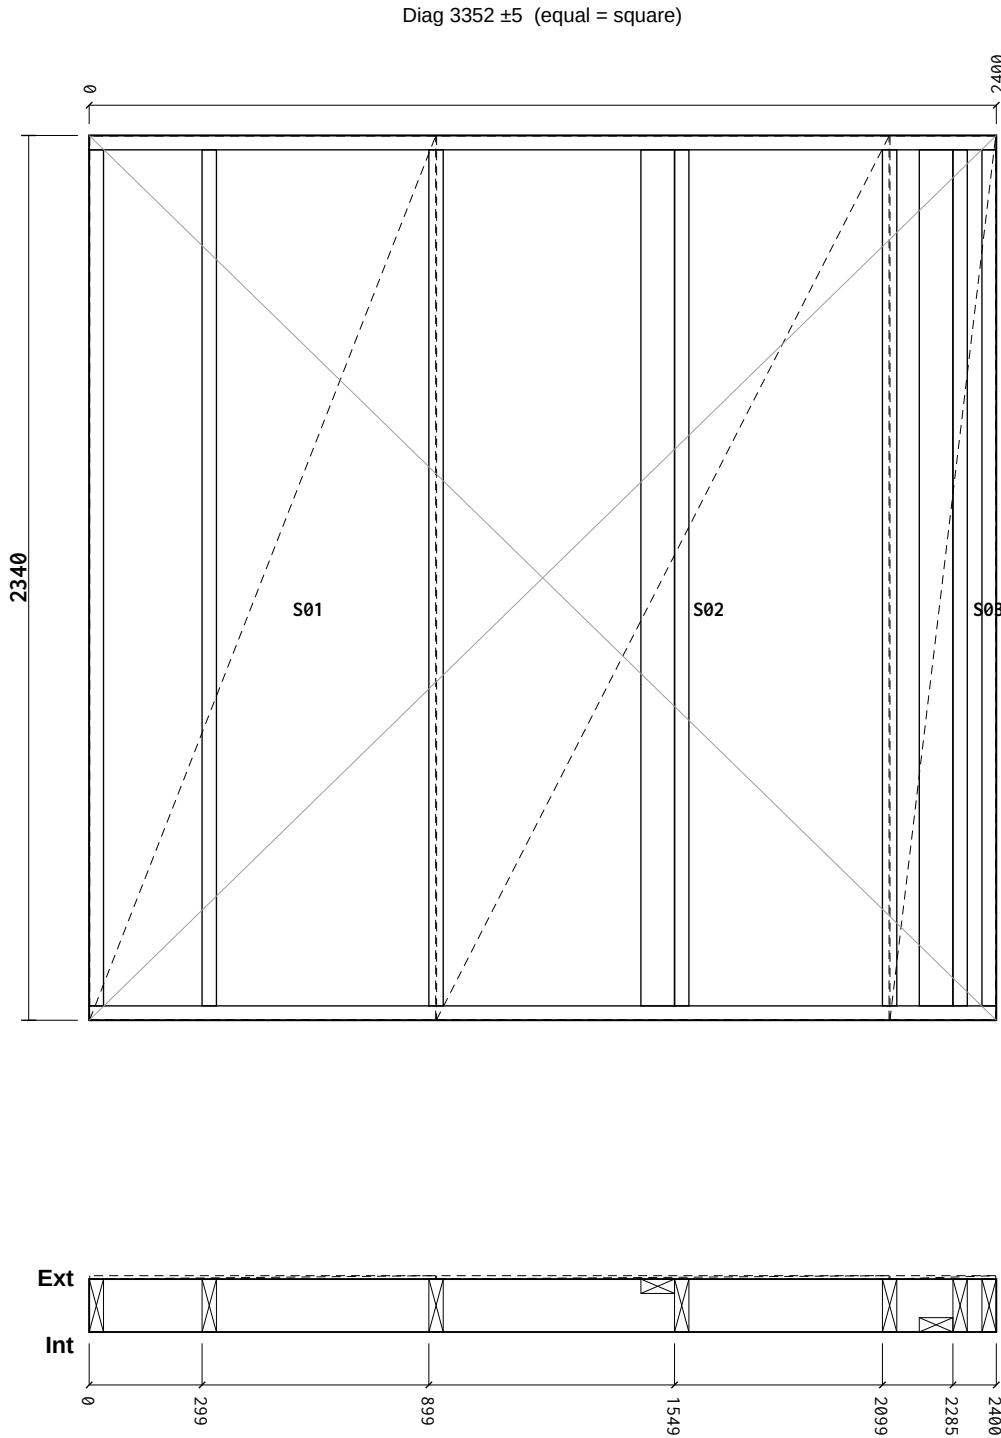

Cut List

Item	Section	Len	Bot°	Top°	Qty
BR1 Bottom Rail	38×140 C16	2400	0	0	1
TR1 Top Rail	38×140 C16	2400	0	0	1
ES1 End Stud	38×140 C16	2264	0	0	1
ES2 End Stud	38×140 C16	2264	0	0	1
VS1 Vertical Stud	38×140 C16	2264	0	0	5
JS1 Junction Stud	38×89 C16	2264	0	0	2
Total: 11 pcs / 25.18 m					

Sheathing & Insulation

Material	W	H	Label
OSB 9mm	915	2337	S01
OSB 9mm	1197	2337	S02
OSB 9mm	280	2337	S03

General Notes:

Frame Nailing:
140mm Frames Nail Using 3no, 3.1×90mm length field galvanised twisted strip nails
90mm Frames Nail Using 2no, 3.1×90mm length field galvanised twisted strip nails


Sheathing Nails:
Components ≤ 100mm should be +/- 1mm
Components > 100mm should be +/- 1.5mm
Stepped check should be +/- 1.5mm
Sloped Opening sizes are +/-2mm

Nailing:
30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.

Manufacturing Tolerances:
Length ±3 · Height ±2 · Diagonals ±5 · Openings 0/+5 (mm).
Do not scale — work to figured dimensions. All dims in mm.



Panel Changes:
When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.

KEY PLAN



Revisions (Rev · Date · Note):		C01 - Construction issue					
Date:	2026-09-13	Scale:	1:20	Drawn:	TS	Checked:	
Project Name:		MP Adams Plot 3, Eckington					
Site:	Eckington			Client:	MP Adams		
Title:	Panel Fabrication — 38 x 140 C16 CLS						
Project Number:	P3			Revision:	C01		
Panel No:	FF-IL1			Drawing No:	P3-MF-FF-IL1		
Panel L×H×T:	2400×2340×149			Weight:	83 kg		
Status:	CONSTRUCTION			Sheet:	1 / 1		

Nailing: OSB/Ply racking: 150mm perimeter / 300mm field nails (EC5 §9.2.4, 2:1 panel h:b)

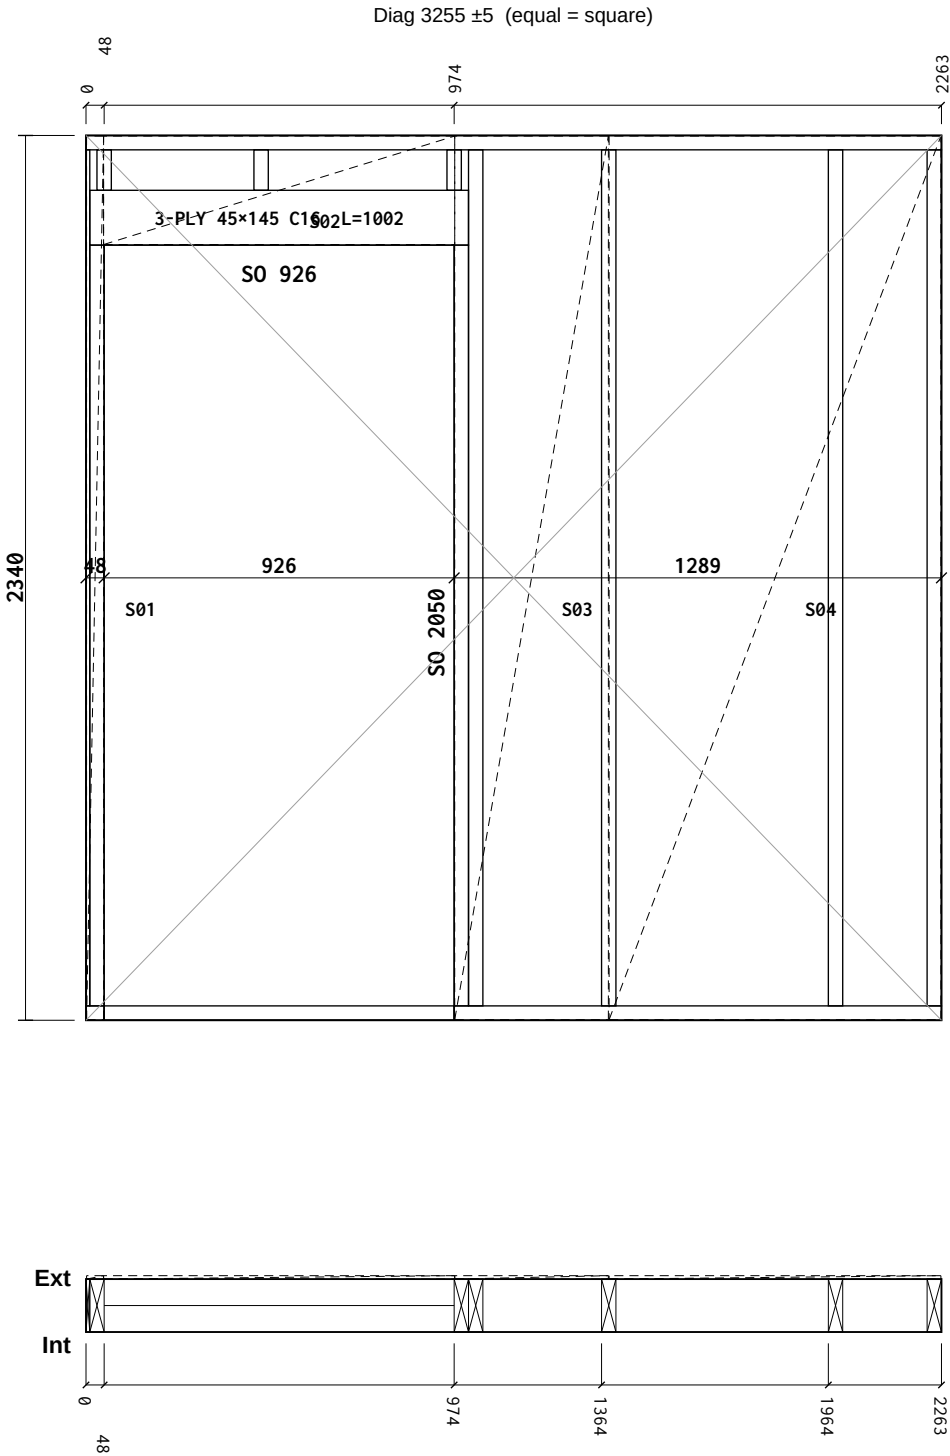

Cut List

Item	Section	Len	Bot°	Top°	Qty
BR1 Bottom Rail	38×140 C16	1289	0	0	1
BR2 Bottom Rail	38×140 C16	926	0	0	1
BR3 Bottom Rail	38×140 C16	48	0	0	1
TR1 Top Rail	38×140 C16	2263	0	0	1
ES1 End Stud	38×140 C16	107	0	0	1
ES2 End Stud	38×140 C16	2264	0	0	1
KS1 Vertical Stud	38×140 C16	2264	0	0	1
KS2 Vertical Stud	10×140 C16	2264	0	0	1
CS1 Cripple Stud	38×140 C16	2012	0	0	2
LP1 Lintel Ply	1002×45 C16	1002	0	0	3
OS1 OSB Support	38×140 C16	107	0	0	2
VS1 Vertical Stud	38×140 C16	2264	0	0	2
Total: 17 pcs / 23.20 m					

Sheathing & Insulation

Material	W	H	Label
OSB 9mm	45	2337	S01
OSB 9mm	929	287	S02
OSB 9mm	406	2337	S03
OSB 9mm	878	2337	S04

General Notes:

Frame Nailing:
140mm Frames Nail Using 3no, 3.1×90mm length field galvanised twisted strip nails
90mm Frames Nail Using 2no, 3.1×90mm length field galvanised twisted strip nails


Sheathing Nails:
Components ≤ 100mm should be +/- 1mm
Components > 100mm should be +/- 1.5mm
Stepped check should be +/- 1.5mm
Sloped Opening sizes are +/-2mm

Nailing:
30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.

Manufacturing Tolerances:
Length ±3 · Height ±2 · Diagonals ±5 · Openings 0/+5 (mm).
Do not scale — work to figured dimensions. All dims in mm.

Panel Changes:
When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.

KEY PLAN



Revisions (Rev · Date · Note):

C01 - Construction issue

Date:	2026-09-13	Scale:	1:20	Drawn:	TS	Checked:	
Project Name:		MP Adams Plot 3, Eckington					
Site:	Eckington			Client:	MP Adams		
Title:	Panel Fabrication — 38 x 140 C16 CLS						
Project Number:	P3			Revision:	C01		
Panel No:	FF-IL2			Drawing No:	P3-MF-FF-IL2		
Panel L×H×T:	2263×2340×149			Weight:	68 kg		
Status:	CONSTRUCTION			Sheet:	1 / 1		
