




Nailing: OSB/Ply racking: 150mm perimeter / 300mm field nails (EC5 §9.2.4, 2:1 panel h:b)

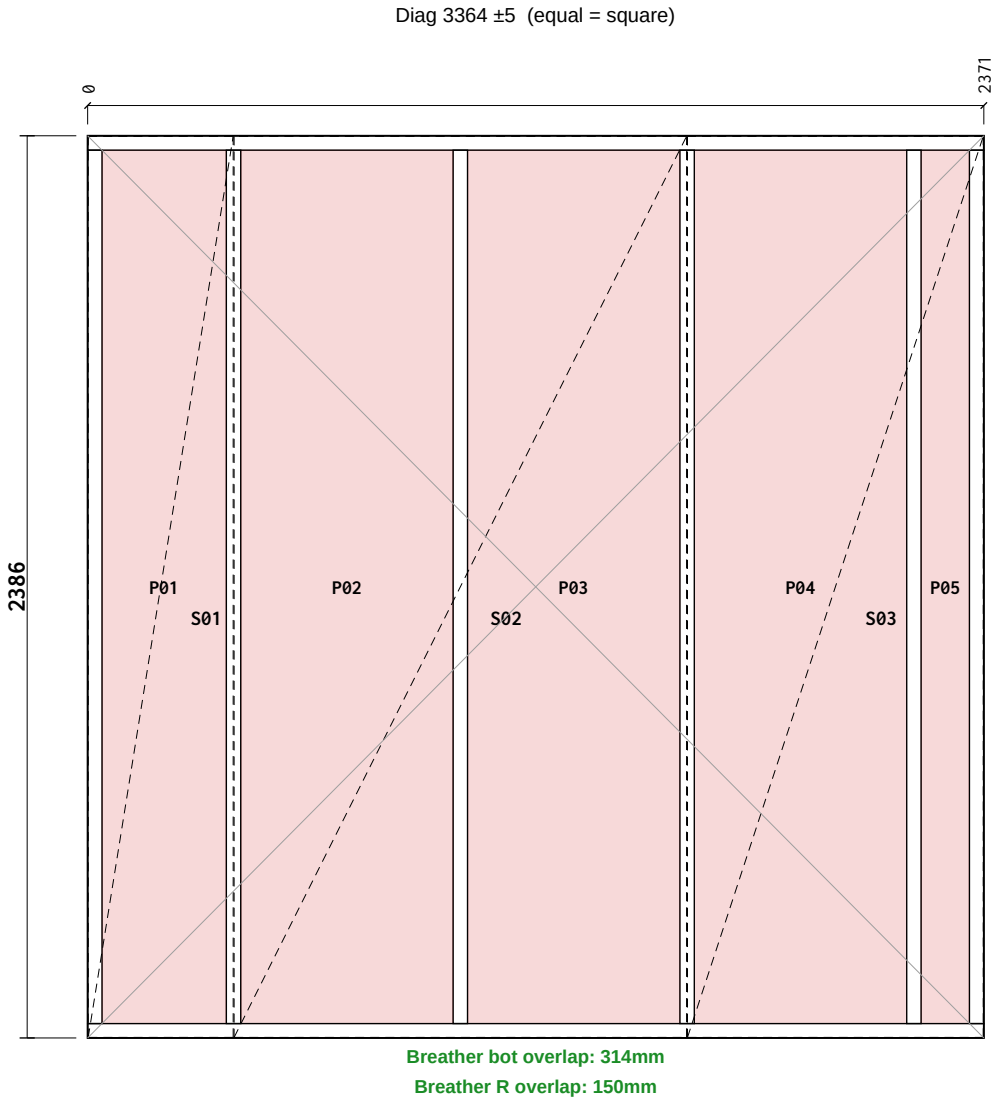

Cut List

Item	Section	Len	Bot°	Top°	Qty
BR1 Bottom Rail	38×140 C16	2371	0	0	1
TR1 Top Rail	38×140 C16	2371	0	0	1
ES1 End Stud	38×140 C16	2310	0	0	1
ES2 End Stud	38×140 C16	2310	0	0	1
VS1 Vertical Stud	38×140 C16	2310	0	0	4
Total: 8 pcs / 18.60 m					

Sheathing & Insulation

Material	W	H	Label
OSB 9mm	384	2383	S01
OSB 9mm	1197	2383	S02
OSB 9mm	782	2383	S03
PIR 120mm	328	2310	P01
PIR 120mm	561	2310	P02
PIR 120mm	561	2310	P03
PIR 120mm	561	2310	P04
PIR 120mm	127	2310	P05

General Notes:

Frame Nailing:
140mm Frames Nail Using 3no, 3.1×90mm length field galvanised twisted strip nails
90mm Frames Nail Using 2no, 3.1×90mm length field galvanised twisted strip nails

Sheathing Nails:
Components ≤ 100mm should be +/- 1mm
Components > 100mm should be +/- 1.5mm
Stepped check should be +/- 1.5mm
Sloped Opening sizes are +/-2mm


Nailing:
30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.

Manufacturing Tolerances:
Length ±3 · Height ±2 · Diagonals ±5 · Openings 0/+5 (mm).
Do not scale — work to figured dimensions. All dims in mm.

Breather Membrane:
Laps 100mm horizontal / 150mm vertical, upper lapping lower.

Panel Changes:
When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.

KEY PLAN






Revisions (Rev · Date · Note):

C01 - Construction issue

Date:	2026-09-13	Scale:	1:20	Drawn:	TS	Checked:	
Project Name:		MP Adams Plot 3, Eckington					
Site:		Eckington		Client:		MP Adams	
Title:		Panel Fabrication — 38 x 140 C16 CLS					
Project Number:		P3		Revision:		C01	
Panel No:		GF-EX1		Drawing No:		P3-MF-GF-EX1	
Panel L×H×T:		2371×2386×149		Weight:		93 kg	
Status:		CONSTRUCTION		Sheet:		1 / 1	

Nailing: OSB/Ply racking: 150mm perimeter / 300mm field nails (EC5 §9.2.4, 2:1 panel h:b)

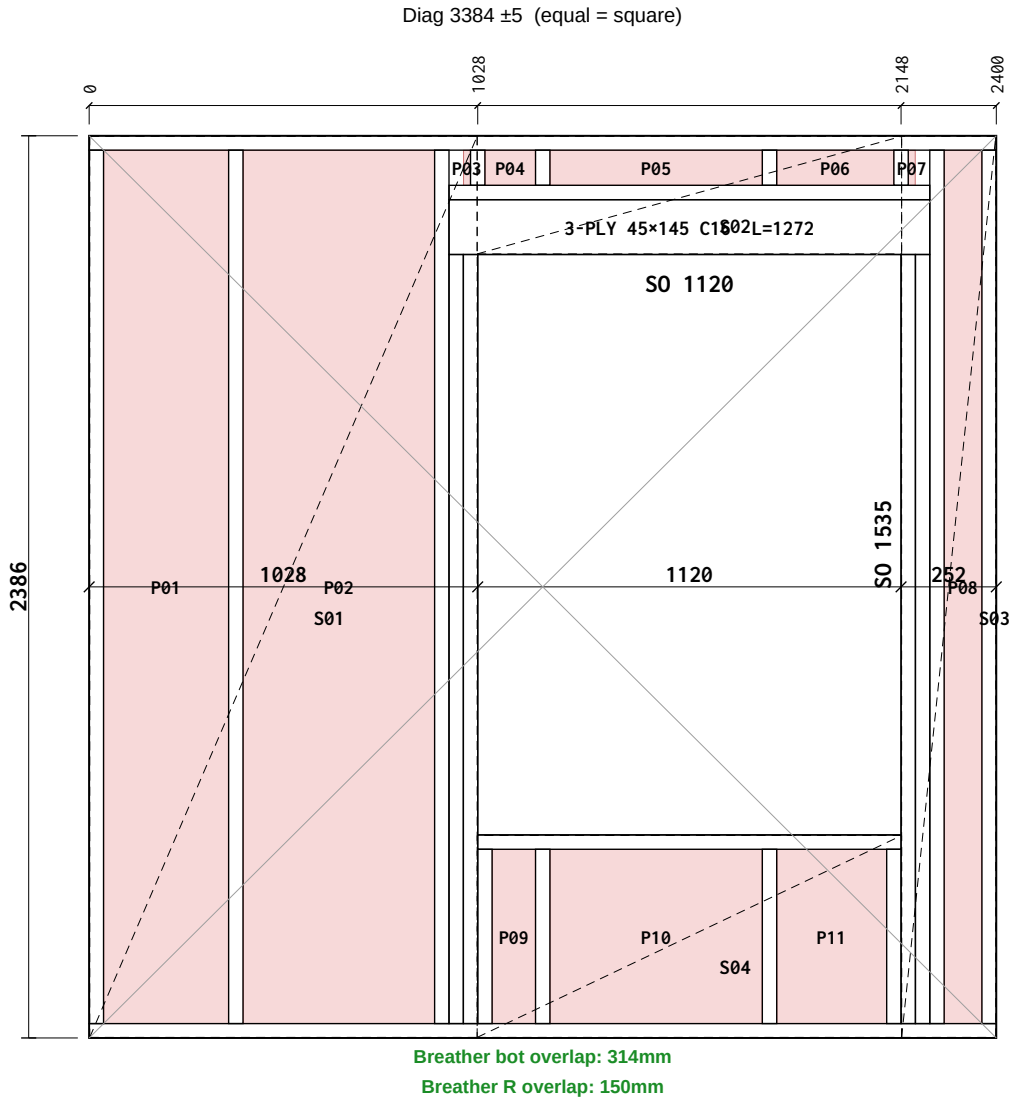

Cut List

Item	Section	Len	Bot°	Top°	Qty
BR1 Bottom Rail	38×140 C16	2400	0	0	1
TR1 Top Rail	38×140 C16	2400	0	0	1
TR2 Top Rail	38×140 C16	1272	0	0	1
ES1 End Stud	38×140 C16	2310	0	0	1
ES2 End Stud	38×140 C16	2310	0	0	1
KS1 Vertical Stud	38×140 C16	2310	0	0	2
CS1 Cripple Stud	38×140 C16	2034	0	0	4
SP1 Sill Plate	38×140 C16	1120	0	0	1
LP1 Lintel Ply	1272×45 C16	1272	0	0	3
SS1 Sill Support	38×140 C16	461	0	0	2
OS1 OSB Support	38×140 C16	93	0	0	2
VS1 Vertical Stud	38×140 C16	2310	0	0	1
VS2 Vertical Stud	38×140 C16	461	0	0	2
VS3 Vertical Stud	38×140 C16	93	0	0	2

Total: 24 pcs / 32.91 m

Sheathing & Insulation

Material	W	H	Label
OSB 9mm	1025	2383	S01
OSB 9mm	1123	311	S02
OSB 9mm	249	2383	S03
OSB 9mm	1123	534	S04
PIR 120mm	330	2310	P01
PIR 120mm	505	2310	P02
PIR 120mm	18	93	P03
PIR 120mm	133	93	P04
PIR 120mm	561	93	P05
PIR 120mm	309	93	P06
PIR 120mm	18	93	P07
PIR 120mm	99	2310	P08
PIR 120mm	114	460	P09
PIR 120mm	561	460	P10
PIR 120mm	290	460	P11

General Notes:

Frame Nailing:
140mm Frames Nail Using 3no, 3.1×90mm length field galvanised twisted strip nails
90mm Frames Nail Using 2no, 3.1×90mm length field galvanised twisted strip nails

Sheathing Nails:
Components ≤ 100mm should be +/- 1mm
Components > 100mm should be +/- 1.5mm
Stepped check should be +/- 1.5mm
Sloped Opening sizes are +/-2mm


Nailing:
30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.

Manufacturing Tolerances:
Length ±3 · Height ±2 · Diagonals ±5 · Openings 0/+5 (mm).
Do not scale — work to figured dimensions. All dims in mm.

Breather Membrane:
Laps 100mm horizontal / 150mm vertical, upper lapping lower.

Panel Changes:
When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.

KEY PLAN



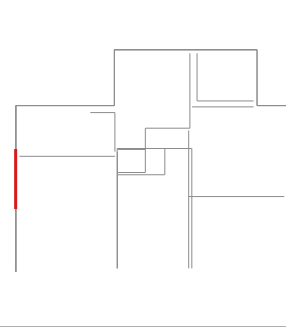


Revisions (Rev · Date · Note):

C01 - Construction issue

Date:	2026-09-13	Scale:	1:20	Drawn:	TS	Checked:	
Project Name:		MP Adams Plot 3, Eckington					
Site:	Eckington			Client:	MP Adams		
Title:	Panel Fabrication — 38 x 140 C16 CLS						
Project Number:	P3			Revision:	C01		
Panel No:	GF-EX2			Drawing No:	P3-MF-GF-EX2		
Panel L×H×T:	2400×2386×149			Weight:	109 kg		
Status:	CONSTRUCTION			Sheet:	1 / 1		

Nailing: OSB/Ply racking: 150mm perimeter / 300mm field nails (EC5 §9.2.4, 2:1 panel h:b)

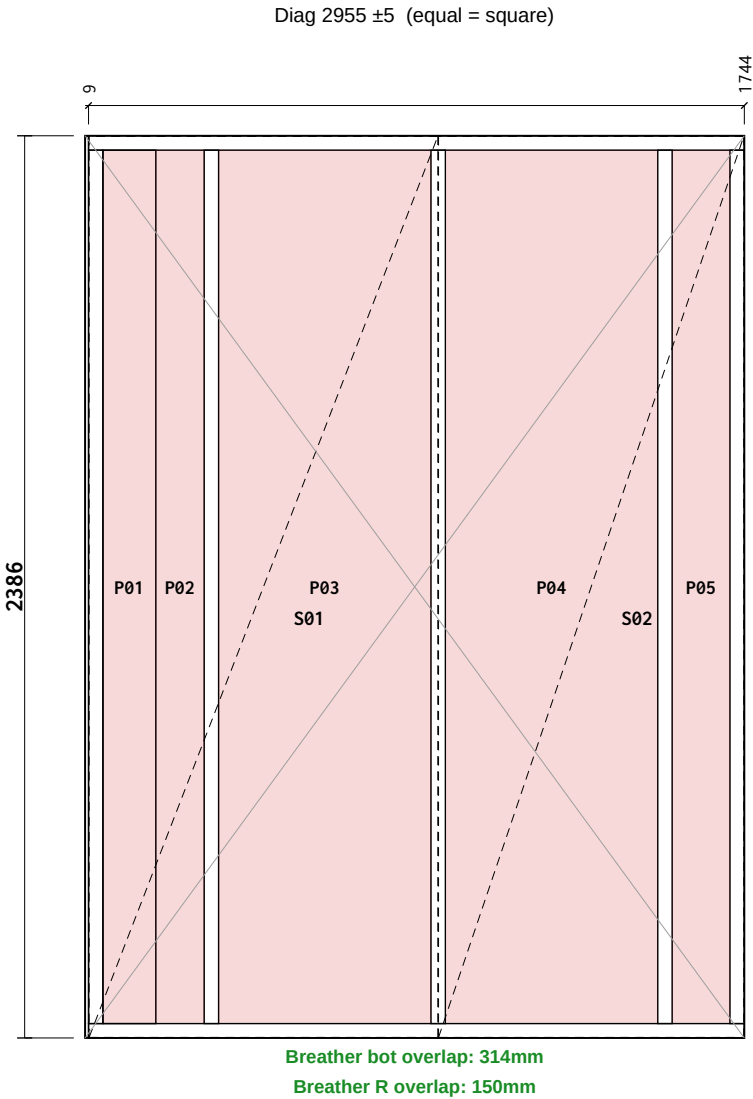

Cut List

Item	Section	Len	Bot°	Top°	Qty
BR1 Bottom Rail	38×140 C16	1735	0	0	1
TR1 Top Rail	38×140 C16	1735	0	0	1
ES1 End Stud	38×140 C16	2310	0	0	1
ES2 End Stud	38×140 C16	2310	0	0	1
VS1 Vertical Stud	38×140 C16	2310	0	0	3
JS1 Junction Stud	38×140 C16	2310	0	0	1
Total: 8 pcs / 17.33 m					

Sheathing & Insulation

Material	W	HLabel
OSB 9mm	923	2383 S01
OSB 9mm	807	2383 S02
PIR 100mm	140	2310 P01
PIR 120mm	128	2310 P02
PIR 120mm	561	2310 P03
PIR 120mm	561	2310 P04
PIR 120mm	152	2310 P05
OSB End Cap 9mm	146	2383 E01

General Notes:

Frame Nailing:
140mm Frames Nail Using 3no, 3.1×90mm length field galvanised twisted strip nails
90mm Frames Nail Using 2no, 3.1×90mm length field galvanised twisted strip nails

Sheathing Nails:
Components ≤ 100mm should be +/- 1mm
Components > 100mm should be +/- 1.5mm
Stepped check should be +/- 1.5mm
Sloped Opening sizes are +/-2mm


Nailing:
30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.

Manufacturing Tolerances:
Length ±3 · Height ±2 · Diagonals ±5 · Openings 0/+5 (mm).
Do not scale — work to figured dimensions. All dims in mm.

Breather Membrane:
Laps 100mm horizontal / 150mm vertical, upper lapping lower.




Panel Changes:
When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.

KEY PLAN



Revisions (Rev · Date · Note):		C01 - Construction issue					
Date:	2026-09-13	Scale:	1:20	Drawn:	TS	Checked:	
Project Name:		MP Adams Plot 3, Eckington					
Site:	Eckington			Client:	MP Adams		
Title:	Panel Fabrication — 38 x 140 C16 CLS						
Project Number:	P3			Revision:	C01		
Panel No:	GF-EX3			Drawing No:	P3-MF-GF-EX3		
Panel L×H×T:	1744×2386×149			Weight:	78 kg		
Status:	CONSTRUCTION			Sheet:	1 / 1		

Nailing: OSB/Ply racking: 150mm perimeter / 300mm field nails (EC5 §9.2.4, 2:1 panel h:b)

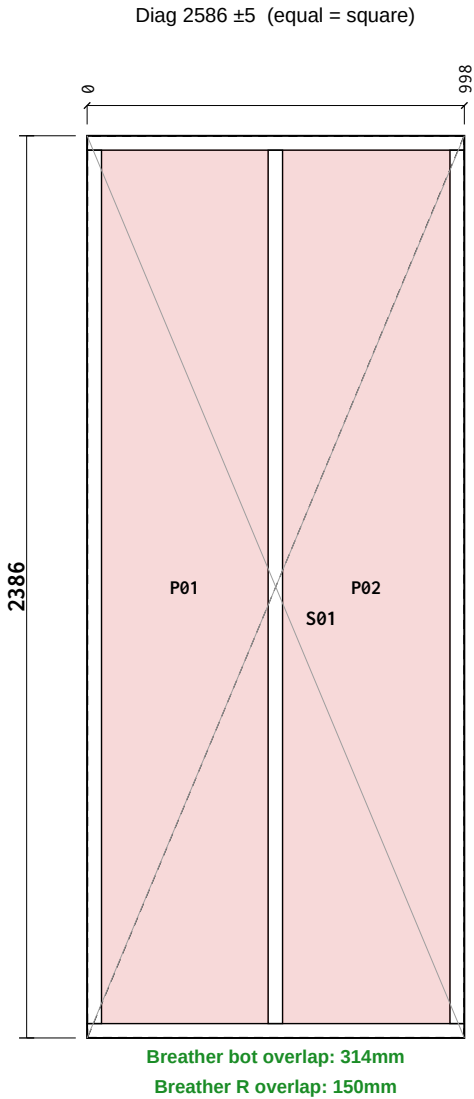

Cut List

Item	Section	Len	Bot°	Top°	Qty
BR1 Bottom Rail	38×140 C16	998	0	0	1
TR1 Top Rail	38×140 C16	998	0	0	1
ES1 End Stud	38×140 C16	2310	0	0	1
ES2 End Stud	38×140 C16	2310	0	0	1
VS1 Vertical Stud	38×140 C16	2310	0	0	1
Total: 5 pcs / 8.93 m					

Sheathing & Insulation

Material	W	H	Label
OSB 9mm	995	2383	S01
PIR 120mm	440	2310	P01
PIR 120mm	442	2310	P02

General Notes:

Frame Nailing:
140mm Frames Nail Using 3no, 3.1×90mm length field galvanised twisted strip nails
90mm Frames Nail Using 2no, 3.1×90mm length field galvanised twisted strip nails

Sheathing Nails:
Components ≤ 100mm should be +/- 1mm
Components > 100mm should be +/- 1.5mm
Stepped check should be +/- 1.5mm
Sloped Opening sizes are +/-2mm


Nailing:
30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.

Manufacturing Tolerances:
Length ±3 · Height ±2 · Diagonals ±5 · Openings 0/+5 (mm).
Do not scale — work to figured dimensions. All dims in mm.

Breather Membrane:
Laps 100mm horizontal / 150mm vertical, upper lapping lower.




Panel Changes:
When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.

KEY PLAN



Revisions (Rev · Date · Note):		C01 - Construction issue					
Date:	2026-09-13	Scale:	1:20	Drawn:	TS	Checked:	
Project Name:		MP Adams Plot 3, Eckington					
Site:	Eckington			Client:	MP Adams		
Title:	Panel Fabrication — 38 x 140 C16 CLS						
Project Number:	P3			Revision:	C01		
Panel No:	GF-EX4			Drawing No:	P3-MF-GF-EX4		
Panel L×H×T:	998×2386×149			Weight:	42 kg		
Status:	CONSTRUCTION			Sheet:	1 / 1		

Nailing: OSB/Ply racking: 150mm perimeter / 300mm field nails (EC5 §9.2.4, 2:1 panel h:b)

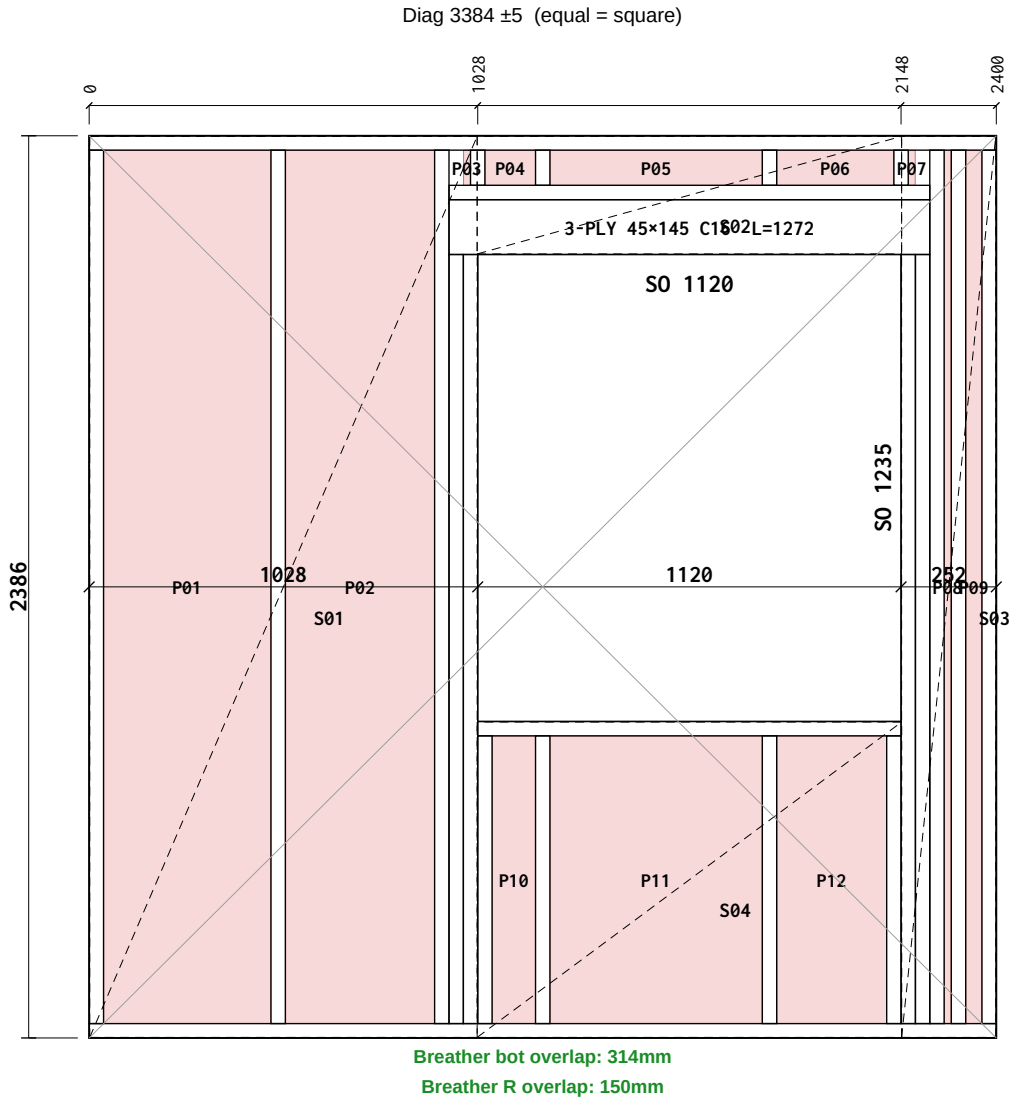

Cut List

Item	Section	Len	Bot°	Top°	Qty
BR1 Bottom Rail	38×140 C16	2400	0	0	1
TR1 Top Rail	38×140 C16	2400	0	0	1
TR2 Top Rail	38×140 C16	1272	0	0	1
ES1 End Stud	38×140 C16	2310	0	0	1
ES2 End Stud	38×140 C16	2310	0	0	1
KS1 Vertical Stud	38×140 C16	2310	0	0	2
CS1 Cripple Stud	38×140 C16	2034	0	0	4
SP1 Sill Plate	38×140 C16	1120	0	0	1
LP1 Lintel Ply	1272×45 C16	1272	0	0	3
SS1 Sill Support	38×140 C16	761	0	0	2
OS1 OSB Support	38×140 C16	93	0	0	2
VS1 Vertical Stud	38×140 C16	2310	0	0	2
VS2 Vertical Stud	38×140 C16	761	0	0	2
VS3 Vertical Stud	38×140 C16	93	0	0	2

Total: 25 pcs / 36.42 m

Sheathing & Insulation

Material	W	H	Label
OSB 9mm	1025	2383	S01
OSB 9mm	1123	311	S02
OSB 9mm	249	2383	S03
OSB 9mm	1123	834	S04
PIR 120mm	442	2310	P01
PIR 120mm	394	2310	P02
PIR 120mm	18	93	P03
PIR 120mm	133	93	P04
PIR 120mm	561	93	P05
PIR 120mm	309	93	P06
PIR 120mm	18	93	P07
PIR 120mm	17	2310	P08
PIR 120mm	42	2310	P09
PIR 120mm	114	760	P10
PIR 120mm	561	760	P11
PIR 120mm	290	760	P12

General Notes:

Frame Nailing:
140mm Frames Nail Using 3no, 3.1×90mm length field galvanised twisted strip nails
90mm Frames Nail Using 2no, 3.1×90mm length field galvanised twisted strip nails

Sheathing Nails:
Components ≤ 100mm should be +/- 1mm
Components > 100mm should be +/- 1.5mm
Stepped check should be +/- 1.5mm
Sloped Opening sizes are +/-2mm


Nailing:
30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.

Manufacturing Tolerances:
Length ±3 · Height ±2 · Diagonals ±5 · Openings 0/+5 (mm).
Do not scale — work to figured dimensions. All dims in mm.

Breather Membrane:
Laps 100mm horizontal / 150mm vertical, upper lapping lower.

Panel Changes:
When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.

KEY PLAN

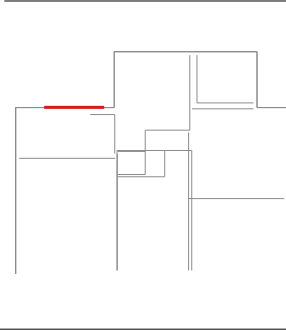



Revisions (Rev · Date · Note):

C01 - Construction issue


Date:	2026-09-13	Scale:	1:20	Drawn:	TS	Checked:	
Project Name:		MP Adams Plot 3, Eckington					
Site:	Eckington			Client:	MP Adams		
Title:		Panel Fabrication — 38 x 140 C16 CLS					
Project Number:		P3		Revision:	C01		
Panel No:		GF-EX5		Drawing No:	P3-MF-GF-EX5		
Panel L×H×T:		2400×2386×149		Weight:	119 kg		
Status:		CONSTRUCTION		Sheet:	1 / 1		

Nailing: OSB/Ply racking: 150mm perimeter / 300mm field nails (EC5 §9.2.4, 2:1 panel h:b)

Diag 2446 ±5 (equal = square)

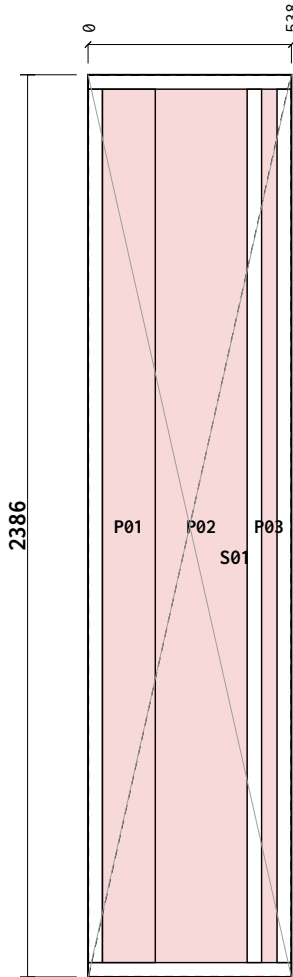

Section A-A



Cut List

Item	Section	Len	Bot°	Top°	Qty
BR1 Bottom Rail	38×140 C16	538	0	0	1
TR1 Top Rail	38×140 C16	538	0	0	1
ES1 End Stud	38×140 C16	2310	0	0	1
ES2 End Stud	38×140 C16	2310	0	0	1
VS1 Vertical Stud	38×140 C16	2310	0	0	1
JS1 Junction Stud	38×140 C16	2310	0	0	1
Total: 6 pcs / 10.32 m					

Sheathing & Insulation

Material	W	H	Label
OSB 9mm	535	2383	S01
PIR 100mm	140	2310	P01
PIR 120mm	242	2310	P02
PIR 120mm	40	2310	P03

General Notes:

Frame Nailing:
140mm Frames Nail Using 3no, 3.1×90mm length field galvanised twisted strip nails
90mm Frames Nail Using 2no, 3.1×90mm length field galvanised twisted strip nails

Sheathing Nails:
Components ≤ 100mm should be +/- 1mm
Components > 100mm should be +/- 1.5mm
Stepped check should be +/- 1.5mm
Sloped Opening sizes are +/-2mm


Nailing:
30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.

Manufacturing Tolerances:
Length ±3 · Height ±2 · Diagonals ±5 · Openings 0/+5 (mm).
Do not scale — work to figured dimensions. All dims in mm.

Breather Membrane:
Laps 100mm horizontal / 150mm vertical, upper lapping lower.

Panel Changes:
When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.

KEY PLAN






Revisions (Rev · Date · Note):

C01 - Construction issue

Date:	2026-09-13	Scale:	1:20	Drawn:	TS	Checked:	
Project Name:		MP Adams Plot 3, Eckington					
Site:	Eckington			Client:	MP Adams		
Title:	Panel Fabrication — 38 x 140 C16 CLS						
Project Number:	P3			Revision:	C01		
Panel No:	GF-EX6			Drawing No:	P3-MF-GF-EX6		
Panel L×H×T:	538×2386×149			Weight:	34 kg		
Status:	CONSTRUCTION			Sheet:	1 / 1		

Nailing: OSB/Ply racking: 150mm perimeter / 300mm field nails (EC5 §9.2.4, 2:1 panel h:b)

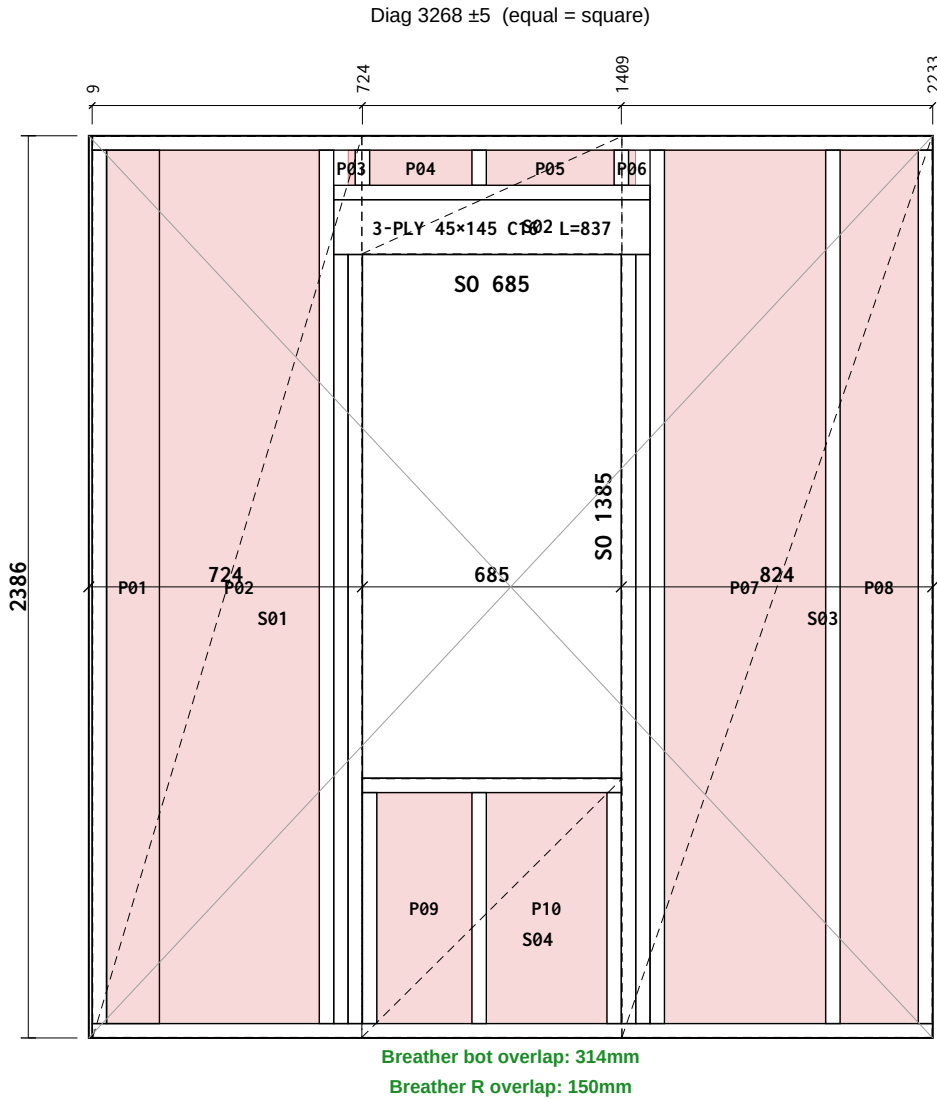

Cut List

Item	Section	Len	Bot°	Top°	Qty
BR1 Bottom Rail	38×140 C16	2224	0	0	1
TR1 Top Rail	38×140 C16	2224	0	0	1
TR2 Top Rail	38×140 C16	837	0	0	1
ES1 End Stud	38×140 C16	2310	0	0	1
ES2 End Stud	38×140 C16	2310	0	0	1
KS1 Vertical Stud	38×140 C16	2310	0	0	2
CS1 Cripple Stud	38×140 C16	2034	0	0	4
SP1 Sill Plate	38×140 C16	685	0	0	1
LP1 Lintel Ply	837×45 C16	837	0	0	3
SS1 Sill Support	38×140 C16	611	0	0	2
OS1 OSB Support	38×140 C16	93	0	0	2
VS1 Vertical Stud	38×140 C16	2310	0	0	1
VS2 Vertical Stud	38×140 C16	611	0	0	1
VS3 Vertical Stud	38×140 C16	93	0	0	1
JS1 Junction Stud	38×140 C16	2310	0	0	1

Total: 23 pcs / 32.59 m

Sheathing & Insulation

Material	W	H	Label
OSB 9mm	712	2383	S01
OSB 9mm	688	311	S02
OSB 9mm	821	2383	S03
OSB 9mm	688	684	S04
PIR 100mm	139	2310	P01
PIR 120mm	422	2310	P02
PIR 120mm	18	93	P03
PIR 120mm	270	93	P04
PIR 120mm	337	93	P05
PIR 120mm	18	93	P06
PIR 120mm	425	2310	P07
PIR 120mm	206	2310	P08
PIR 120mm	251	610	P09
PIR 120mm	318	610	P10
OSB End Cap 9mm	146	2383	E01

General Notes:

Frame Nailing:
140mm Frames Nail Using 3no, 3.1×90mm length field galvanised twisted strip nails
90mm Frames Nail Using 2no, 3.1×90mm length field galvanised twisted strip nails

Sheathing Nails:
Components ≤ 100mm should be +/- 1mm
Components > 100mm should be +/- 1.5mm
Stepped check should be +/- 1.5mm
Sloped Opening sizes are +/-2mm


Nailing:
30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.

Manufacturing Tolerances:
Length ±3 · Height ±2 · Diagonals ±5 · Openings 0/+5 (mm).
Do not scale — work to figured dimensions. All dims in mm.

Breather Membrane:
Laps 100mm horizontal / 150mm vertical, upper lapping lower.

Panel Changes:
When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.

KEY PLAN






Revisions (Rev · Date · Note):

C01 - Construction issue

Date:	2026-09-13	Scale:	1:20	Drawn:	TS	Checked:	
Project Name:		MP Adams Plot 3, Eckington					
Site:		Eckington		Client:		MP Adams	
Title:		Panel Fabrication — 38 x 140 C16 CLS					
Project Number:		P3		Revision:		C01	
Panel No:		GF-EX7		Drawing No:		P3-MF-GF-EX7	
Panel L×H×T:		2233×2386×149		Weight:		113 kg	
Status:		CONSTRUCTION		Sheet:		1 / 1	

Nailing: OSB/Ply racking: 150mm perimeter / 300mm field nails (EC5 §9.2.4, 2:1 panel h:b)

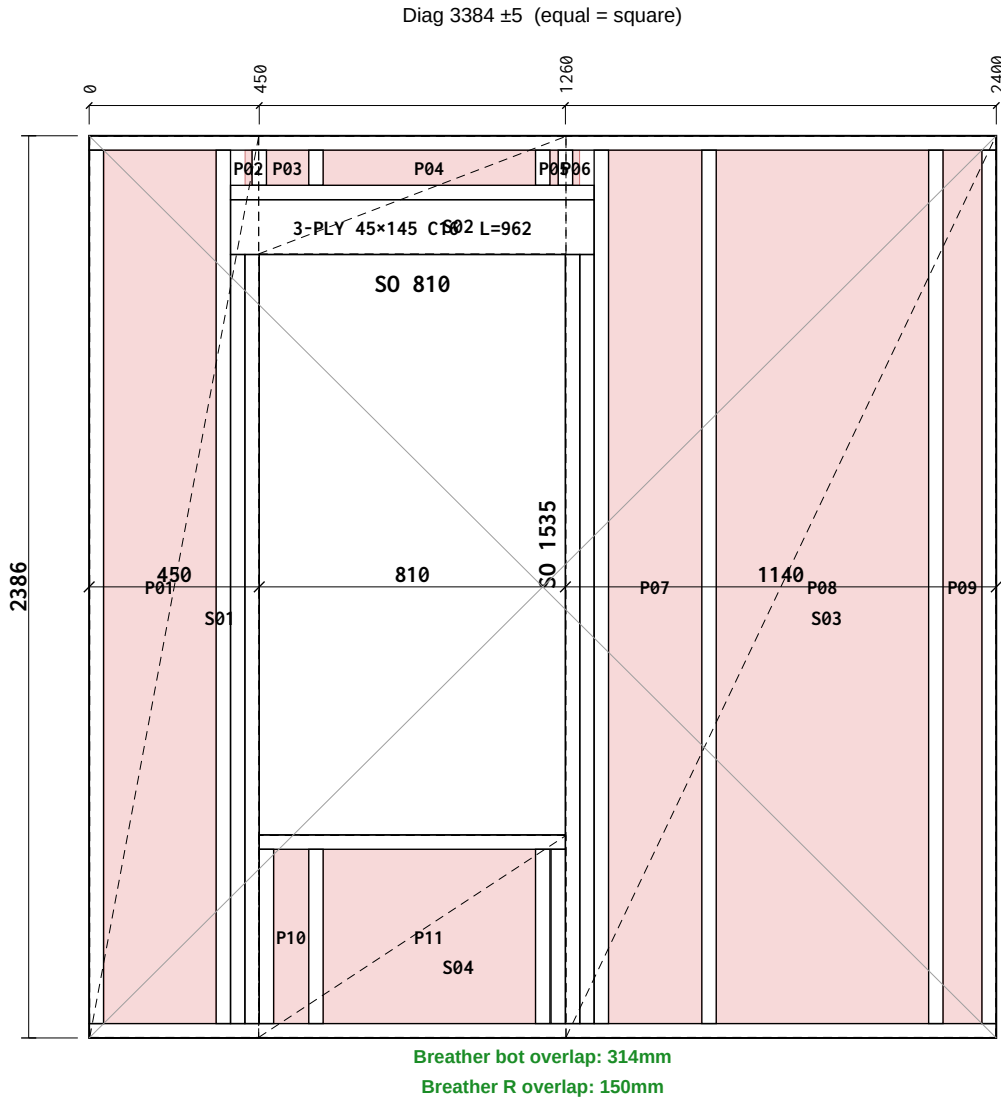

Cut List

Item	Section	Len	Bot°	Top°	Qty
BR1 Bottom Rail	38×140 C16	2400	0	0	1
TR1 Top Rail	38×140 C16	2400	0	0	1
TR2 Top Rail	38×140 C16	962	0	0	1
ES1 End Stud	38×140 C16	2310	0	0	1
ES2 End Stud	38×140 C16	2310	0	0	1
KS1 Vertical Stud	38×140 C16	2310	0	0	2
CS1 Cripple Stud	38×140 C16	2034	0	0	4
SP1 Sill Plate	38×140 C16	810	0	0	1
LP1 Lintel Ply	962×45 C16	962	0	0	3
SS1 Sill Support	38×140 C16	461	0	0	2
OS1 OSB Support	38×140 C16	93	0	0	2
VS1 Vertical Stud	38×140 C16	2310	0	0	2
VS2 Vertical Stud	38×140 C16	461	0	0	2
VS3 Vertical Stud	38×140 C16	93	0	0	2

Total: 25 pcs / 33.67 m

Sheathing & Insulation

Material	W	H	Label
OSB 9mm	447	2383	S01
OSB 9mm	813	311	S02
OSB 9mm	1137	2383	S03
OSB 9mm	813	534	S04
PIR 120mm	297	2310	P01
PIR 120mm	18	93	P02
PIR 120mm	111	93	P03
PIR 120mm	561	93	P04
PIR 120mm	21	93	P05
PIR 120mm	18	93	P06
PIR 120mm	245	2310	P07
PIR 120mm	561	2310	P08
PIR 120mm	102	2310	P09
PIR 120mm	92	460	P10
PIR 120mm	561	460	P11
PIR 120mm	2	460	P12

General Notes:

Frame Nailing:
140mm Frames Nail Using 3no, 3.1×90mm length field galvanised twisted strip nails
90mm Frames Nail Using 2no, 3.1×90mm length field galvanised twisted strip nails

Sheathing Nails:
Components ≤ 100mm should be +/- 1mm
Components > 100mm should be +/- 1.5mm
Stepped check should be +/- 1.5mm
Sloped Opening sizes are +/-2mm


Nailing:
30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.

Manufacturing Tolerances:
Length ±3 · Height ±2 · Diagonals ±5 · Openings 0/+5 (mm).
Do not scale — work to figured dimensions. All dims in mm.

Breather Membrane:
Laps 100mm horizontal / 150mm vertical, upper lapping lower.

Panel Changes:
When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.

KEY PLAN



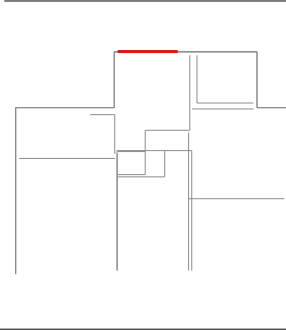


Revisions (Rev · Date · Note):

C01 - Construction issue

Date:	2026-09-13	Scale:	1:20	Drawn:	TS	Checked:	
Project Name:		MP Adams Plot 3, Eckington					
Site:	Eckington			Client:	MP Adams		
Title:	Panel Fabrication — 38 x 140 C16 CLS						
Project Number:	P3			Revision:	C01		
Panel No:	GF-EX8			Drawing No:	P3-MF-GF-EX8		
Panel L×H×T:	2400×2386×149			Weight:	114 kg		
Status:	CONSTRUCTION			Sheet:	1 / 1		

Nailing: OSB/Ply racking: 150mm perimeter / 300mm field nails (EC5 §9.2.4, 2:1 panel h:b)

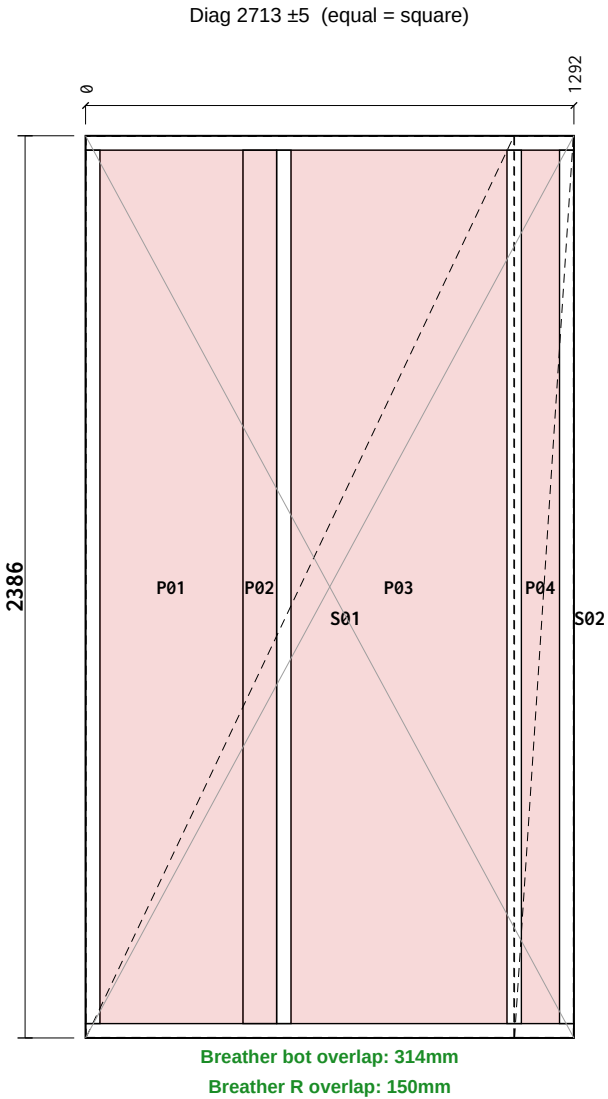

Cut List

Item	Section	Len	Bot°	Top°	Qty
BR1 Bottom Rail	38×140 C16	1292	0	0	1
TR1 Top Rail	38×140 C16	1292	0	0	1
ES1 End Stud	38×140 C16	2310	0	0	1
ES2 End Stud	38×140 C16	2310	0	0	1
VS1 Vertical Stud	38×140 C16	2310	0	0	2
JS1 Junction Stud	38×89 C16	2310	0	0	1
Total: 7 pcs / 14.13 m					

Sheathing & Insulation

Material	W	H	Label
OSB 9mm	1131	2383	S01
OSB 9mm	156	2383	S02
PIR 120mm	378	2310	P01
PIR 100mm	89	2310	P02
PIR 120mm	570	2310	P03
PIR 120mm	100	2310	P04

General Notes:

Frame Nailing:
140mm Frames Nail Using 3no, 3.1×90mm length field galvanised twisted strip nails
90mm Frames Nail Using 2no, 3.1×90mm length field galvanised twisted strip nails

Sheathing Nails:
Components ≤ 100mm should be +/- 1mm
Components > 100mm should be +/- 1.5mm
Stepped check should be +/- 1.5mm
Sloped Opening sizes are +/-2mm


Nailing:
30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.

Manufacturing Tolerances:
Length ±3 · Height ±2 · Diagonals ±5 · Openings 0/+5 (mm).
Do not scale — work to figured dimensions. All dims in mm.

Breather Membrane:
Laps 100mm horizontal / 150mm vertical, upper lapping lower.




Panel Changes:
When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.

KEY PLAN



Revisions (Rev · Date · Note):		C01 - Construction issue					
Date:	2026-09-13	Scale:	1:20	Drawn:	TS	Checked:	
Project Name:		MP Adams Plot 3, Eckington					
Site:	Eckington			Client:	MP Adams		
Title:	Panel Fabrication — 38 x 140 C16 CLS						
Project Number:	P3			Revision:	C01		
Panel No:	GF-EX9			Drawing No:	P3-MF-GF-EX9		
Panel L×H×T:	1292×2386×149			Weight:	57 kg		
Status:	CONSTRUCTION			Sheet:	1 / 1		

Nailing: OSB/Ply racking: 150mm perimeter / 300mm field nails (EC5 §9.2.4, 2:1 panel h:b)

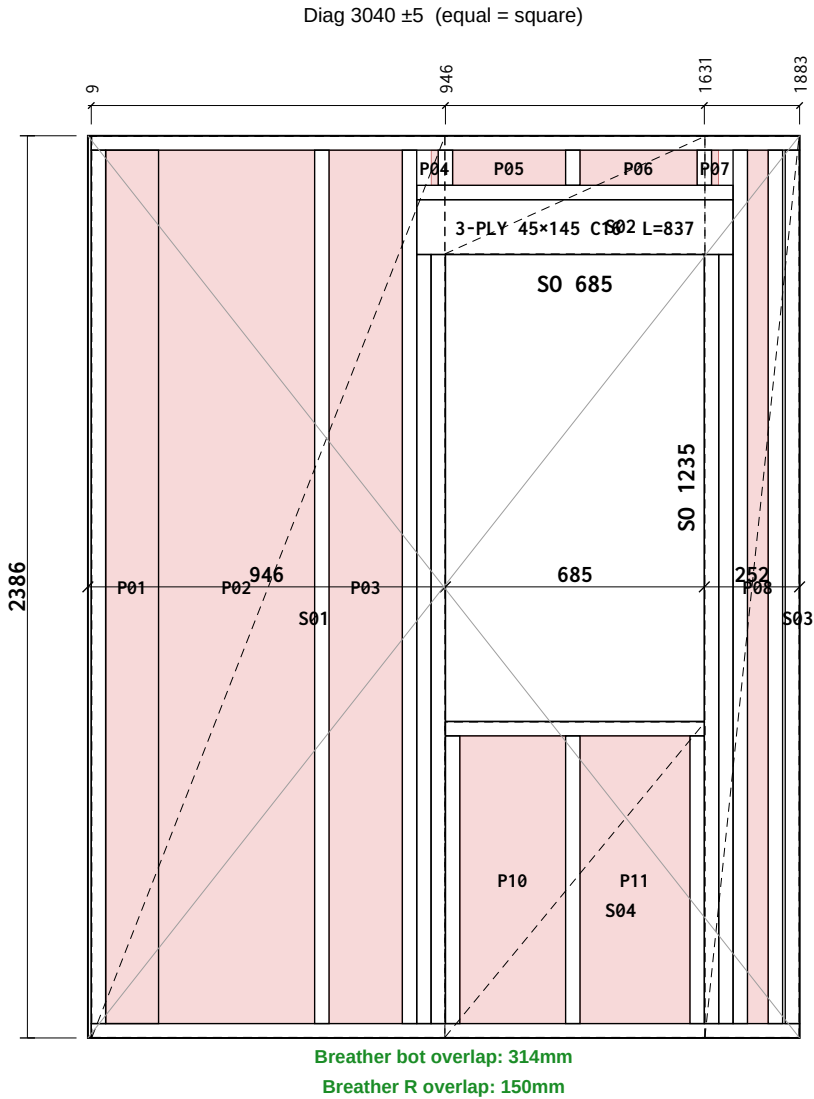

Cut List

Item	Section	Len	Bot°	Top°	Qty
BR1 Bottom Rail	38×140 C16	1874	0	0	1
TR1 Top Rail	38×140 C16	1874	0	0	1
TR2 Top Rail	38×140 C16	837	0	0	1
ES1 End Stud	38×140 C16	2310	0	0	1
ES2 End Stud	38×140 C16	2310	0	0	1
KS1 Vertical Stud	38×140 C16	2310	0	0	2
CS1 Cripple Stud	38×140 C16	2034	0	0	4
SP1 Sill Plate	38×140 C16	685	0	0	1
LP1 Lintel Ply	837×45 C16	837	0	0	3
SS1 Sill Support	38×140 C16	761	0	0	2
OS1 OSB Support	38×140 C16	93	0	0	2
VS1 Vertical Stud	38×140 C16	2310	0	0	2
VS2 Vertical Stud	38×140 C16	761	0	0	1
VS3 Vertical Stud	38×140 C16	93	0	0	1
JS1 Junction Stud	38×140 C16	2310	0	0	1

Total: 24 pcs / 34.65 m

Sheathing & Insulation

Material	W	H	Label
OSB 9mm	934	2383	S01
OSB 9mm	688	311	S02
OSB 9mm	249	2383	S03
OSB 9mm	688	834	S04
PIR 100mm	140	2310	P01
PIR 120mm	412	2310	P02
PIR 120mm	193	2310	P03
PIR 120mm	18	93	P04
PIR 120mm	298	93	P05
PIR 120mm	309	93	P06
PIR 120mm	18	93	P07
PIR 120mm	53	2310	P08
PIR 120mm	6	2310	P09
PIR 120mm	279	760	P10
PIR 120mm	290	760	P11
OSB End Cap 9mm	146	2383	E01

General Notes:

Frame Nailing:
140mm Frames Nail Using 3no, 3.1×90mm length field galvanised twisted strip nails
90mm Frames Nail Using 2no, 3.1×90mm length field galvanised twisted strip nails

Sheathing Nails:
Components ≤ 100mm should be +/- 1mm
Components > 100mm should be +/- 1.5mm
Stepped check should be +/- 1.5mm
Sloped Opening sizes are +/-2mm


Nailing:
30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.

Manufacturing Tolerances:
Length ±3 · Height ±2 · Diagonals ±5 · Openings 0/+5 (mm).
Do not scale — work to figured dimensions. All dims in mm.

Breather Membrane:
Laps 100mm horizontal / 150mm vertical, upper lapping lower.

Panel Changes:
When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.

KEY PLAN





Revisions (Rev · Date · Note):

C01 - Construction issue

Date:	2026-09-13	Scale:	1:20	Drawn:	TS	Checked:	
Project Name: MP Adams Plot 3, Eckington							
Site: Eckington				Client: MP Adams			
Title: Panel Fabrication — 38 x 140 C16 CLS							
Project Number: P3				Revision: C01			
Panel No: GF-EX10				Drawing No: P3-MF-GF-EX10			
Panel L×H×T: 1883×2386×149				Weight: 110 kg			
Status: CONSTRUCTION				Sheet: 1 / 1			


Nailing: OSB/Ply racking: 150mm perimeter / 300mm field nails (EC5 §9.2.4, 2:1 panel h:b)

Diag 3197 $\pm$ 5 (equal = square)

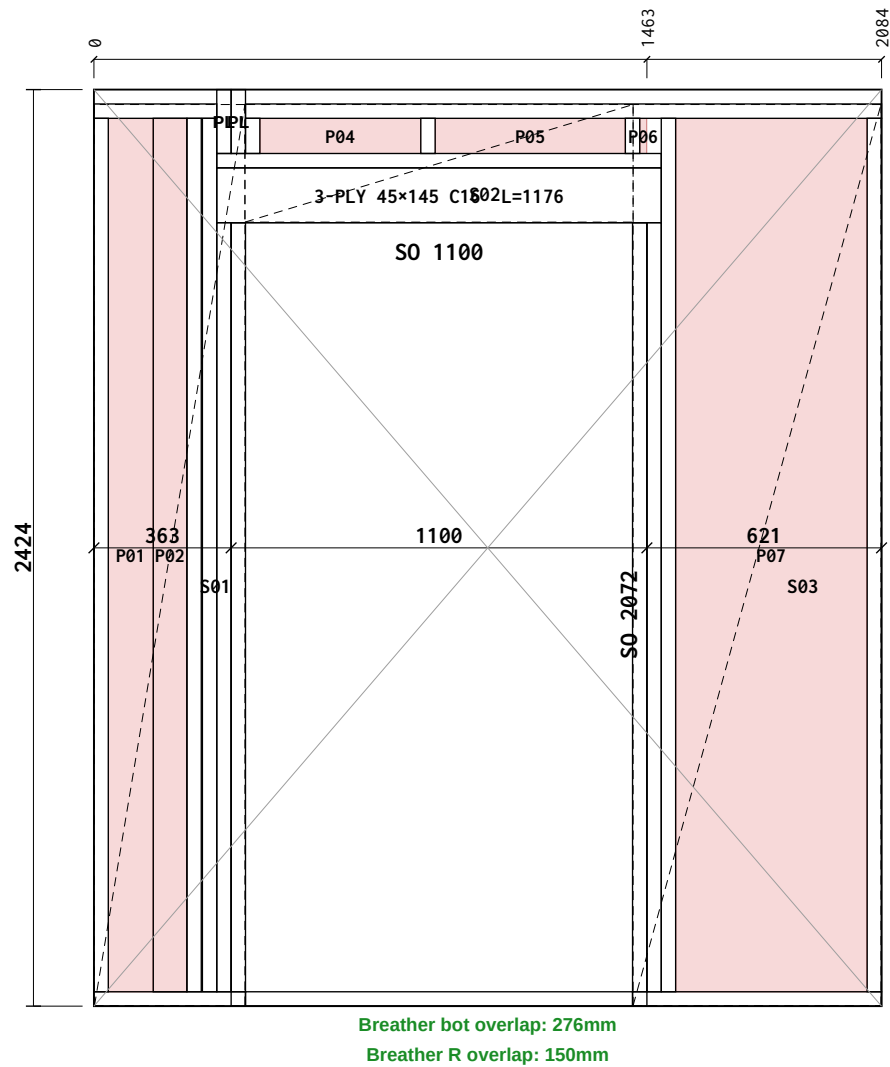

Section A-A

Ext	Int
-----	-----



Cut List

Item	Section	Len	Bot°	Top°	Qty
BR1 Bottom Rail	38×140 C16	1024	0	0	1
BR2 Bottom Rail	38×140 C16	659	0	0	1
BR3 Bottom Rail	38×140 C16	401	0	0	1
TR1 Top Rail	38×140 C16	1683	0	0	1
TR2 Top Rail	38×140 C16	1176	0	0	1
TR3 Top Rail	38×140 C16	325	0	0	1
ES1 End Stud	38×140 C16	2310	0	0	1
ES2 End Stud	38×140 C16	2310	0	0	1
KS1 Vertical Stud	38×140 C16	2310	0	0	2
CS1 Cripple Stud	38×140 C16	2034	0	0	4
CS2 Cripple Stud	38×140 C16	93	0	0	1
LP1 Lintel Ply	1176×45 C16	1176	0	0	3
OS1 OSB Support	38×140 C16	93	0	0	1
VS1 Vertical Stud	38×140 C16	2310	0	0	1
VS2 Vertical Stud	38×140 C16	93	0	0	1
JS1 Junction Stud	38×89 C16	2310	0	0	1

Total: 22 pcs / 31.07 m

Sheathing & Insulation

Material	W	H	Label
OSB 9mm	398	2383	S01
OSB 9mm	1027	311	S02
OSB 9mm	656	2383	S03
PIR 120mm	118	2310	P01
PIR 100mm	89	2310	P02
PIR 120mm	1	2310	P03
PIR 120mm	425	93	P04
PIR 120mm	502	93	P05
PIR 120mm	18	93	P06
PIR 120mm	505	2310	P07

General Notes:

Frame Nailing:

140mm Frames Nail Using 3no, 3.1×90mm length field galvanised twisted strip nails
90mm Frames Nail Using 2no, 3.1×90mm length field galvanised twisted strip nails

Sheathing Nails:

Components $\leq 100\text{mm}$ should be $\pm 1\text{mm}$
 Components $> 100\text{mm}$ should be $\pm 1.5\text{mm}$
 Stepped check should be $\pm 1.5\text{mm}$
 Sloped Opening sizes are $\pm 2\text{mm}$

Nailing:

30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.

Manufacturing Tolerances:

Length ± 3 · Height ± 2 · Diagonals ± 5 · Openings 0/+5 (mm).
Do not scale — work to figured dimensions. All dims in mm.


Breather Membrane:

Laps 100mm horizontal / 150mm vertical, upper lapping lower.

Panel Changes:

When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.

KEY PLAN


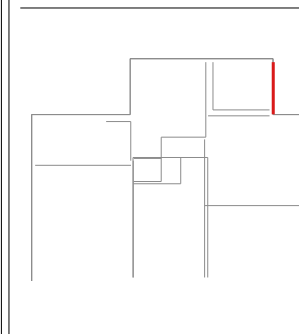


Revisions (Rev · Date · Note):

C01 - Construction issue

Date:	2026-09-13	Scale:	1:20	Drawn:	TS	Checked:	
Project Name:		MP Adams Plot 3, Eckington					
Site:		Eckington		Client:		MP Adams	
Title:		Panel Fabrication — 38 x 140 C16 CLS					
Project Number:		P3		Revision:		C01	
Panel No:		GF-EX11		Drawing No:		P3-MF-GF-EX11	
Panel L×H×T:		2084×2424×149		Weight:		92 kg	
Status:		CONSTRUCTION		Sheet:		1 / 1	

Nailing: OSB/Ply racking: 150mm perimeter / 300mm field nails (EC5 §9.2.4, 2:1 panel h:b)

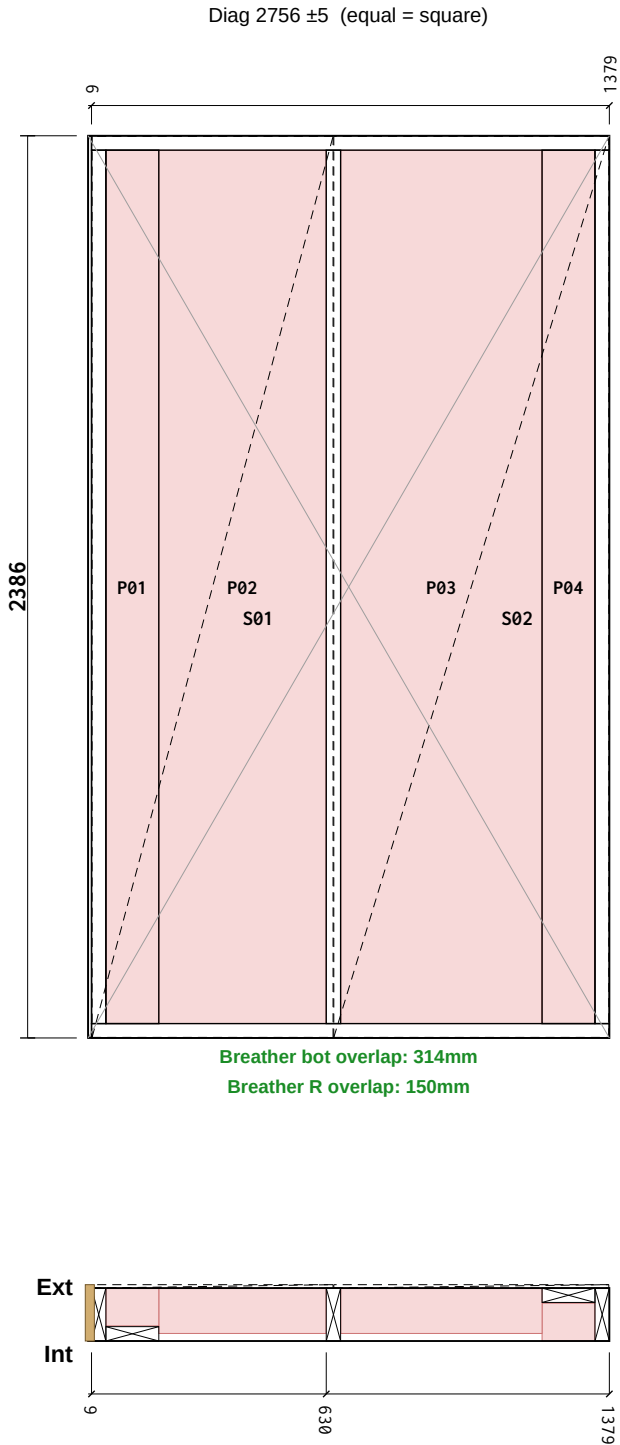

Cut List

Item	Section	Len	Bot°	Top°	Qty
BR1 Bottom Rail	38×140 C16	1370	0	0	1
TR1 Top Rail	38×140 C16	1370	0	0	1
ES1 End Stud	38×140 C16	2310	0	0	1
ES2 End Stud	38×140 C16	2310	0	0	1
VS1 Vertical Stud	38×140 C16	2310	0	0	1
JS1 Junction Stud	38×140 C16	2310	0	0	2
Total: 7 pcs / 14.29 m					

Sheathing & Insulation

Material	W	HLabel
OSB 9mm	637	2383 S01
OSB 9mm	728	2383 S02
PIR 100mm	140	2310 P01
PIR 120mm	442	2310 P02
PIR 120mm	533	2310 P03
PIR 100mm	140	2310 P04
OSB End Cap 9mm	146	2383 E01

General Notes:

Frame Nailing:
140mm Frames Nail Using 3no, 3.1×90mm length field galvanised twisted strip nails
90mm Frames Nail Using 2no, 3.1×90mm length field galvanised twisted strip nails

Sheathing Nails:
Components ≤ 100mm should be +/- 1mm
Components > 100mm should be +/- 1.5mm
Stepped check should be +/- 1.5mm
Sloped Opening sizes are +/-2mm


Nailing:
30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.

Manufacturing Tolerances:
Length ±3 · Height ±2 · Diagonals ±5 · Openings 0/+5 (mm).
Do not scale — work to figured dimensions. All dims in mm.

Breather Membrane:
Laps 100mm horizontal / 150mm vertical, upper lapping lower.



Panel Changes:
When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.

KEY PLAN



Revisions (Rev · Date · Note):		C01 - Construction issue					
Date:	2026-09-13	Scale:	1:20	Drawn:	TS	Checked:	
Project Name:		MP Adams Plot 3, Eckington					
Site:	Eckington			Client:	MP Adams		
Title:	Panel Fabrication — 38 x 140 C16 CLS						
Project Number:	P3			Revision:	C01		
Panel No:	GF-EX12			Drawing No:	P3-MF-GF-EX12		
Panel L×H×T:	1379×2386×149			Weight:	63 kg		
Status:	CONSTRUCTION			Sheet:	1 / 1		

Nailing: OSB/Ply racking: 150mm perimeter / 300mm field nails (EC5 §9.2.4, 2:1 panel h:b)

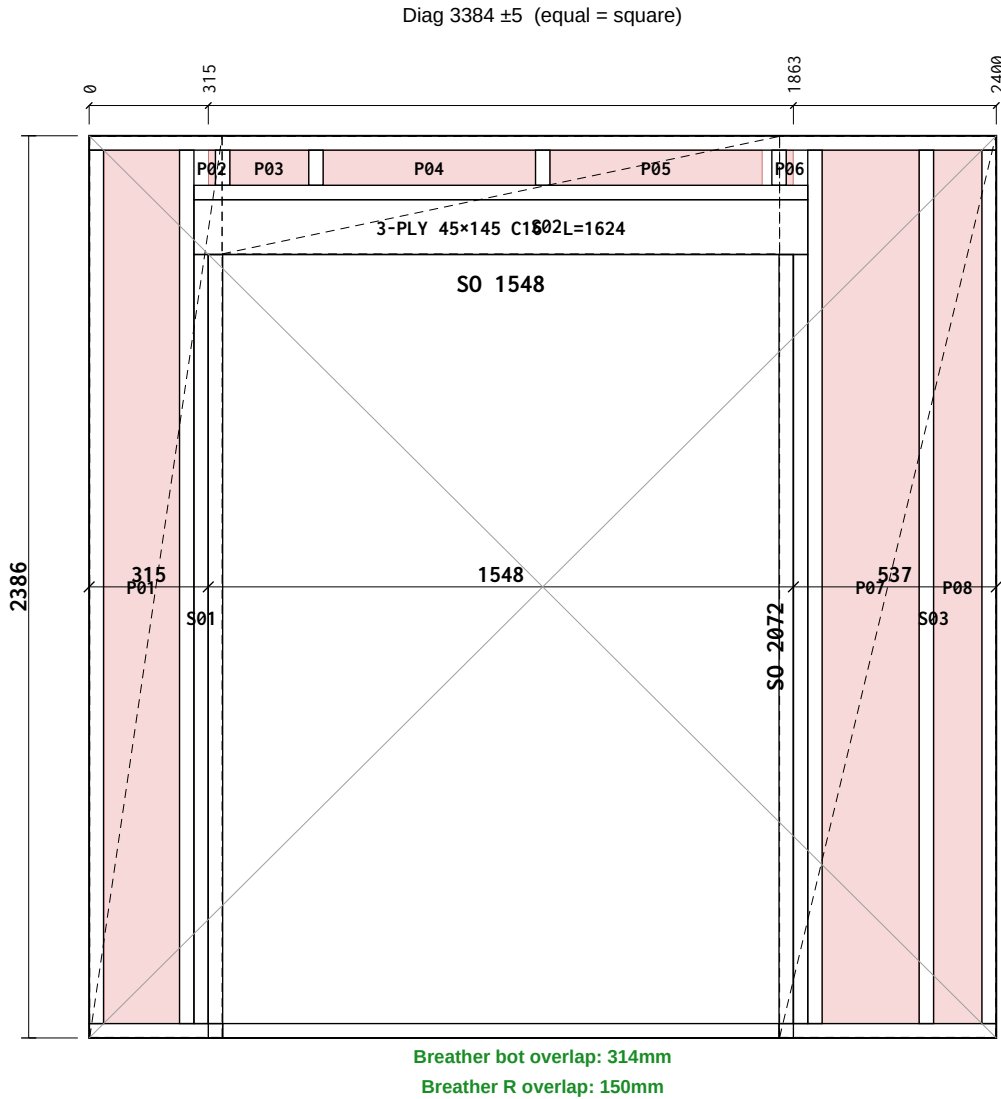

Cut List

Item	Section	Len	Bot°	Top°	Qty
BR1 Bottom Rail	38×140 C16	1472	0	0	1
BR2 Bottom Rail	38×140 C16	575	0	0	1
BR3 Bottom Rail	38×140 C16	353	0	0	1
TR1 Top Rail	38×140 C16	2400	0	0	1
TR2 Top Rail	38×140 C16	1624	0	0	1
ES1 End Stud	38×140 C16	2310	0	0	1
ES2 End Stud	38×140 C16	2310	0	0	1
KS1 Vertical Stud	38×140 C16	2310	0	0	2
CS1 Cripple Stud	38×140 C16	2034	0	0	4
LP1 Lintel Ply	1624×45 C16	1624	0	0	3
OS1 OSB Support	38×140 C16	93	0	0	2
VS1 Vertical Stud	38×140 C16	2310	0	0	1
VS2 Vertical Stud	38×140 C16	93	0	0	2

Total: 21 pcs / 31.35 m

Sheathing & Insulation

Material	W	H	Label
OSB 9mm	350	2383	S01
OSB 9mm	1475	311	S02
OSB 9mm	572	2383	S03
PIR 120mm	200	2310	P01
PIR 120mm	18	93	P02
PIR 120mm	208	93	P03
PIR 120mm	561	93	P04
PIR 120mm	561	93	P05
PIR 120mm	18	93	P06
PIR 120mm	255	2310	P07
PIR 120mm	127	2310	P08

General Notes:

Frame Nailing:
140mm Frames Nail Using 3no, 3.1×90mm length field galvanised twisted strip nails
90mm Frames Nail Using 2no, 3.1×90mm length field galvanised twisted strip nails

Sheathing Nails:
Components ≤ 100mm should be +/- 1mm
Components > 100mm should be +/- 1.5mm
Stepped check should be +/- 1.5mm
Sloped Opening sizes are +/-2mm


Nailing:
30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.

Manufacturing Tolerances:
Length ±3 · Height ±2 · Diagonals ±5 · Openings 0/+5 (mm).
Do not scale — work to figured dimensions. All dims in mm.

Breather Membrane:
Laps 100mm horizontal / 150mm vertical, upper lapping lower.

Panel Changes:
When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.

KEY PLAN





Revisions (Rev · Date · Note):

C01 - Construction issue

Date:	2026-09-13	Scale:	1:20	Drawn:	TS	Checked:	
Project Name:	MP Adams Plot 3, Eckington						
Site:	Eckington			Client:	MP Adams		
Title:	Panel Fabrication — 38 x 140 C16 CLS						
Project Number:	P3			Revision:	C01		
Panel No:	GF-EX13			Drawing No:	P3-MF-GF-EX13		
Panel L×H×T:	2400×2386×149			Weight:	93 kg		
Status:	CONSTRUCTION			Sheet:	1 / 1		

Nailing: OSB/Ply racking: 150mm perimeter / 300mm field nails (EC5 §9.2.4, 2:1 panel h:b)

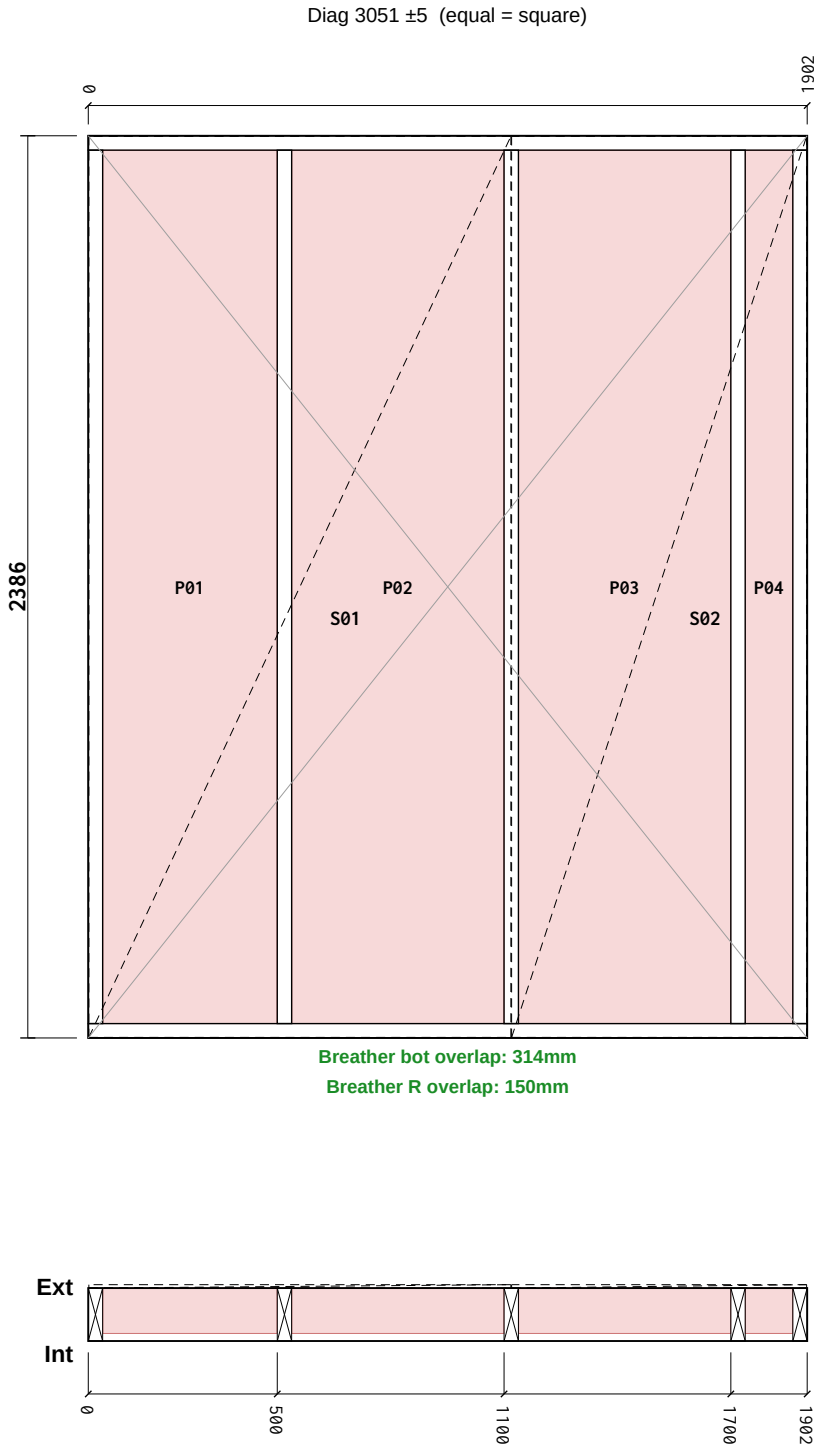

Cut List

Item	Section	Len	Bot°	Top°	Qty
BR1 Bottom Rail	38×140 C16	1902	0	0	1
TR1 Top Rail	38×140 C16	1902	0	0	1
ES1 End Stud	38×140 C16	2310	0	0	1
ES2 End Stud	38×140 C16	2310	0	0	1
VS1 Vertical Stud	38×140 C16	2310	0	0	3
Total: 7 pcs / 15.35 m					
Sheathing & Insulation					
Material		W	H	Label	
OSB 9mm		1116	2383	S01	
OSB 9mm		781	2383	S02	
PIR 120mm		461	2310	P01	
PIR 120mm		561	2310	P02	
PIR 120mm		561	2310	P03	
PIR 120mm		125	2310	P04	

General Notes:

Frame Nailing:
140mm Frames Nail Using 3no, 3.1×90mm length field galvanised twisted strip nails
90mm Frames Nail Using 2no, 3.1×90mm length field galvanised twisted strip nails

Sheathing Nails:
Components ≤ 100mm should be +/- 1mm
Components > 100mm should be +/- 1.5mm
Stepped check should be +/- 1.5mm
Sloped Opening sizes are +/-2mm


Nailing:
30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.

Manufacturing Tolerances:
Length ±3 · Height ±2 · Diagonals ±5 · Openings 0/+5 (mm).
Do not scale — work to figured dimensions. All dims in mm.

Breather Membrane:
Laps 100mm horizontal / 150mm vertical, upper lapping lower.




Panel Changes:
When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.

KEY PLAN



Revisions (Rev · Date · Note):		C01 - Construction issue					
Date:	2026-09-13	Scale:	1:20	Drawn:	TS	Checked:	
Project Name:		MP Adams Plot 3, Eckington					
Site:	Eckington			Client:	MP Adams		
Title:	Panel Fabrication — 38 x 140 C16 CLS						
Project Number:	P3			Revision:	C01		
Panel No:	GF-EX14			Drawing No:	P3-MF-GF-EX14		
Panel L×H×T:	1902×2386×149			Weight:	76 kg		
Status:	CONSTRUCTION			Sheet:	1 / 1		

Nailing: OSB/Ply racking: 150mm perimeter / 300mm field nails (EC5 §9.2.4, 2:1 panel h:b)

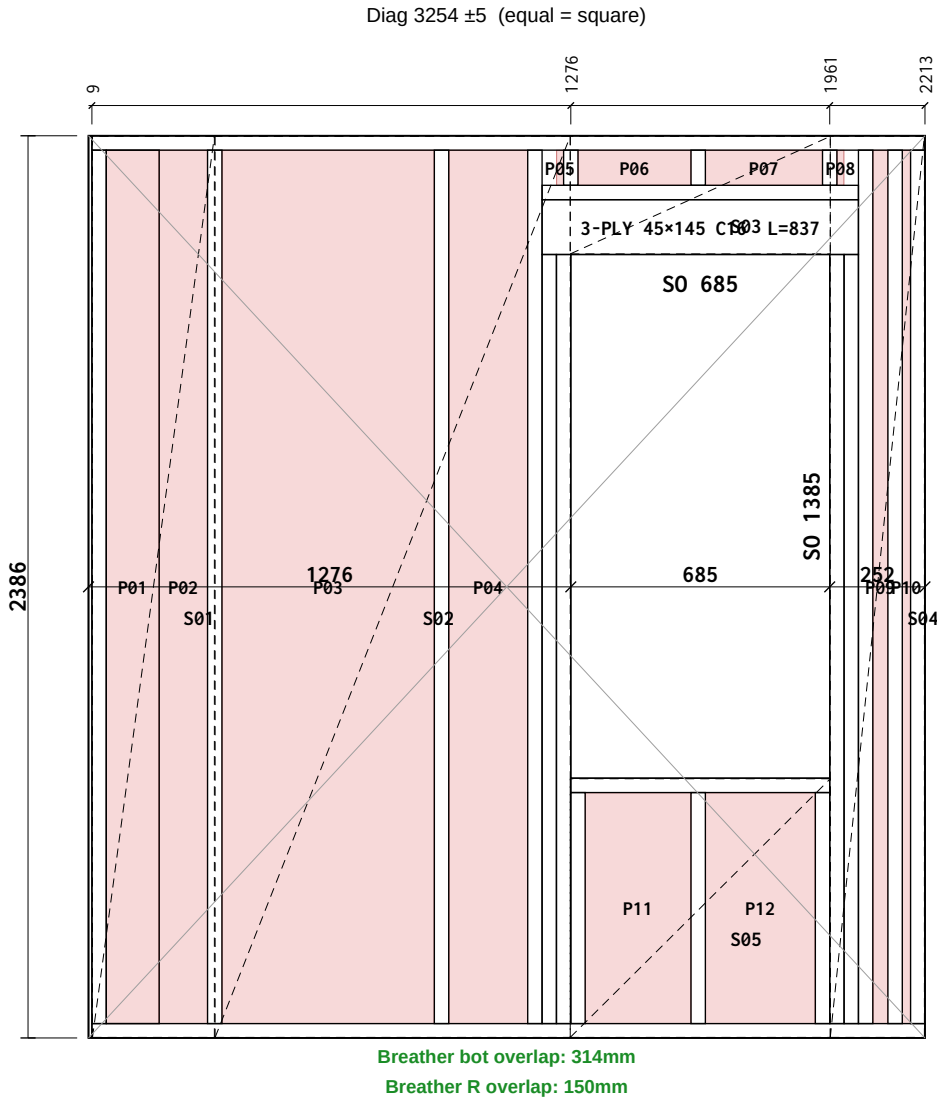

Cut List

Item	Section	Len	Bot°	Top°	Qty
BR1 Bottom Rail	38×140 C16	2204	0	0	1
TR1 Top Rail	38×140 C16	2204	0	0	1
TR2 Top Rail	38×140 C16	837	0	0	1
ES1 End Stud	38×140 C16	2310	0	0	1
ES2 End Stud	38×140 C16	2310	0	0	1
KS1 Vertical Stud	38×140 C16	2310	0	0	2
CS1 Cripple Stud	38×140 C16	2034	0	0	4
SP1 Sill Plate	38×140 C16	685	0	0	1
LP1 Lintel Ply	837×45 C16	837	0	0	3
SS1 Sill Support	38×140 C16	611	0	0	2
OS1 OSB Support	38×140 C16	93	0	0	2
VS1 Vertical Stud	38×140 C16	2310	0	0	3
VS2 Vertical Stud	38×140 C16	611	0	0	1
VS3 Vertical Stud	38×140 C16	93	0	0	1
JS1 Junction Stud	38×140 C16	2310	0	0	1

Total: 25 pcs / 37.17 m

Sheathing & Insulation

Material	W	H	Label
OSB 9mm	322	2383	S01
OSB 9mm	940	2383	S02
OSB 9mm	688	311	S03
OSB 9mm	249	2383	S04
OSB 9mm	688	684	S05
PIR 100mm	140	2310	P01
PIR 120mm	127	2310	P02
PIR 120mm	561	2310	P03
PIR 120mm	208	2310	P04
PIR 120mm	18	93	P05
PIR 120mm	298	93	P06
PIR 120mm	309	93	P07
PIR 120mm	18	93	P08
PIR 120mm	38	2310	P09
PIR 120mm	21	2310	P10
PIR 120mm	279	610	P11
PIR 120mm	290	610	P12
OSB End Cap 9mm	146	2383	E01

General Notes:

Frame Nailing:
140mm Frames Nail Using 3no, 3.1×90mm length field galvanised twisted strip nails
90mm Frames Nail Using 2no, 3.1×90mm length field galvanised twisted strip nails

Sheathing Nails:
Components ≤ 100mm should be +/- 1mm
Components > 100mm should be +/- 1.5mm
Stepped check should be +/- 1.5mm
Sloped Opening sizes are +/-2mm


Nailing:
30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.

Manufacturing Tolerances:
Length ±3 · Height ±2 · Diagonals ±5 · Openings 0/+5 (mm).
Do not scale — work to figured dimensions. All dims in mm.

Breather Membrane:
Laps 100mm horizontal / 150mm vertical, upper lapping lower.

Panel Changes:
When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.

KEY PLAN






Revisions (Rev · Date · Note):

C01 - Construction issue

Date:	2026-09-13	Scale:	1:20	Drawn:	TS	Checked:	
Project Name:	MP Adams Plot 3, Eckington						
Site:	Eckington			Client:	MP Adams		
Title:	Panel Fabrication — 38 x 140 C16 CLS						
Project Number:	P3			Revision:	C01		
Panel No:	GF-EX15			Drawing No:	P3-MF-GF-EX15		
Panel L×H×T:	2213×2386×149			Weight:	122 kg		
Status:	CONSTRUCTION			Sheet:	1 / 1		

Nailing: OSB/Ply racking: 150mm perimeter / 300mm field nails (EC5 §9.2.4, 2:1 panel h:b)

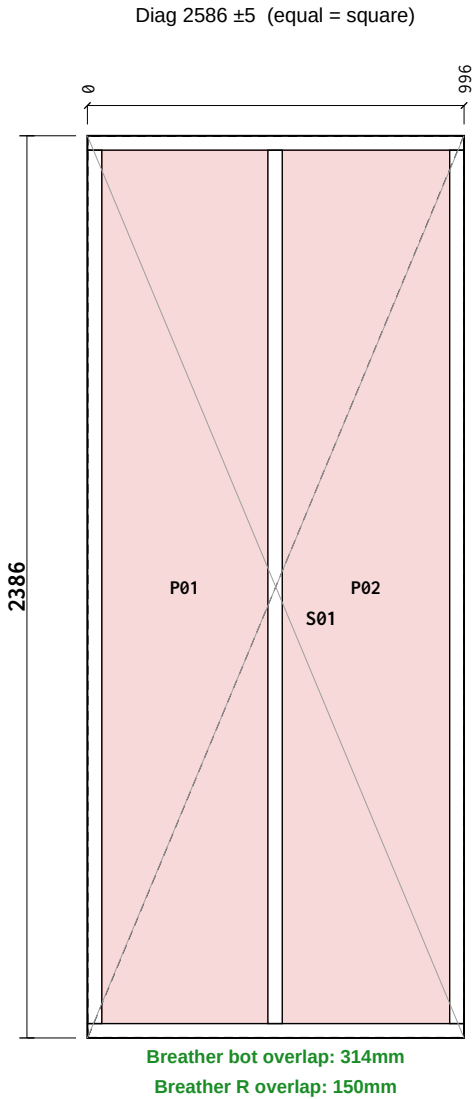

Cut List

Item	Section	Len	Bot°	Top°	Qty
BR1 Bottom Rail	38×140 C16	997	0	0	1
TR1 Top Rail	38×140 C16	997	0	0	1
ES1 End Stud	38×140 C16	2310	0	0	1
ES2 End Stud	38×140 C16	2310	0	0	1
VS1 Vertical Stud	38×140 C16	2310	0	0	1
Total: 5 pcs / 8.92 m					

Sheathing & Insulation

Material	W	H	Label
OSB 9mm	994	2383	S01
PIR 120mm	439	2310	P01
PIR 120mm	442	2310	P02

General Notes:

Frame Nailing:
140mm Frames Nail Using 3no, 3.1×90mm length field galvanised twisted strip nails
90mm Frames Nail Using 2no, 3.1×90mm length field galvanised twisted strip nails

Sheathing Nails:
Components ≤ 100mm should be +/- 1mm
Components > 100mm should be +/- 1.5mm
Stepped check should be +/- 1.5mm
Sloped Opening sizes are +/-2mm


Nailing:
30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.

Manufacturing Tolerances:
Length ±3 · Height ±2 · Diagonals ±5 · Openings 0/+5 (mm).
Do not scale — work to figured dimensions. All dims in mm.

Breather Membrane:
Laps 100mm horizontal / 150mm vertical, upper lapping lower.

Panel Changes:
When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.

KEY PLAN






Revisions (Rev · Date · Note):

C01 - Construction issue

Date:	2026-09-13	Scale:	1:20	Drawn:	TS	Checked:	
Project Name:		MP Adams Plot 3, Eckington					
Site:		Eckington		Client:		MP Adams	
Title:		Panel Fabrication — 38 x 140 C16 CLS					
Project Number:		P3		Revision:		C01	
Panel No:		GF-EX16		Drawing No:		P3-MF-GF-EX16	
Panel L×H×T:		997×2386×149		Weight:		41 kg	
Status:		CONSTRUCTION		Sheet:		1 / 1	

Nailing: OSB/Ply racking: 150mm perimeter / 300mm field nails (EC5 §9.2.4, 2:1 panel h:b)

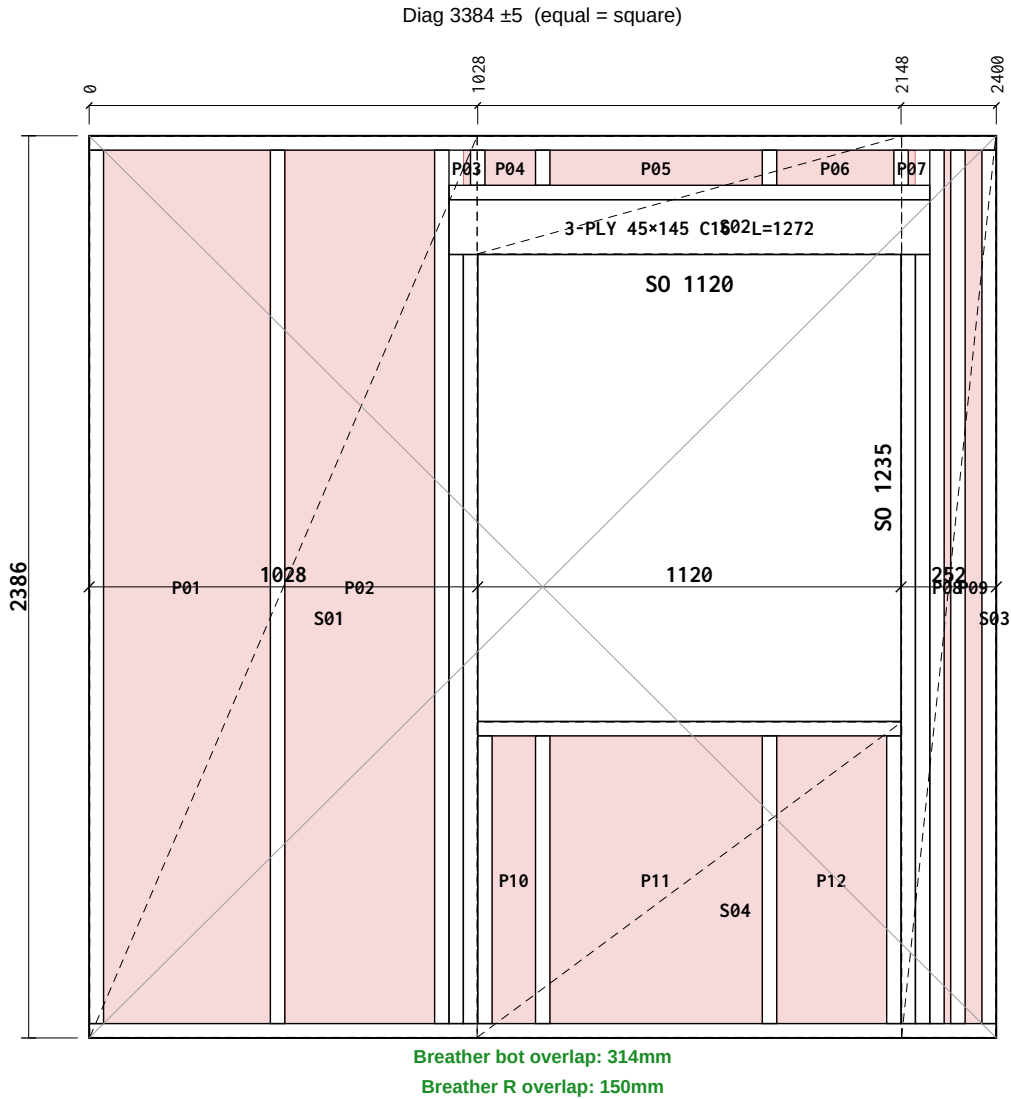

Cut List

Item	Section	Len	Bot°	Top°	Qty
BR1 Bottom Rail	38×140 C16	2400	0	0	1
TR1 Top Rail	38×140 C16	2400	0	0	1
TR2 Top Rail	38×140 C16	1272	0	0	1
ES1 End Stud	38×140 C16	2310	0	0	1
ES2 End Stud	38×140 C16	2310	0	0	1
KS1 Vertical Stud	38×140 C16	2310	0	0	2
CS1 Cripple Stud	38×140 C16	2034	0	0	4
SP1 Sill Plate	38×140 C16	1120	0	0	1
LP1 Lintel Ply	1272×45 C16	1272	0	0	3
SS1 Sill Support	38×140 C16	761	0	0	2
OS1 OSB Support	38×140 C16	93	0	0	2
VS1 Vertical Stud	38×140 C16	2310	0	0	2
VS2 Vertical Stud	38×140 C16	761	0	0	2
VS3 Vertical Stud	38×140 C16	93	0	0	2

Total: 25 pcs / 36.42 m

Sheathing & Insulation

Material	W	H	Label
OSB 9mm	1025	2383	S01
OSB 9mm	1123	311	S02
OSB 9mm	249	2383	S03
OSB 9mm	1123	834	S04
PIR 120mm	441	2310	P01
PIR 120mm	395	2310	P02
PIR 120mm	18	93	P03
PIR 120mm	133	93	P04
PIR 120mm	561	93	P05
PIR 120mm	309	93	P06
PIR 120mm	18	93	P07
PIR 120mm	16	2310	P08
PIR 120mm	43	2310	P09
PIR 120mm	114	760	P10
PIR 120mm	561	760	P11
PIR 120mm	290	760	P12

General Notes:

Frame Nailing:
140mm Frames Nail Using 3no, 3.1×90mm length field galvanised twisted strip nails
90mm Frames Nail Using 2no, 3.1×90mm length field galvanised twisted strip nails

Sheathing Nails:
Components ≤ 100mm should be +/- 1mm
Components > 100mm should be +/- 1.5mm
Stepped check should be +/- 1.5mm
Sloped Opening sizes are +/-2mm


Nailing:
30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.

Manufacturing Tolerances:
Length ±3 · Height ±2 · Diagonals ±5 · Openings 0/+5 (mm).
Do not scale — work to figured dimensions. All dims in mm.

Breather Membrane:
Laps 100mm horizontal / 150mm vertical, upper lapping lower.

Panel Changes:
When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.

KEY PLAN






Revisions (Rev · Date · Note):

C01 - Construction issue

Date:	2026-09-13	Scale:	1:20	Drawn:	TS	Checked:	
Project Name:		MP Adams Plot 3, Eckington					
Site:	Eckington			Client:	MP Adams		
Title:	Panel Fabrication — 38 x 140 C16 CLS						
Project Number:	P3			Revision:	C01		
Panel No:	GF-EX17			Drawing No:	P3-MF-GF-EX17		
Panel L×H×T:	2400×2386×149			Weight:	119 kg		
Status:	CONSTRUCTION			Sheet:	1 / 1		

Nailing: OSB/Ply racking: 150mm perimeter / 300mm field nails (EC5 §9.2.4, 2:1 panel h:b)

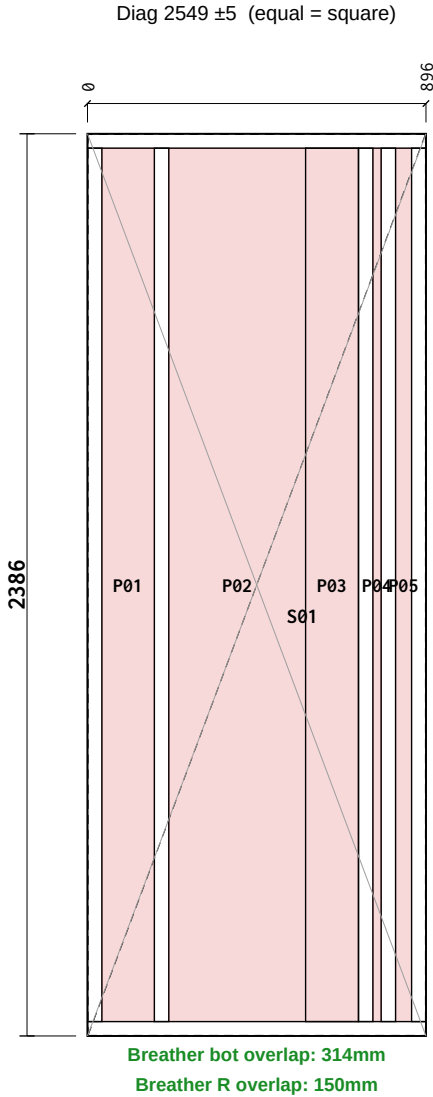

Cut List

Item	Section	Len	Bot°	Top°	Qty
BR1 Bottom Rail	38×140 C16	896	0	0	1
TR1 Top Rail	38×140 C16	896	0	0	1
ES1 End Stud	38×140 C16	2310	0	0	1
ES2 End Stud	38×140 C16	2310	0	0	1
VS1 Vertical Stud	38×140 C16	2310	0	0	3
JS1 Junction Stud	38×140 C16	2310	0	0	1
Total: 8 pcs / 15.65 m					

Sheathing & Insulation

Material	W	H	Label
OSB 9mm	893	2383	S01
PIR 120mm	138	2310	P01
PIR 120mm	361	2310	P02
PIR 100mm	140	2310	P03
PIR 120mm	21	2310	P04
PIR 120mm	41	2310	P05

General Notes:

Frame Nailing:
140mm Frames Nail Using 3no, 3.1×90mm length field galvanised twisted strip nails
90mm Frames Nail Using 2no, 3.1×90mm length field galvanised twisted strip nails

Sheathing Nails:
Components ≤ 100mm should be +/- 1mm
Components > 100mm should be +/- 1.5mm
Stepped check should be +/- 1.5mm
Sloped Opening sizes are +/-2mm


Nailing:
30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.

Manufacturing Tolerances:
Length ±3 · Height ±2 · Diagonals ±5 · Openings 0/+5 (mm).
Do not scale — work to figured dimensions. All dims in mm.

Breather Membrane:
Laps 100mm horizontal / 150mm vertical, upper lapping lower.




Panel Changes:
When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.

KEY PLAN



Revisions (Rev · Date · Note):				C01 - Construction issue			
Date:	2026-09-13	Scale:	1:20	Drawn:	TS	Checked:	
Project Name:		MP Adams Plot 3, Eckington					
Site:	Eckington			Client:	MP Adams		
Title:		Panel Fabrication — 38 x 140 C16 CLS					
Project Number:		P3		Revision:		C01	
Panel No:		GF-EX18		Drawing No:		P3-MF-GF-EX18	
Panel L×H×T:		896×2386×149		Weight:		53 kg	
Status:		CONSTRUCTION		Sheet:		1 / 1	

Nailing: OSB/Ply racking: 150mm perimeter / 300mm field nails (EC5 §9.2.4, 2:1 panel h:b)

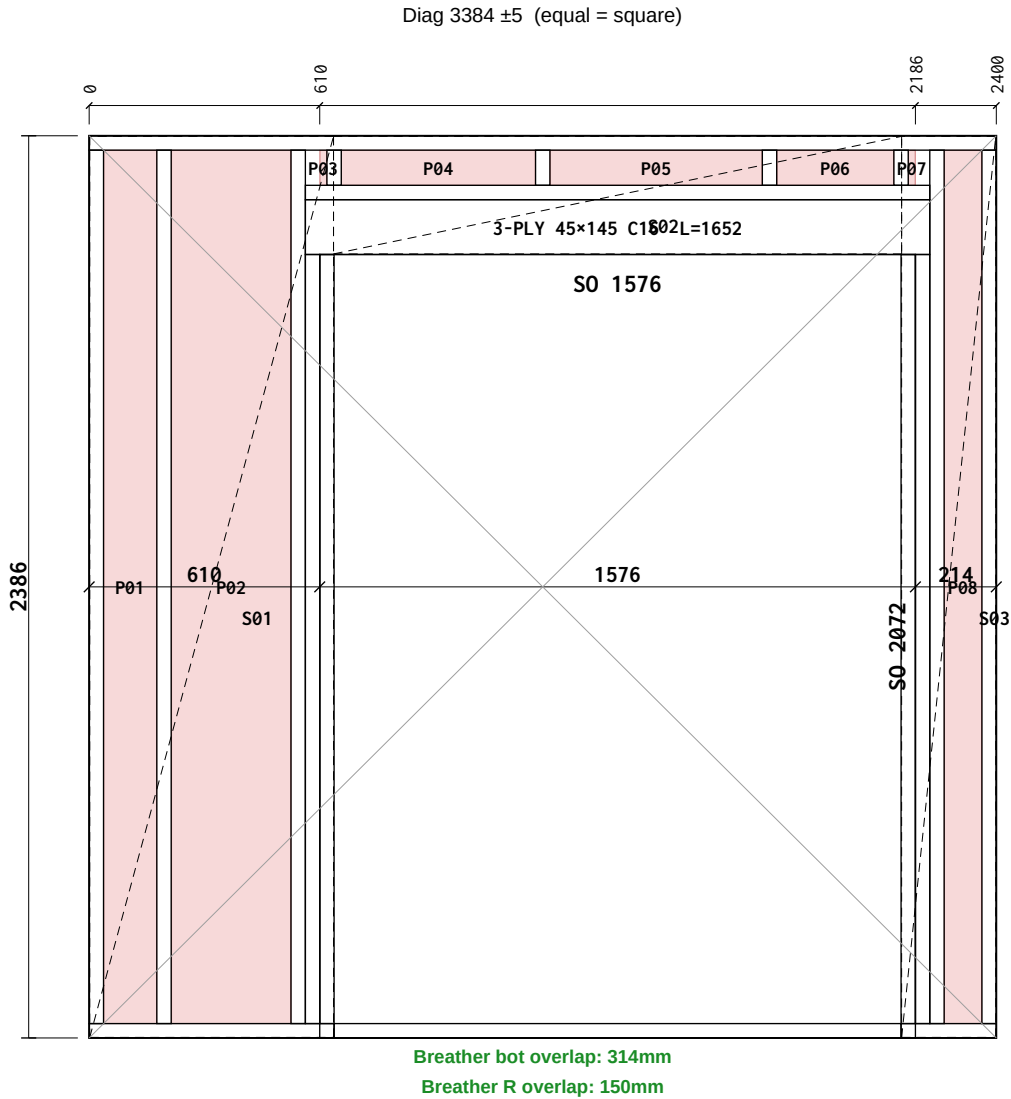

Cut List

Item	Section	Len	Bot°	Top°	Qty
BR1 Bottom Rail	38×140 C16	1500	0	0	1
BR2 Bottom Rail	38×140 C16	648	0	0	1
BR3 Bottom Rail	38×140 C16	252	0	0	1
TR1 Top Rail	38×140 C16	2400	0	0	1
TR2 Top Rail	38×140 C16	1652	0	0	1
ES1 End Stud	38×140 C16	2310	0	0	1
ES2 End Stud	38×140 C16	2310	0	0	1
KS1 Vertical Stud	38×140 C16	2310	0	0	2
CS1 Cripple Stud	38×140 C16	2034	0	0	4
LP1 Lintel Ply	1652×45 C16	1652	0	0	3
OS1 OSB Support	38×140 C16	93	0	0	2
VS1 Vertical Stud	38×140 C16	2310	0	0	1
VS2 Vertical Stud	38×140 C16	93	0	0	2

Total: 21 pcs / 31.47 m

Sheathing & Insulation

Material	W	H	Label
OSB 9mm	645	2383	S01
OSB 9mm	1503	311	S02
OSB 9mm	249	2383	S03
PIR 120mm	140	2310	P01
PIR 120mm	315	2310	P02
PIR 120mm	18	93	P03
PIR 120mm	513	93	P04
PIR 120mm	561	93	P05
PIR 120mm	309	93	P06
PIR 120mm	18	93	P07
PIR 120mm	99	2310	P08

General Notes:

Frame Nailing:
140mm Frames Nail Using 3no, 3.1×90mm length field galvanised twisted strip nails
90mm Frames Nail Using 2no, 3.1×90mm length field galvanised twisted strip nails

Sheathing Nails:
Components ≤ 100mm should be +/- 1mm
Components > 100mm should be +/- 1.5mm
Stepped check should be +/- 1.5mm
Sloped Opening sizes are +/-2mm


Nailing:
30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.

Manufacturing Tolerances:
Length ±3 · Height ±2 · Diagonals ±5 · Openings 0/+5 (mm).
Do not scale — work to figured dimensions. All dims in mm.

Breather Membrane:
Laps 100mm horizontal / 150mm vertical, upper lapping lower.

Panel Changes:
When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.

KEY PLAN






Revisions (Rev · Date · Note):

C01 - Construction issue

Date:	2026-09-13	Scale:	1:20	Drawn:	TS	Checked:	
Project Name:	MP Adams Plot 3, Eckington						
Site:	Eckington			Client:	MP Adams		
Title:	Panel Fabrication — 38 x 140 C16 CLS						
Project Number:	P3			Revision:	C01		
Panel No:	GF-EX19			Drawing No:	P3-MF-GF-EX19		
Panel L×H×T:	2400×2386×149			Weight:	93 kg		
Status:	CONSTRUCTION			Sheet:	1 / 1		

Nailing: OSB/Ply racking: 150mm perimeter / 300mm field nails (EC5 §9.2.4, 2:1 panel h:b)

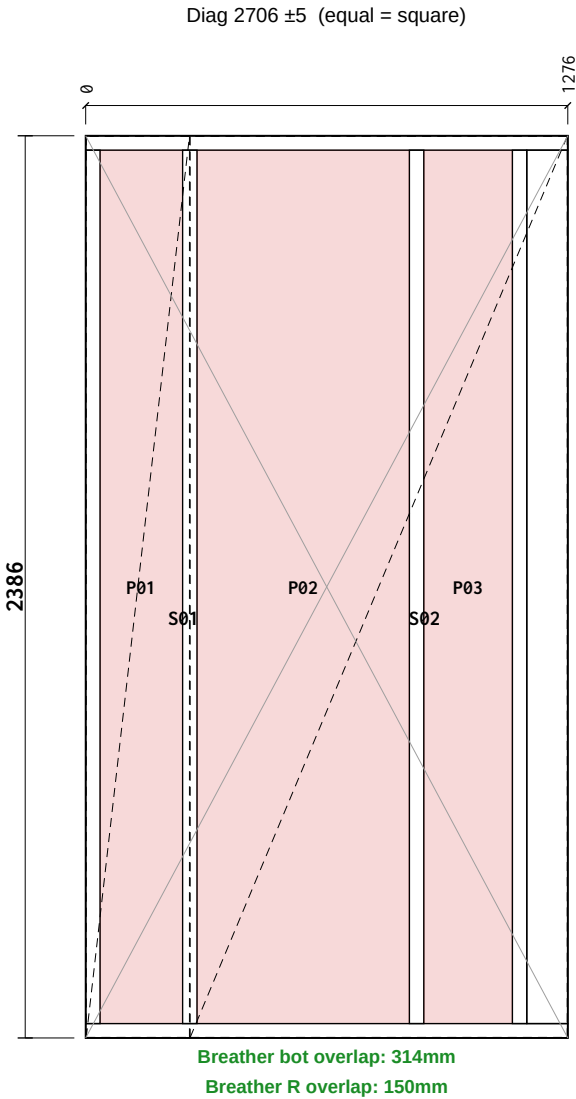

Cut List

Item	Section	Len	Bot°	Top°	Qty
BR1 Bottom Rail	38×140 C16	1275	0	0	1
TR1 Top Rail	38×140 C16	1275	0	0	1
ES1 End Stud	38×140 C16	2310	0	0	1
ES2 End Stud	38×140 C16	2310	0	0	1
VS1 Vertical Stud	38×140 C16	2310	0	0	2
JS1 Junction Stud	38×109 C16	2310	0	0	1
Total: 7 pcs / 14.10 m					

Sheathing & Insulation

Material	W	H	Label
OSB 9mm	273	2383	S01
OSB 9mm	997	2383	S02
PIR 120mm	218	2310	P01
PIR 120mm	561	2310	P02
PIR 120mm	233	2310	P03

General Notes:

Frame Nailing:
140mm Frames Nail Using 3no, 3.1×90mm length field galvanised twisted strip nails
90mm Frames Nail Using 2no, 3.1×90mm length field galvanised twisted strip nails

Sheathing Nails:
Components ≤ 100mm should be +/- 1mm
Components > 100mm should be +/- 1.5mm
Stepped check should be +/- 1.5mm
Sloped Opening sizes are +/-2mm


Nailing:
30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.

Manufacturing Tolerances:
Length ±3 · Height ±2 · Diagonals ±5 · Openings 0/+5 (mm).
Do not scale — work to figured dimensions. All dims in mm.

Breather Membrane:
Laps 100mm horizontal / 150mm vertical, upper lapping lower.



Panel Changes:
When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.

KEY PLAN



Revisions (Rev · Date · Note):		C01 - Construction issue					
Date:	2026-09-13	Scale:	1:20	Drawn:	TS	Checked:	
Project Name:		MP Adams Plot 3, Eckington					
Site:	Eckington			Client:	MP Adams		
Title:	Panel Fabrication — 38 x 140 C16 CLS						
Project Number:	P3			Revision:	C01		
Panel No:	GF-EX20			Drawing No:	P3-MF-GF-EX20		
Panel L×H×T:	1275×2386×149			Weight:	57 kg		
Status:	CONSTRUCTION			Sheet:	1 / 1		

Nailing: OSB/Ply racking: 150mm perimeter / 300mm field nails (EC5 §9.2.4, 2:1 panel h:b)

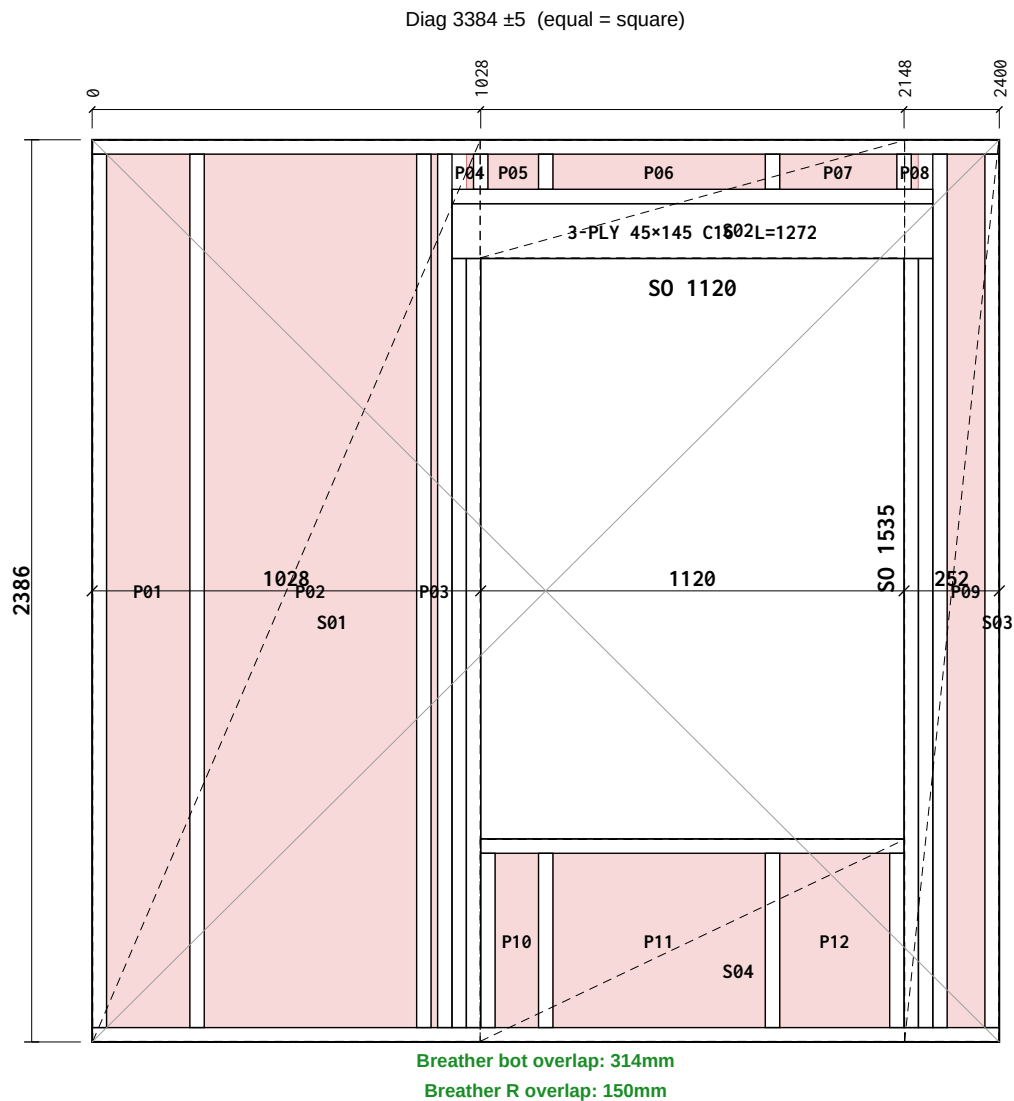


Cut List

Item	Section	Len	Bot°	Top° Qty
BR1 Bottom Rail	38×140 C16	2400	0	0 1
TR1 Top Rail	38×140 C16	2400	0	0 1
TR2 Top Rail	38×140 C16	1272	0	0 1
ES1 End Stud	38×140 C16	2310	0	0 1
ES2 End Stud	38×140 C16	2310	0	0 1
KS1 Vertical Stud	38×140 C16	2310	0	0 2
CS1 Cripple Stud	38×140 C16	2034	0	0 4
SP1 Sill Plate	38×140 C16	1120	0	0 1
LP1 Lintel Ply	1272×45 C16	1272	0	0 3
SS1 Sill Support	38×140 C16	461	0	0 2
OS1 OSB Support	38×140 C16	93	0	0 2
VS1 Vertical Stud	38×140 C16	2310	0	0 2
VS2 Vertical Stud	38×140 C16	461	0	0 2
VS3 Vertical Stud	38×140 C16	93	0	0 2

Sheathing & Insulation

Material	W	H	Label
OSB 9mm	1025	2383	S01
OSB 9mm	1123	311	S02
OSB 9mm	249	2383	S03
OSB 9mm	1123	534	S04
PIR 120mm	220	2310	P01
PIR 120mm	561	2310	P02
PIR 120mm	16	2310	P03
PIR 120mm	18	93	P04
PIR 120mm	133	93	P05
PIR 120mm	561	93	P06
PIR 120mm	309	93	P07
PIR 120mm	18	93	P08
PIR 120mm	99	2310	P09
PIR 120mm	114	460	P10
PIR 120mm	561	460	P11
PIR 120mm	290	460	P12

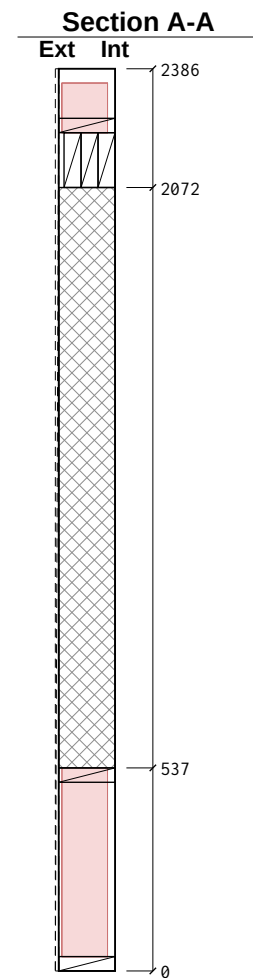

General Notes:

Frame Nailing:

140mm Frames Nail Using 3no, 3.1×90mm length field galvanised twisted strip nails
90mm Frames Nail Using 2no, 3.1×90mm length field galvanised twisted strip nails

Sheathing Nails:

Components $\leq 100\text{mm}$ should be $\pm 1\text{mm}$
 Components $> 100\text{mm}$ should be $\pm 1.5\text{mm}$
 Stepped check should be $\pm 1.5\text{mm}$
 Sloped Opening sizes are $\pm 2\text{mm}$

Nailing:

30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.

Manufacturing Tolerances:

Length ± 3 · Height ± 2 · Diagonals ± 5 · Openings 0/+5 (mm).
Do not scale — work to figured dimensions. All dims in mm.


Breather Membrane:

Laps 100mm horizontal / 150mm vertical, upper lapping lower.

Panel Changes:

When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.

KEY PLAN




Revisions (Rev · Date · Note):

C01 - Construction issue



Date:	2026-09-13	Scale:	1:20	Drawn:	TS	Checked:	
Project Name:		MP Adams Plot 3, Eckington					
Site:	Eckington			Client:	MP Adams		
Title:		Panel Fabrication — 38 x 140 C16 CLS					
Project Number:	P3			Revision:	C01		
Panel No:	GF-EX21			Drawing No:	P3-MF-GF-EX21		
Panel LxHxT:	2400x2386x149			Weight:	113 kg		
Status:	CONSTRUCTION			Sheet:	1 / 1		

Nailing: OSB/Ply racking: 150mm perimeter / 300mm field nails (EC5 §9.2.4, 2:1 panel h:b)

Diag 2414 ±5 (equal = square)



Breather bot overlap: 314mm
Breather R overlap: 150mm



Cut List

Item	Section	Len	Bot°	Top°	Qty
BR1 Bottom Rail	38×140 C16	360	0	0	1
TR1 Top Rail	38×140 C16	360	0	0	1
ES1 End Stud	38×140 C16	2310	0	0	1
ES2 End Stud	38×140 C16	2310	0	0	1
JS1 Junction Stud	38×140 C16	2310	0	0	1
Total: 5 pcs / 7.65 m					
Sheathing & Insulation					
Material		W	H	Label	
OSB 9mm		357	2383	S01	
PIR 100mm		140	2310	P01	
PIR 120mm		144	2310	P02	
OSB End Cap 9mm		146	2383	E01	

General Notes:

Frame Nailing:
140mm Frames Nail Using 3no, 3.1×90mm length field galvanised twisted strip nails
90mm Frames Nail Using 2no, 3.1×90mm length field galvanised twisted strip nails

Sheathing Nails:
Components ≤ 100mm should be +/- 1mm
Components > 100mm should be +/- 1.5mm
Stepped check should be +/- 1.5mm
Sloped Opening sizes are +/-2mm


Nailing:
30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.

Manufacturing Tolerances:
Length ±3 · Height ±2 · Diagonals ±5 · Openings 0/+5 (mm).
Do not scale — work to figured dimensions. All dims in mm.

Breather Membrane:
Laps 100mm horizontal / 150mm vertical, upper lapping lower.

Panel Changes:
When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.

KEY PLAN



Revisions (Rev · Date · Note):		C01 - Construction issue					
Date:	2026-09-13	Scale:	1:20	Drawn:	TS	Checked:	
Project Name:		MP Adams Plot 3, Eckington					
Site:	Eckington			Client:	MP Adams		
Title:	Panel Fabrication — 38 x 140 C16 CLS						
Project Number:	P3			Revision:	C01		
Panel No:	GF-EX22			Drawing No:	P3-MF-GF-EX22		
Panel L×H×T:	369×2386×149			Weight:	26 kg		
Status:	CONSTRUCTION			Sheet:	1 / 1		
