


Nailing: OSB/Ply racking: 150mm perimeter / 300mm field nails (EC5 §9.2.4, 2:1 panel h:b)



Cut List

Item	Section	Len	Bot°	Top°	Qty
BR1 Bottom Rail	38×140 C16	2400	0	0	1
TR1 Top Rail	38×140 C16	2400	0	0	1
ES1 End Stud	38×140 C16	2264	0	0	1
ES2 End Stud	38×140 C16	2264	0	0	1
VS1 Vertical Stud	38×140 C16	2264	0	0	4
Total: 8 pcs / 18.38 m					
Sheathing & Insulation					
Material		W	H	Label	
OSB 9mm		413	2337	S01	
OSB 9mm		1197	2337	S02	
OSB 9mm		782	2337	S03	
PIR 120mm		357	2264	P01	
PIR 120mm		561	2264	P02	
PIR 120mm		561	2264	P03	
PIR 120mm		561	2264	P04	
PIR 120mm		127	2264	P05	

General Notes:

Frame Nailing:
140mm Frames Nail Using 3no, 3.1×90mm length field galvanised twisted strip nails
90mm Frames Nail Using 2no, 3.1×90mm length field galvanised twisted strip nails

Sheathing Nails:
Components ≤ 100mm should be +/- 1mm
Components > 100mm should be +/- 1.5mm
Stepped check should be +/- 1.5mm
Sloped Opening sizes are +/-2mm


Nailing:
30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.

Manufacturing Tolerances:
Length ±3 · Height ±2 · Diagonals ±5 · Openings 0/+5 (mm).
Do not scale — work to figured dimensions. All dims in mm.

Breather Membrane:
Laps 100mm horizontal / 150mm vertical, upper lapping lower.




Panel Changes:
When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.

KEY PLAN



Revisions (Rev · Date · Note):		C01 - Construction issue					
Date:	2026-09-13	Scale:	1:20	Drawn:	TS	Checked:	
Project Name:		MP Adams Plot 3, Eckington					
Site:	Eckington			Client:	MP Adams		
Title:	Panel Fabrication — 38 x 140 C16 CLS						
Project Number:	P3			Revision:	C01		
Panel No:	FF-EX1			Drawing No:	P3-MF-FF-EX1		
Panel L×H×T:	2400×2340×149			Weight:	92 kg		
Status:	CONSTRUCTION			Sheet:	1 / 1		

Nailing: OSB/Ply racking: 150mm perimeter / 300mm field nails (EC5 §9.2.4, 2:1 panel h:b)

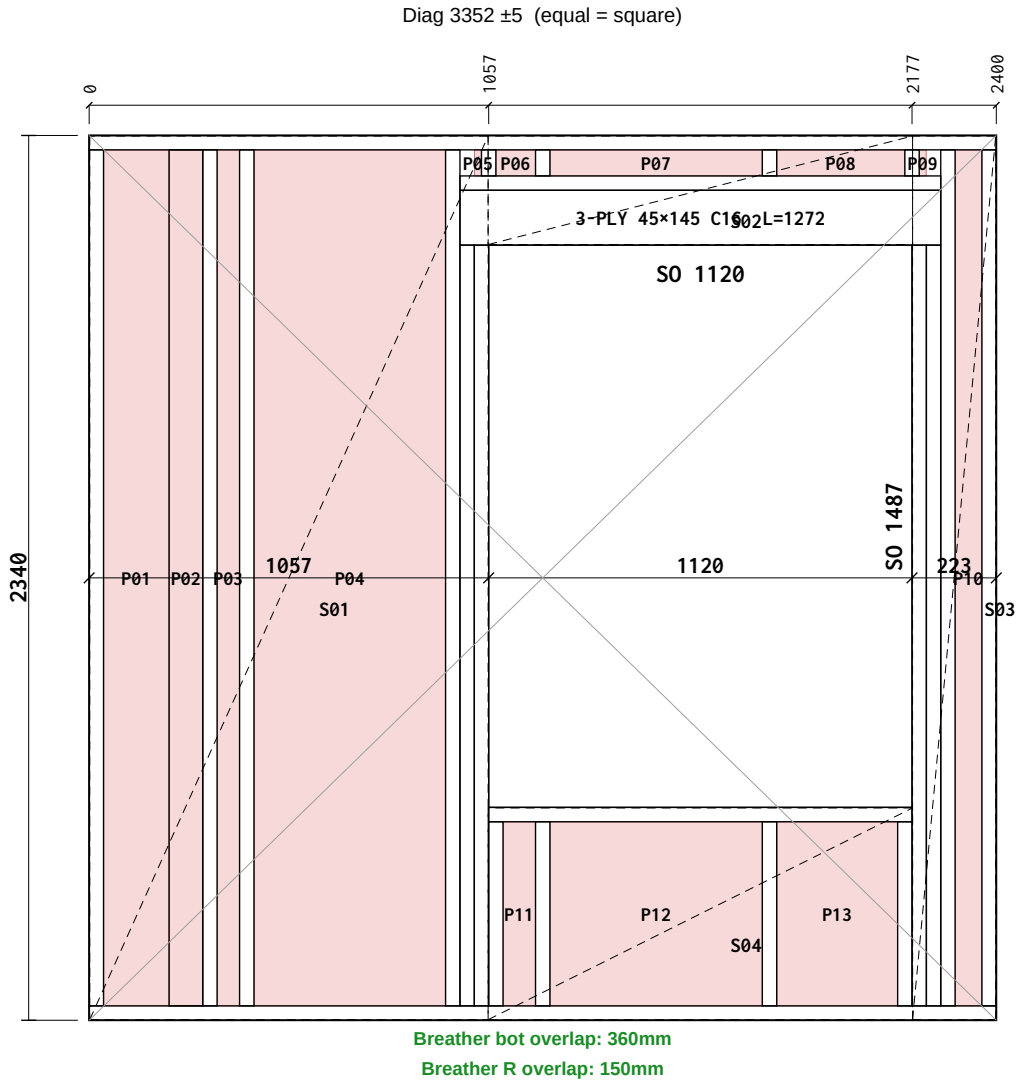

Cut List

Item	Section	Len	Bot°	Top°	Qty
BR1 Bottom Rail	38×140 C16	2400	0	0	1
TR1 Top Rail	38×140 C16	2400	0	0	1
TR2 Top Rail	38×140 C16	1272	0	0	1
ES1 End Stud	38×140 C16	2264	0	0	1
ES2 End Stud	38×140 C16	2264	0	0	1
KS1 Vertical Stud	38×140 C16	2264	0	0	2
CS1 Cripple Stud	38×140 C16	2012	0	0	4
SP1 Sill Plate	38×140 C16	1120	0	0	1
LP1 Lintel Ply	1272×45 C16	1272	0	0	3
SS1 Sill Support	38×140 C16	487	0	0	2
OS1 OSB Support	38×140 C16	69	0	0	2
VS1 Vertical Stud	38×140 C16	2264	0	0	2
VS2 Vertical Stud	38×140 C16	487	0	0	2
VS3 Vertical Stud	38×140 C16	69	0	0	2
JS1 Junction Stud	38×89 C16	2264	0	0	1

Total: 26 pcs / 37.13 m

Sheathing & Insulation

Material	W	H	Label
OSB 9mm	1054	2337	S01
OSB 9mm	1123	287	S02
OSB 9mm	220	2337	S03
OSB 9mm	1123	560	S04
PIR 120mm	173	2264	P01
PIR 100mm	88	2264	P02
PIR 120mm	59	2264	P03
PIR 120mm	505	2264	P04
PIR 120mm	18	69	P05
PIR 120mm	104	69	P06
PIR 120mm	561	69	P07
PIR 120mm	338	69	P08
PIR 120mm	18	69	P09
PIR 120mm	70	2264	P10
PIR 120mm	85	487	P11
PIR 120mm	561	487	P12
PIR 120mm	319	487	P13

General Notes:

Frame Nailing:
140mm Frames Nail Using 3no, 3.1×90mm length field galvanised twisted strip nails
90mm Frames Nail Using 2no, 3.1×90mm length field galvanised twisted strip nails

Sheathing Nails:
Components ≤ 100mm should be +/- 1mm
Components > 100mm should be +/- 1.5mm
Stepped check should be +/- 1.5mm
Sloped Opening sizes are +/-2mm


Nailing:
30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.

Manufacturing Tolerances:
Length ±3 · Height ±2 · Diagonals ±5 · Openings 0/+5 (mm).
Do not scale — work to figured dimensions. All dims in mm.

Breather Membrane:
Laps 100mm horizontal / 150mm vertical, upper lapping lower.

Panel Changes:
When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.

KEY PLAN


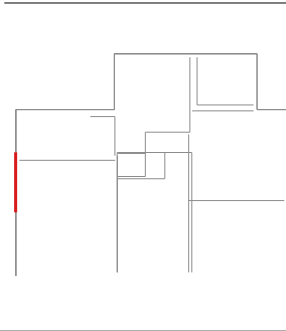


Revisions (Rev · Date · Note):


C01 - Construction issue

Date:	2026-09-13	Scale:	1:20	Drawn:	TS	Checked:	
Project Name: MP Adams Plot 3, Eckington							
Site: Eckington				Client: MP Adams			
Title: Panel Fabrication — 38 x 140 C16 CLS							
Project Number: P3				Revision: C01			
Panel No: FF-EX2				Drawing No: P3-MF-FF-EX2			
Panel L×H×T: 2400×2340×149				Weight: 115 kg			
Status: CONSTRUCTION				Sheet: 1 / 1			

Nailing: OSB/Ply racking: 150mm perimeter / 300mm field nails (EC5 §9.2.4, 2:1 panel h:b)

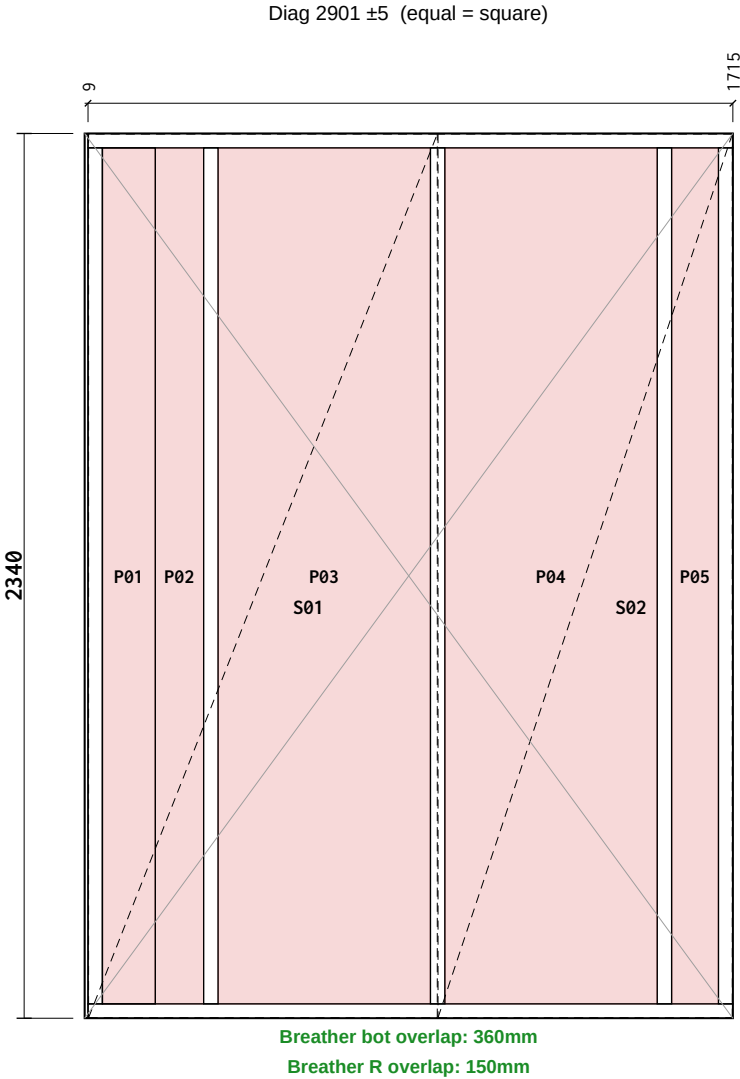

Section A-A



Cut List

Item	Section	Len	Bot°	Top°	Qty
BR1 Bottom Rail	38×140 C16	1706	0	0	1
TR1 Top Rail	38×140 C16	1706	0	0	1
ES1 End Stud	38×140 C16	2264	0	0	1
ES2 End Stud	38×140 C16	2264	0	0	1
VS1 Vertical Stud	38×140 C16	2264	0	0	3
JS1 Junction Stud	38×140 C16	2264	0	0	1
Total: 8 pcs / 17.00 m					

Sheathing & Insulation

Material	W	HLabel
OSB 9mm	923	2337 S01
OSB 9mm	778	2337 S02
PIR 100mm	140	2263 P01
PIR 120mm	128	2263 P02
PIR 120mm	561	2263 P03
PIR 120mm	561	2263 P04
PIR 120mm	123	2263 P05
OSB End Cap 9mm	146	2337 E01

General Notes:

Frame Nailing:
140mm Frames Nail Using 3no, 3.1×90mm length field galvanised twisted strip nails
90mm Frames Nail Using 2no, 3.1×90mm length field galvanised twisted strip nails

Sheathing Nails:
Components ≤ 100mm should be +/- 1mm
Components > 100mm should be +/- 1.5mm
Stepped check should be +/- 1.5mm
Sloped Opening sizes are +/-2mm


Nailing:
30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.

Manufacturing Tolerances:
Length ±3 · Height ±2 · Diagonals ±5 · Openings 0/+5 (mm).
Do not scale — work to figured dimensions. All dims in mm.

Breather Membrane:
Laps 100mm horizontal / 150mm vertical, upper lapping lower.

Panel Changes:
When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.


KEY PLAN




Revisions (Rev · Date · Note):		C01 - Construction issue					
Date:	2026-09-13	Scale:	1:20	Drawn:	TS	Checked:	
Project Name:		MP Adams Plot 3, Eckington					
Site:	Eckington			Client:	MP Adams		
Title:	Panel Fabrication — 38 x 140 C16 CLS						
Project Number:	P3			Revision:	C01		
Panel No:	FF-EX3			Drawing No:	P3-MF-FF-EX3		
Panel L×H×T:	1715×2340×149			Weight:	76 kg		
Status:	CONSTRUCTION			Sheet:	1 / 1		

Nailing: OSB/Ply racking: 150mm perimeter / 300mm field nails (EC5 §9.2.4, 2:1 panel h:b)


Diag 2363 ±5 (equal = square)



Breather bot overlap: 360mm
Breather R overlap: 150mm



Section A-A



Cut List

Item	Section	Len	Bot°	Top°	Qty
BR1 Bottom Rail	38×140 C16	323	0	0	1
TR1 Top Rail	38×140 C16	323	0	0	1
ES1 End Stud	38×140 C16	2264	0	0	1
ES2 End Stud	38×140 C16	2264	0	0	1
JS1 Junction Stud	38×140 C16	2264	0	0	1
Total: 5 pcs / 7.44 m					
Sheathing & Insulation					
Material		W	H	Label	
OSB 9mm		320	2337	S01	
PIR 100mm		140	2264	P01	
PIR 120mm		106	2264	P02	
OSB End Cap 9mm		146	2337	E01	

General Notes:

Frame Nailing:
140mm Frames Nail Using 3no, 3.1×90mm length field galvanised twisted strip nails
90mm Frames Nail Using 2no, 3.1×90mm length field galvanised twisted strip nails

Sheathing Nails:
Components ≤ 100mm should be +/- 1mm
Components > 100mm should be +/- 1.5mm
Stepped check should be +/- 1.5mm
Sloped Opening sizes are +/-2mm


Nailing:
30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.

Manufacturing Tolerances:
Length ±3 · Height ±2 · Diagonals ±5 · Openings 0/+5 (mm).
Do not scale — work to figured dimensions. All dims in mm.

Breather Membrane:
Laps 100mm horizontal / 150mm vertical, upper lapping lower.




Panel Changes:
When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.

KEY PLAN



Revisions (Rev · Date · Note):		C01 - Construction issue					
Date:	2026-09-13	Scale:	1:20	Drawn:	TS	Checked:	
Project Name:		MP Adams Plot 3, Eckington					
Site:	Eckington			Client:	MP Adams		
Title:	Panel Fabrication — 38 x 140 C16 CLS						
Project Number:	P3			Revision:	C01		
Panel No:	FF-EX4			Drawing No:	P3-MF-FF-EX4		
Panel L×H×T:	332×2340×149			Weight:	25 kg		
Status:	CONSTRUCTION			Sheet:	1 / 1		

Nailing: OSB/Ply racking: 150mm perimeter / 300mm field nails (EC5 §9.2.4, 2:1 panel h:b)

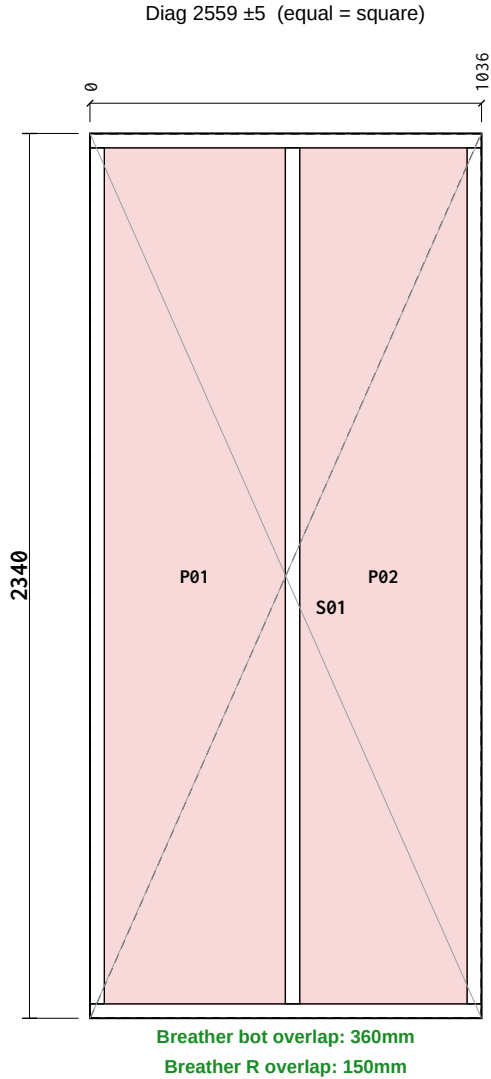

Cut List

Item	Section	Len	Bot°	Top°	Qty
BR1 Bottom Rail	38×140 C16	1036	0	0	1
TR1 Top Rail	38×140 C16	1036	0	0	1
ES1 End Stud	38×140 C16	2264	0	0	1
ES2 End Stud	38×140 C16	2264	0	0	1
VS1 Vertical Stud	38×140 C16	2264	0	0	1
Total: 5 pcs / 8.86 m					

Sheathing & Insulation

Material	W	H	Label
OSB 9mm	1033	2337	S01
PIR 120mm	478	2264	P01
PIR 120mm	442	2264	P02

General Notes:

Frame Nailing:
140mm Frames Nail Using 3no, 3.1×90mm length field galvanised twisted strip nails
90mm Frames Nail Using 2no, 3.1×90mm length field galvanised twisted strip nails

Sheathing Nails:
Components ≤ 100mm should be +/- 1mm
Components > 100mm should be +/- 1.5mm
Stepped check should be +/- 1.5mm
Sloped Opening sizes are +/-2mm


Nailing:
30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.

Manufacturing Tolerances:
Length ±3 · Height ±2 · Diagonals ±5 · Openings 0/+5 (mm).
Do not scale — work to figured dimensions. All dims in mm.

Breather Membrane:
Laps 100mm horizontal / 150mm vertical, upper lapping lower.




Panel Changes:
When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.

KEY PLAN



Revisions (Rev · Date · Note):		C01 - Construction issue					
Date:	2026-09-13	Scale:	1:20	Drawn:	TS	Checked:	
Project Name:		MP Adams Plot 3, Eckington					
Site:	Eckington			Client:	MP Adams		
Title:	Panel Fabrication — 38 x 140 C16 CLS						
Project Number:	P3			Revision:	C01		
Panel No:	FF-EX5			Drawing No:	P3-MF-FF-EX5		
Panel L×H×T:	1036×2340×149			Weight:	42 kg		
Status:	CONSTRUCTION			Sheet:	1 / 1		

Nailing: OSB/Ply racking: 150mm perimeter / 300mm field nails (EC5 §9.2.4, 2:1 panel h:b)

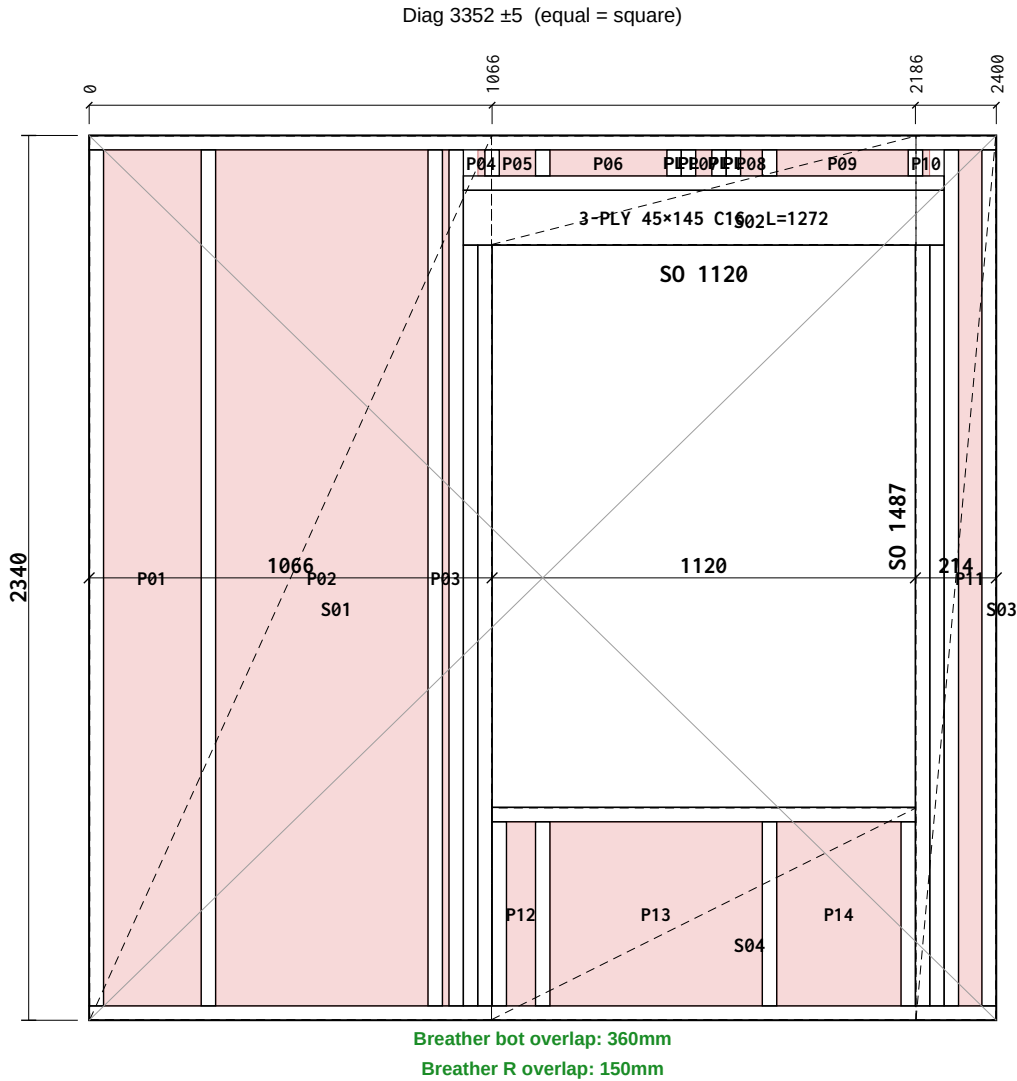

Cut List

Item	Section	Len	Bot°	Top°	Qty
BR1 Bottom Rail	38×140 C16	2400	0	0	1
TR1 Top Rail	38×140 C16	2400	0	0	1
TR2 Top Rail	38×140 C16	1272	0	0	1
ES1 End Stud	38×140 C16	2264	0	0	1
ES2 End Stud	38×140 C16	2264	0	0	1
KS1 Vertical Stud	38×140 C16	2264	0	0	2
CS1 Cripple Stud	38×140 C16	2012	0	0	4
SP1 Sill Plate	38×140 C16	1120	0	0	1
LP1 Lintel Ply	1272×45 C16	1272	0	0	3
SS1 Sill Support	38×140 C16	487	0	0	2
OS1 OSB Support	38×140 C16	69	0	0	2
VS1 Vertical Stud	38×140 C16	2264	0	0	2
VS2 Vertical Stud	38×140 C16	487	0	0	2
VS3 Vertical Stud	38×140 C16	69	0	0	2

Total: 25 pcs / 34.86 m

Sheathing & Insulation

Material	W	H	Label
OSB 9mm	1063	2337	S01
OSB 9mm	1123	287	S02
OSB 9mm	211	2337	S03
OSB 9mm	1123	560	S04
PIR 120mm	258	2264	P01
PIR 120mm	561	2264	P02
PIR 120mm	16	2264	P03
PIR 120mm	18	69	P04
PIR 120mm	95	69	P05
PIR 120mm	309	69	P06
PIR 120mm	42	69	P07
PIR 120mm	57	69	P08
PIR 120mm	347	69	P09
PIR 120mm	18	69	P10
PIR 120mm	61	2264	P11
PIR 120mm	76	487	P12
PIR 120mm	561	487	P13
PIR 120mm	328	487	P14

General Notes:

Frame Nailing:
140mm Frames Nail Using 3no, 3.1×90mm length field galvanised twisted strip nails
90mm Frames Nail Using 2no, 3.1×90mm length field galvanised twisted strip nails

Sheathing Nails:
Components ≤ 100mm should be +/- 1mm
Components > 100mm should be +/- 1.5mm
Stepped check should be +/- 1.5mm
Sloped Opening sizes are +/-2mm


Nailing:
30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.

Manufacturing Tolerances:
Length ±3 · Height ±2 · Diagonals ±5 · Openings 0/+5 (mm).
Do not scale — work to figured dimensions. All dims in mm.

Breather Membrane:
Laps 100mm horizontal / 150mm vertical, upper lapping lower.

Panel Changes:
When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.

KEY PLAN



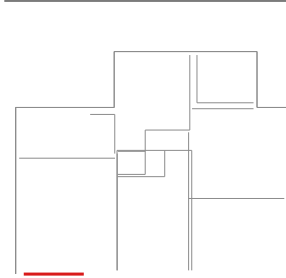


Revisions (Rev · Date · Note):

C01 - Construction issue

Date:	2026-09-13	Scale:	1:20	Drawn:	TS	Checked:	
Project Name: MP Adams Plot 3, Eckington							
Site: Eckington				Client: MP Adams			
Title: Panel Fabrication — 38 x 140 C16 CLS							
Project Number: P3				Revision: C01			
Panel No: FF-EX6				Drawing No: P3-MF-FF-EX6			
Panel L×H×T: 2400×2340×149				Weight: 112 kg			
Status: CONSTRUCTION				Sheet: 1 / 1			

Nailing: OSB/Ply racking: 150mm perimeter / 300mm field nails (EC5 §9.2.4, 2:1 panel h:b)

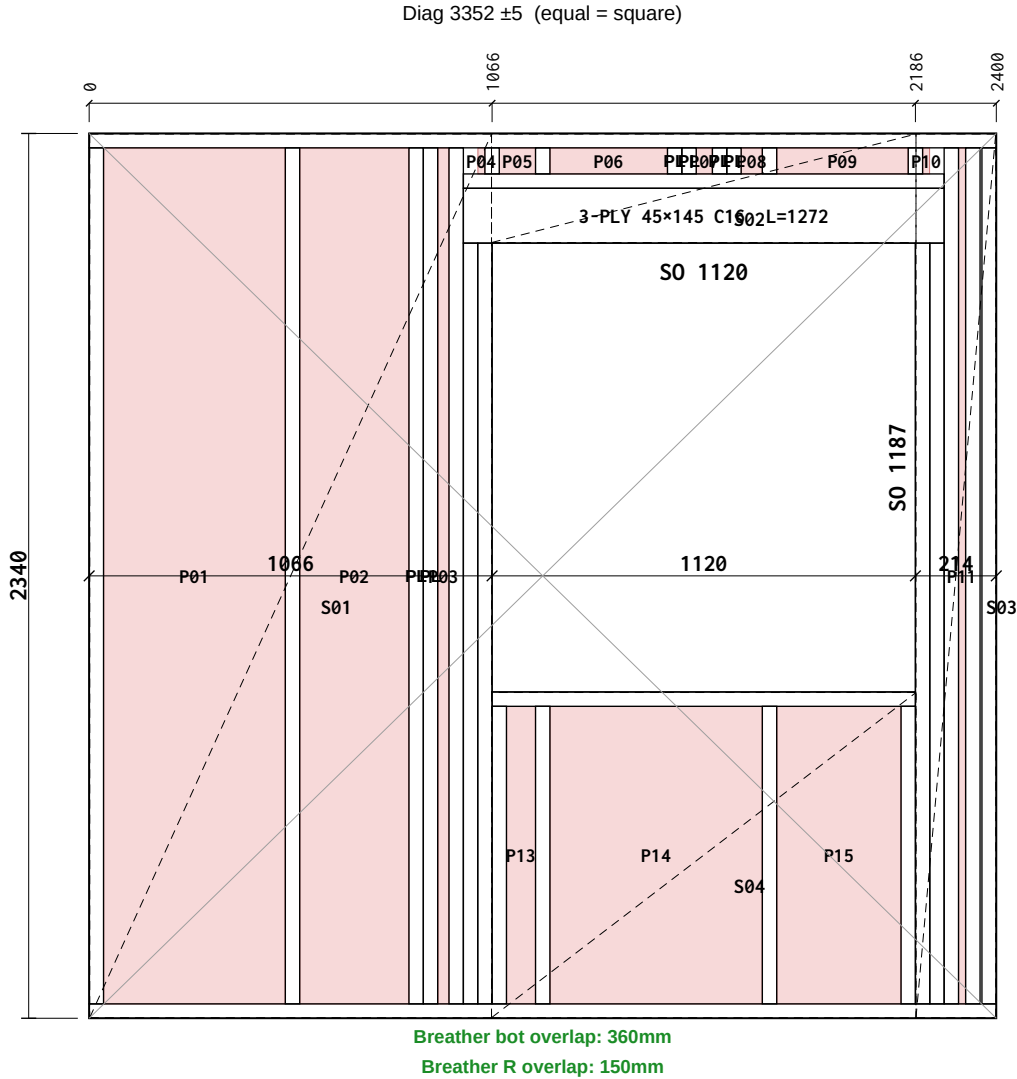

Cut List

Item		Section	Len	Bot°	Top°	Qty
BR1	Bottom Rail	38×140 C16	2400	0	0	1
TR1	Top Rail	38×140 C16	2400	0	0	1
TR2	Top Rail	38×140 C16	1272	0	0	1
ES1	End Stud	38×140 C16	2264	0	0	1
ES2	End Stud	38×140 C16	2264	0	0	1
KS1	Vertical Stud	38×140 C16	2264	0	0	2
CS1	Cripple Stud	38×140 C16	2012	0	0	4
SP1	Sill Plate	38×140 C16	1120	0	0	1
LP1	Lintel Ply	1272×45 C16	1272	0	0	3
SS1	Sill Support	38×140 C16	787	0	0	2
OS1	OSB Support	38×140 C16	69	0	0	2
VS1	Vertical Stud	38×140 C16	2264	0	0	2
VS2	Vertical Stud	38×140 C16	787	0	0	2
VS3	Vertical Stud	38×140 C16	69	0	0	2

Total: 25 pcs / 36.06 m

Sheathing & Insulation

Material	W	H	Label
OSB 9mm	1063	2337	S01
OSB 9mm	1123	287	S02
OSB 9mm	211	2337	S03
OSB 9mm	1123	860	S04
PIR 120mm	480	2264	P01
PIR 120mm	288	2264	P02
PIR 120mm	28	2264	P03
PIR 120mm	18	69	P04
PIR 120mm	95	69	P05
PIR 120mm	310	69	P06
PIR 120mm	42	69	P07
PIR 120mm	55	69	P08
PIR 120mm	347	69	P09
PIR 120mm	18	69	P10
PIR 120mm	17	2264	P11
PIR 120mm	4	2264	P12
PIR 120mm	76	786	P13
PIR 120mm	561	786	P14
PIR 120mm	328	786	P15

General Notes:

Frame Nailing:
140mm Frames Nail Using 3no, 3.1×90mm length field galvanised twisted strip nails
90mm Frames Nail Using 2no, 3.1×90mm length field galvanised twisted strip nails

Sheathing Nails:
Components ≤ 100mm should be +/- 1mm
Components > 100mm should be +/- 1.5mm
Stepped check should be +/- 1.5mm
Sloped Opening sizes are +/-2mm


Nailing:
30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.

Manufacturing Tolerances:
Length ±3 · Height ±2 · Diagonals ±5 · Openings 0/+5 (mm).
Do not scale — work to figured dimensions. All dims in mm.

Breather Membrane:
Laps 100mm horizontal / 150mm vertical, upper lapping lower.

Panel Changes:
When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.

KEY PLAN


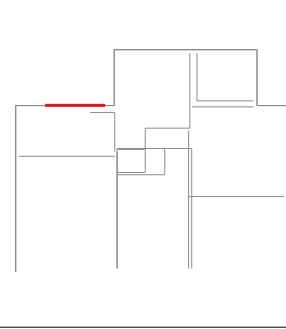


Revisions (Rev · Date · Note):


C01 - Construction issue

Date:	2026-09-13	Scale:	1:20	Drawn:	TS	Checked:	
Project Name:	MP Adams Plot 3, Eckington						
Site:	Eckington			Client:	MP Adams		
Title:	Panel Fabrication — 38 x 140 C16 CLS						
Project Number:	P3			Revision:	C01		
Panel No:	FF-EX7			Drawing No:	P3-MF-FF-EX7		
Panel L×H×T:	2400×2340×149			Weight:	117 kg		
Status:	CONSTRUCTION			Sheet:	1 / 1		

Nailing: OSB/Ply racking: 150mm perimeter / 300mm field nails (EC5 §9.2.4, 2:1 panel h:b)

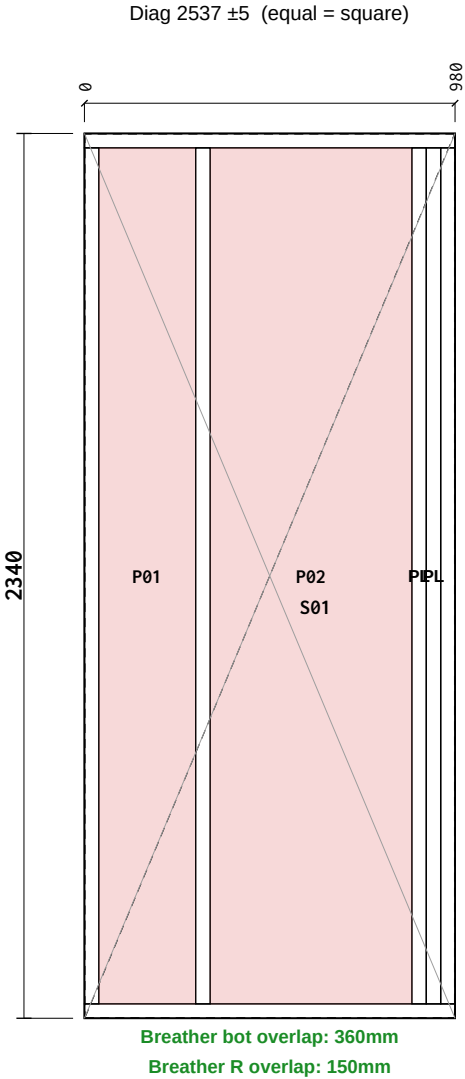

Section A-A



Cut List

Item	Section	Len	Bot°	Top°	Qty
BR1 Bottom Rail	38×140 C16	981	0	0	1
TR1 Top Rail	38×140 C16	981	0	0	1
ES1 End Stud	38×140 C16	2264	0	0	1
ES2 End Stud	38×140 C16	2264	0	0	1
VS1 Vertical Stud	38×140 C16	2264	0	0	1
Total: 5 pcs / 8.75 m					

Sheathing & Insulation

Material	W	H	Label
OSB 9mm	978	2337	S01
PIR 120mm	256	2264	P01
PIR 120mm	533	2264	P02

General Notes:

Frame Nailing:
140mm Frames Nail Using 3no, 3.1×90mm length field galvanised twisted strip nails
90mm Frames Nail Using 2no, 3.1×90mm length field galvanised twisted strip nails

Sheathing Nails:
Components ≤ 100mm should be +/- 1mm
Components > 100mm should be +/- 1.5mm
Stepped check should be +/- 1.5mm
Sloped Opening sizes are +/-2mm


Nailing:
30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.

Manufacturing Tolerances:
Length ±3 · Height ±2 · Diagonals ±5 · Openings 0/+5 (mm).
Do not scale — work to figured dimensions. All dims in mm.

Breather Membrane:
Laps 100mm horizontal / 150mm vertical, upper lapping lower.

Panel Changes:
When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.


KEY PLAN




Revisions (Rev · Date · Note):		C01 - Construction issue					
Date:	2026-09-13	Scale:	1:20	Drawn:	TS	Checked:	
Project Name:		MP Adams Plot 3, Eckington					
Site:	Eckington			Client:	MP Adams		
Title:	Panel Fabrication — 38 x 140 C16 CLS						
Project Number:	P3			Revision:	C01		
Panel No:	FF-EX8			Drawing No:	P3-MF-FF-EX8		
Panel L×H×T:	981×2340×149			Weight:	40 kg		
Status:	CONSTRUCTION			Sheet:	1 / 1		

Nailing: OSB/Ply racking: 150mm perimeter / 300mm field nails (EC5 §9.2.4, 2:1 panel h:b)


Diag 2393 ±5 (equal = square)

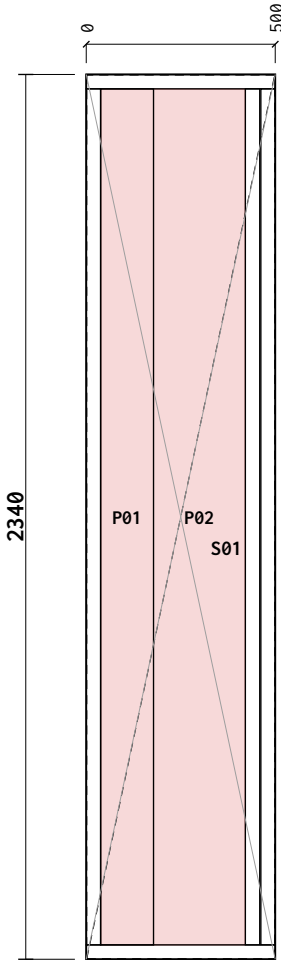

Breather bot overlap: 360mm
Breather R overlap: 150mm



Section A-A



Cut List

Item	Section	Len	Bot°	Top°	Qty
BR1 Bottom Rail	38×140 C16	500	0	0	1
TR1 Top Rail	38×140 C16	500	0	0	1
ES1 End Stud	38×140 C16	2264	0	0	1
ES2 End Stud	38×140 C16	2264	0	0	1
VS1 Vertical Stud	38×140 C16	2264	0	0	1
JS1 Junction Stud	38×140 C16	2264	0	0	1
Total: 6 pcs / 10.06 m					

Sheathing & Insulation

Material	W	H	Label
OSB 9mm	497	2337	S01
PIR 100mm	140	2264	P01
PIR 120mm	242	2264	P02
PIR 120mm	2	2264	P03

General Notes:

Frame Nailing:
140mm Frames Nail Using 3no, 3.1×90mm length field galvanised twisted strip nails
90mm Frames Nail Using 2no, 3.1×90mm length field galvanised twisted strip nails

Sheathing Nails:
Components ≤ 100mm should be +/- 1mm
Components > 100mm should be +/- 1.5mm
Stepped check should be +/- 1.5mm
Sloped Opening sizes are +/-2mm


Nailing:
30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.

Manufacturing Tolerances:
Length ±3 · Height ±2 · Diagonals ±5 · Openings 0/+5 (mm).
Do not scale — work to figured dimensions. All dims in mm.

Breather Membrane:
Laps 100mm horizontal / 150mm vertical, upper lapping lower.



Panel Changes:
When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.

KEY PLAN



Revisions (Rev · Date · Note):		C01 - Construction issue					
Date:	2026-09-13	Scale:	1:20	Drawn:	TS	Checked:	
Project Name:		MP Adams Plot 3, Eckington					
Site:	Eckington			Client:	MP Adams		
Title:	Panel Fabrication — 38 x 140 C16 CLS						
Project Number:	P3			Revision:	C01		
Panel No:	FF-EX9			Drawing No:	P3-MF-FF-EX9		
Panel L×H×T:	500×2340×149			Weight:	32 kg		
Status:	CONSTRUCTION			Sheet:	1 / 1		

Nailing: OSB/Ply racking: 150mm perimeter / 300mm field nails (EC5 §9.2.4, 2:1 panel h:b)

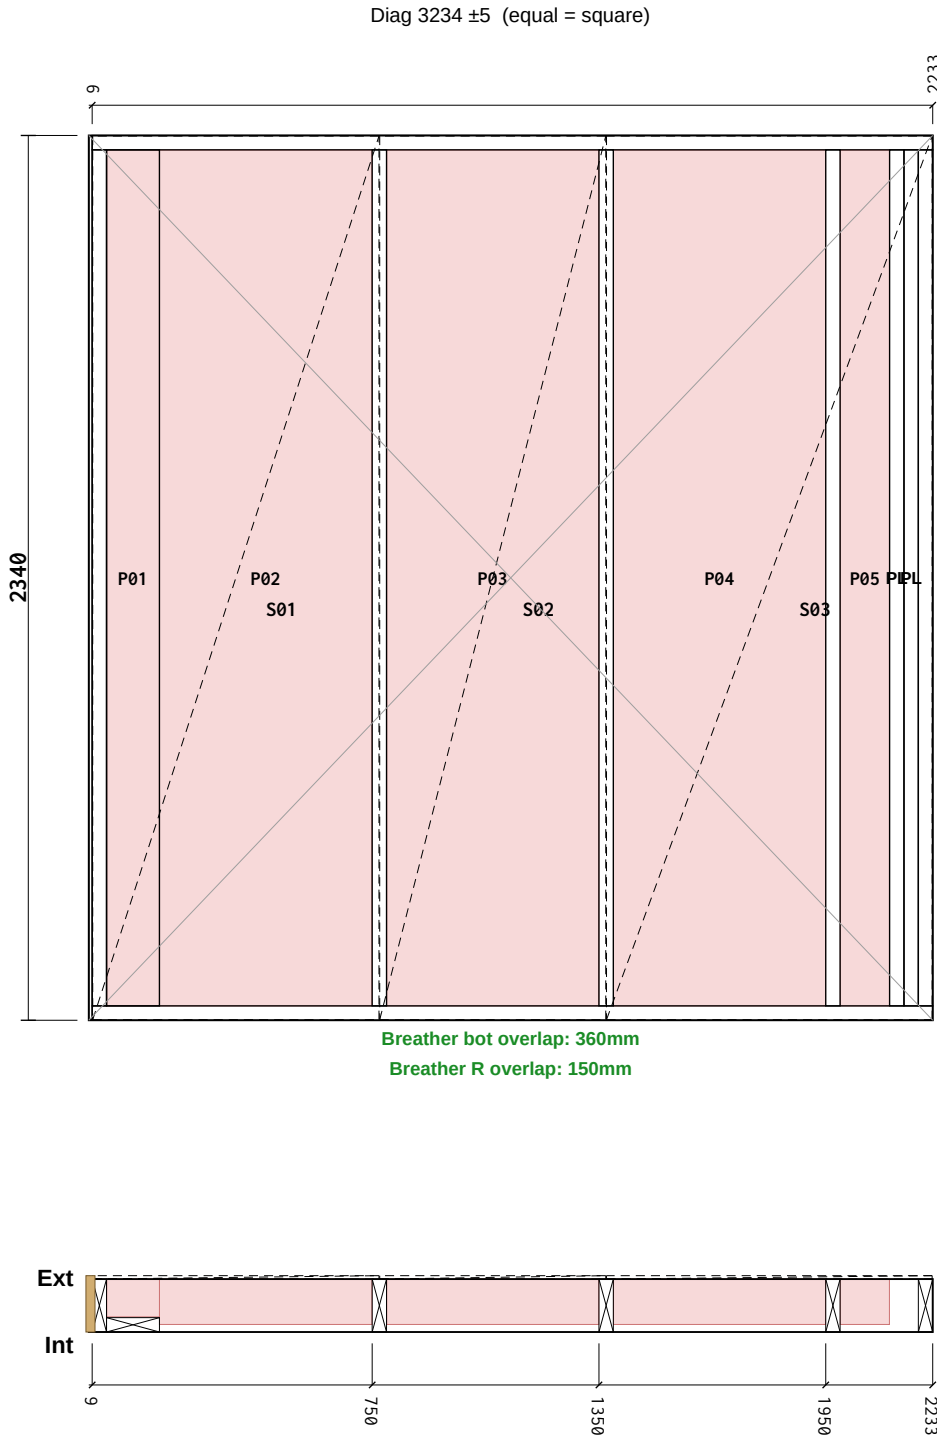

Cut List

Item	Section	Len	Bot°	Top°	Qty
BR1 Bottom Rail	38×140 C16	2224	0	0	1
TR1 Top Rail	38×140 C16	2224	0	0	1
ES1 End Stud	38×140 C16	2264	0	0	1
ES2 End Stud	38×140 C16	2264	0	0	1
VS1 Vertical Stud	38×140 C16	2264	0	0	3
JS1 Junction Stud	38×140 C16	2264	0	0	1
Total: 8 pcs / 18.03 m					

Sheathing & Insulation

Material	W	H	Label
OSB 9mm	757	2337	S01
OSB 9mm	598	2337	S02
OSB 9mm	861	2337	S03
PIR 100mm	140	2264	P01
PIR 120mm	562	2264	P02
PIR 120mm	561	2264	P03
PIR 120mm	561	2264	P04
PIR 120mm	130	2264	P05
OSB End Cap 9mm	146	2337	E01

General Notes:

Frame Nailing:
140mm Frames Nail Using 3no, 3.1×90mm length field galvanised twisted strip nails
90mm Frames Nail Using 2no, 3.1×90mm length field galvanised twisted strip nails

Sheathing Nails:
Components ≤ 100mm should be +/- 1mm
Components > 100mm should be +/- 1.5mm
Stepped check should be +/- 1.5mm
Sloped Opening sizes are +/-2mm


Nailing:
30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.

Manufacturing Tolerances:
Length ±3 · Height ±2 · Diagonals ±5 · Openings 0/+5 (mm).
Do not scale — work to figured dimensions. All dims in mm.

Breather Membrane:
Laps 100mm horizontal / 150mm vertical, upper lapping lower.



Panel Changes:
When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.

KEY PLAN



Revisions (Rev · Date · Note):		C01 - Construction issue					
Date:	2026-09-13	Scale:	1:20	Drawn:	TS	Checked:	
Project Name:		MP Adams Plot 3, Eckington					
Site:	Eckington			Client:	MP Adams		
Title:	Panel Fabrication — 38 x 140 C16 CLS						
Project Number:	P3			Revision:	C01		
Panel No:	FF-EX10			Drawing No:	P3-MF-FF-EX10		
Panel L×H×T:	2233×2340×149			Weight:	89 kg		
Status:	CONSTRUCTION			Sheet:	1 / 1		

Nailing: OSB/Ply racking: 150mm perimeter / 300mm field nails (EC5 §9.2.4, 2:1 panel h:b)

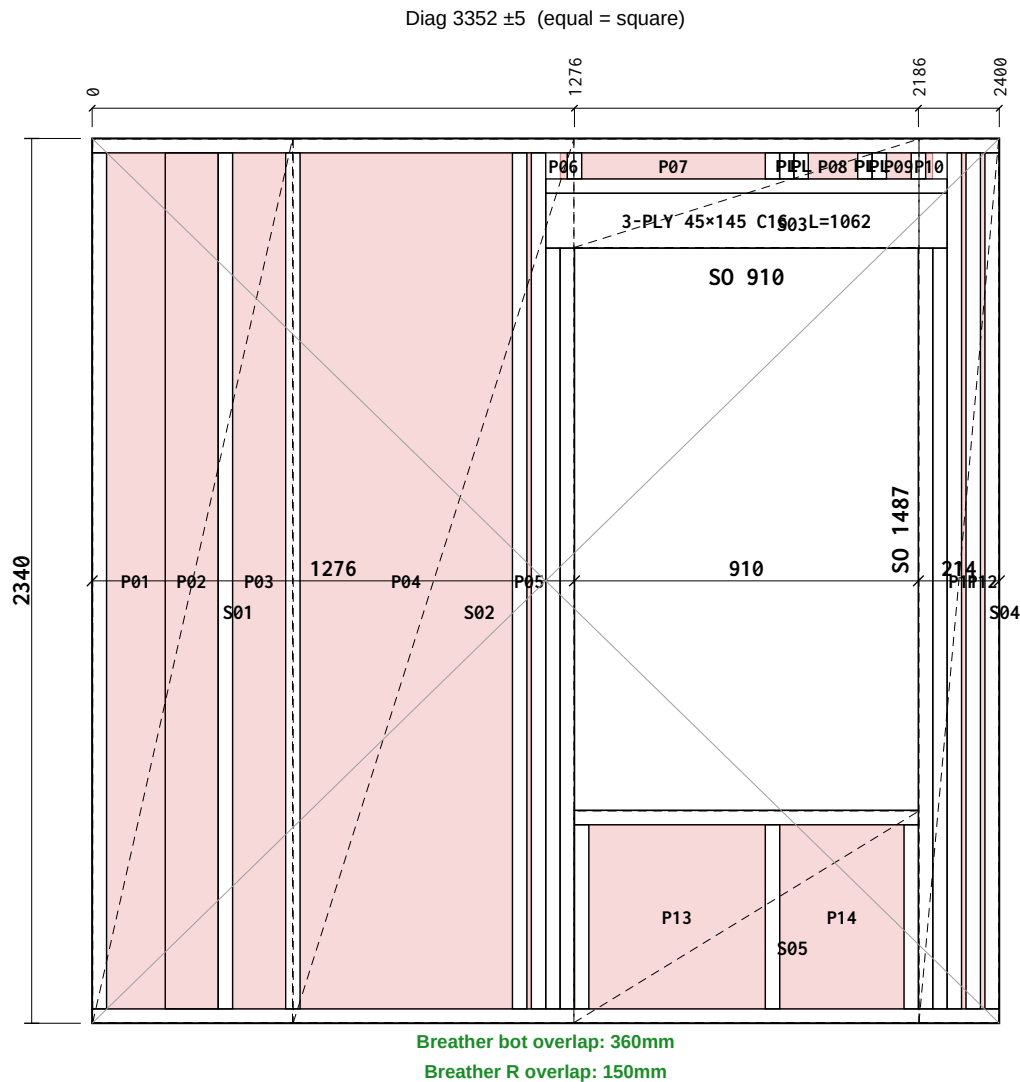


Cut List

Item	Section	Len	Bot*	Top*	Qty
BR1 Bottom Rail	38×140 C16	2400	0	0	1
TR1 Top Rail	38×140 C16	2400	0	0	1
TR2 Top Rail	38×140 C16	1062	0	0	1
ES1 End Stud	38×140 C16	2264	0	0	1
ES2 End Stud	38×140 C16	2264	0	0	1
KS1 Vertical Stud	38×140 C16	2264	0	0	2
CS1 Cripple Stud	38×140 C16	2012	0	0	4
SP1 Sill Plate	38×140 C16	910	0	0	1
LP1 Lintel Ply	1062×45 C16	1062	0	0	3
SS1 Sill Support	38×140 C16	487	0	0	2
OS1 OSB Support	38×140 C16	69	0	0	2
VS1 Vertical Stud	38×140 C16	2264	0	0	4
VS2 Vertical Stud	38×140 C16	487	0	0	1
VS3 Vertical Stud	38×140 C16	69	0	0	1
JS1 Junction Stud	38×140 C16	2264	0	0	1

Total: 26 pcs / 40.05 m

Sheathing & Insulation

Material	W	HLabel
OSB 9mm	529	2337 S01
OSB 9mm	742	2337 S02
OSB 9mm	913	287 S03
OSB 9mm	211	2337 S04
OSB 9mm	913	560 S05
PIR 120mm	155	2264 P01
PIR 100mm	140	2264 P02
PIR 120mm	140	2264 P03
PIR 120mm	561	2264 P04
PIR 120mm	10	2264 P05
PIR 120mm	18	69 P06
PIR 120mm	485	69 P07
PIR 120mm	130	69 P08
PIR 120mm	65	69 P09
PIR 120mm	18	69 P10
PIR 120mm	11	2264 P11
PIR 120mm	11	2264 P12
PIR 120mm	466	487 P13
PIR 120mm	328	487 P14

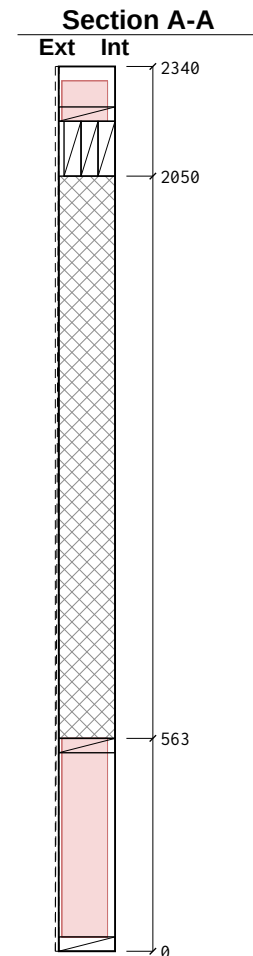

General Notes:

Frame Nailing:

140mm Frames Nail Using 3no, 3.1×90mm length field galvanised twisted strip nails
90mm Frames Nail Using 2no, 3.1×90mm length field galvanised twisted strip nails

Sheathing Nails:

Components $\leq 100\text{mm}$ should be $\pm 1\text{mm}$
 Components $> 100\text{mm}$ should be $\pm 1.5\text{mm}$
 Stepped check should be $\pm 1.5\text{mm}$
 Sloped Opening sizes are $\pm 2\text{mm}$

Nailing:

30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.

Manufacturing Tolerances:

Length ± 3 · Height ± 2 · Diagonals ± 5 · Openings 0/+5 (mm).
Do not scale — work to figured dimensions. All dims in mm.


Breather Membrane:

Laps 100mm horizontal / 150mm vertical, upper lapping lower.

Panel Changes:

When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.

KEY PLAN



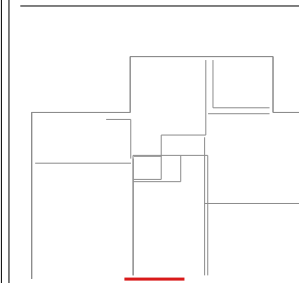


	Revisions (Rev · Date · Note):
--	--------------------------------

C01 - Construction issue

Date:	2026-09-13	Scale:	1:20	Drawn:	TS	Checked:	
Project Name:		MP Adams Plot 3, Eckington					
Site:		Eckington		Client:		MP Adams	
Title:		Panel Fabrication — 38 x 140 C16 CLS					
Project Number:		P3		Revision:		C01	
Panel No:		FF-EX11		Drawing No:		P3-MF-FF-EX11	
Panel L×H×T:		2400×2340×149		Weight:		126 kg	
Status:		CONSTRUCTION		Sheet:		1 / 1	

Nailing: OSB/Ply racking: 150mm perimeter / 300mm field nails (EC5 §9.2.4, 2:1 panel h:b)

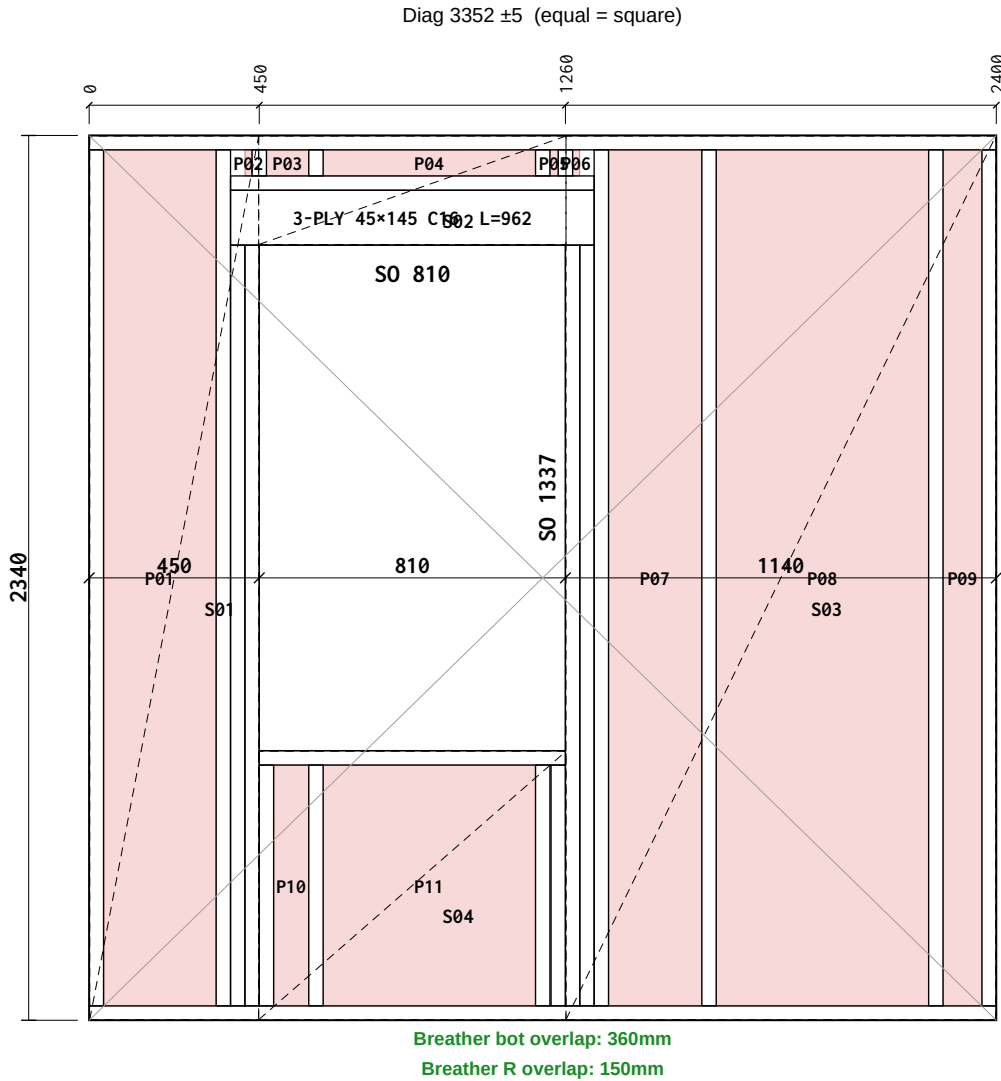

Cut List

Item	Section	Len	Bot°	Top°	Qty
BR1 Bottom Rail	38×140 C16	2400	0	0	1
TR1 Top Rail	38×140 C16	2400	0	0	1
TR2 Top Rail	38×140 C16	962	0	0	1
ES1 End Stud	38×140 C16	2264	0	0	1
ES2 End Stud	38×140 C16	2264	0	0	1
KS1 Vertical Stud	38×140 C16	2264	0	0	2
CS1 Cripple Stud	38×140 C16	2012	0	0	4
SP1 Sill Plate	38×140 C16	810	0	0	1
LP1 Lintel Ply	962×45 C16	962	0	0	3
SS1 Sill Support	38×140 C16	637	0	0	2
OS1 OSB Support	38×140 C16	69	0	0	2
VS1 Vertical Stud	38×140 C16	2264	0	0	2
VS2 Vertical Stud	38×140 C16	637	0	0	2
VS3 Vertical Stud	38×140 C16	69	0	0	2

Total: 25 pcs / 33.91 m

Sheathing & Insulation

Material	W	H	Label
OSB 9mm	447	2337	S01
OSB 9mm	813	287	S02
OSB 9mm	1137	2337	S03
OSB 9mm	813	710	S04
PIR 120mm	296	2264	P01
PIR 120mm	18	69	P02
PIR 120mm	111	69	P03
PIR 120mm	561	69	P04
PIR 120mm	21	69	P05
PIR 120mm	18	69	P06
PIR 120mm	245	2264	P07
PIR 120mm	561	2264	P08
PIR 120mm	102	2264	P09
PIR 120mm	92	636	P10
PIR 120mm	561	636	P11
PIR 120mm	2	636	P12

General Notes:

Frame Nailing:
140mm Frames Nail Using 3no, 3.1×90mm length field galvanised twisted strip nails
90mm Frames Nail Using 2no, 3.1×90mm length field galvanised twisted strip nails

Sheathing Nails:
Components ≤ 100mm should be +/- 1mm
Components > 100mm should be +/- 1.5mm
Stepped check should be +/- 1.5mm
Sloped Opening sizes are +/-2mm


Nailing:
30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.

Manufacturing Tolerances:
Length ±3 · Height ±2 · Diagonals ±5 · Openings 0/+5 (mm).
Do not scale — work to figured dimensions. All dims in mm.

Breather Membrane:
Laps 100mm horizontal / 150mm vertical, upper lapping lower.

Panel Changes:
When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.

KEY PLAN


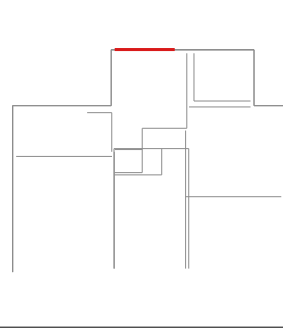


Revisions (Rev · Date · Note):


C01 - Construction issue

Date:	2026-09-13	Scale:	1:20	Drawn:	TS	Checked:	
Project Name: MP Adams Plot 3, Eckington							
Site:	Eckington			Client:	MP Adams		
Title:	Panel Fabrication — 38 x 140 C16 CLS						
Project Number:	P3			Revision:	C01		
Panel No:	FF-EX12			Drawing No:	P3-MF-FF-EX12		
Panel L×H×T:	2400×2340×149			Weight:	115 kg		
Status:	CONSTRUCTION			Sheet:	1 / 1		

Nailing: OSB/Ply racking: 150mm perimeter / 300mm field nails (EC5 §9.2.4, 2:1 panel h:b)

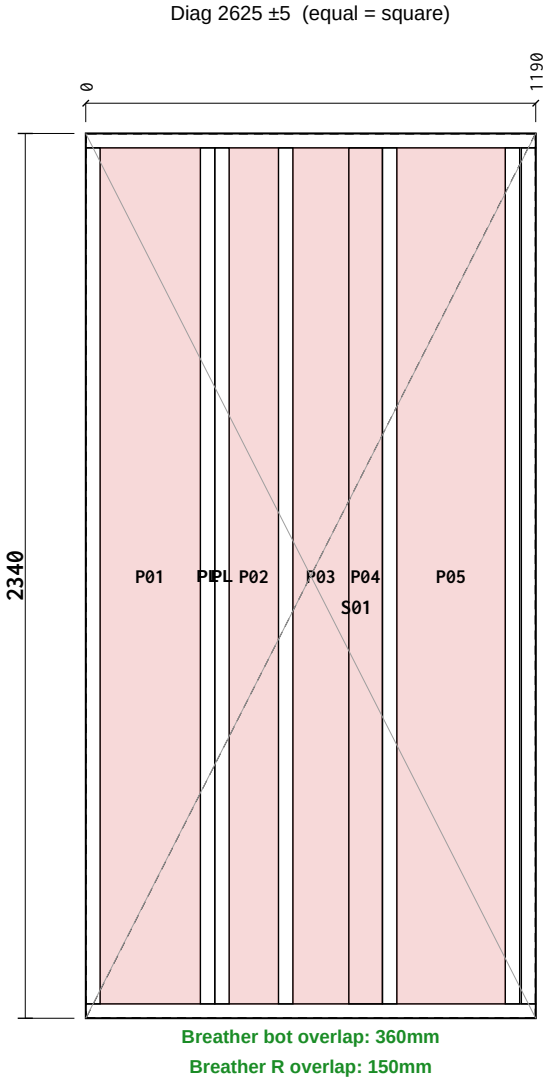

Section A-A



Cut List

Item	Section	Len	Bot°	Top°	Qty
BR1 Bottom Rail	38×140 C16	1190	0	0	1
TR1 Top Rail	38×140 C16	1190	0	0	1
ES1 End Stud	38×140 C16	2264	0	0	1
ES2 End Stud	38×140 C16	2264	0	0	1
VS1 Vertical Stud	38×140 C16	2264	0	0	3
JS1 Junction Stud	38×89 C16	2264	0	0	1
Total: 8 pcs / 15.96 m					

Sheathing & Insulation

Material	W	H	Label
OSB 9mm	1187	2337	S01
PIR 120mm	264	2264	P01
PIR 120mm	130	2264	P02
PIR 120mm	147	2264	P03
PIR 100mm	89	2264	P04
PIR 120mm	286	2264	P05
PIR 120mm	3	2264	P06

General Notes:

Frame Nailing:
140mm Frames Nail Using 3no, 3.1×90mm length field galvanised twisted strip nails
90mm Frames Nail Using 2no, 3.1×90mm length field galvanised twisted strip nails

Sheathing Nails:
Components ≤ 100mm should be +/- 1mm
Components > 100mm should be +/- 1.5mm
Stepped check should be +/- 1.5mm
Sloped Opening sizes are +/-2mm


Nailing:
30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.

Manufacturing Tolerances:
Length ±3 · Height ±2 · Diagonals ±5 · Openings 0/+5 (mm).
Do not scale — work to figured dimensions. All dims in mm.

Breather Membrane:
Laps 100mm horizontal / 150mm vertical, upper lapping lower.

Panel Changes:
When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.

KEY PLAN



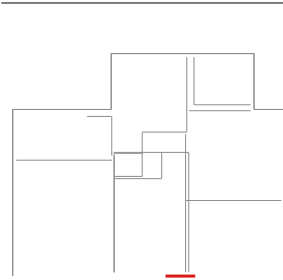


Revisions (Rev · Date · Note):

C01 - Construction issue

Date:	2026-09-13	Scale:	1:20	Drawn:	TS	Checked:	
Project Name:		MP Adams Plot 3, Eckington					
Site:		Eckington			Client:		MP Adams
Title:		Panel Fabrication — 38 x 140 C16 CLS					
Project Number:		P3			Revision:		C01
Panel No:		FF-EX13			Drawing No:		P3-MF-FF-EX13
Panel L×H×T:		1190×2340×149			Weight:		58 kg
Status:		CONSTRUCTION			Sheet:		1 / 1

Nailing: OSB/Ply racking: 150mm perimeter / 300mm field nails (EC5 §9.2.4, 2:1 panel h:b)

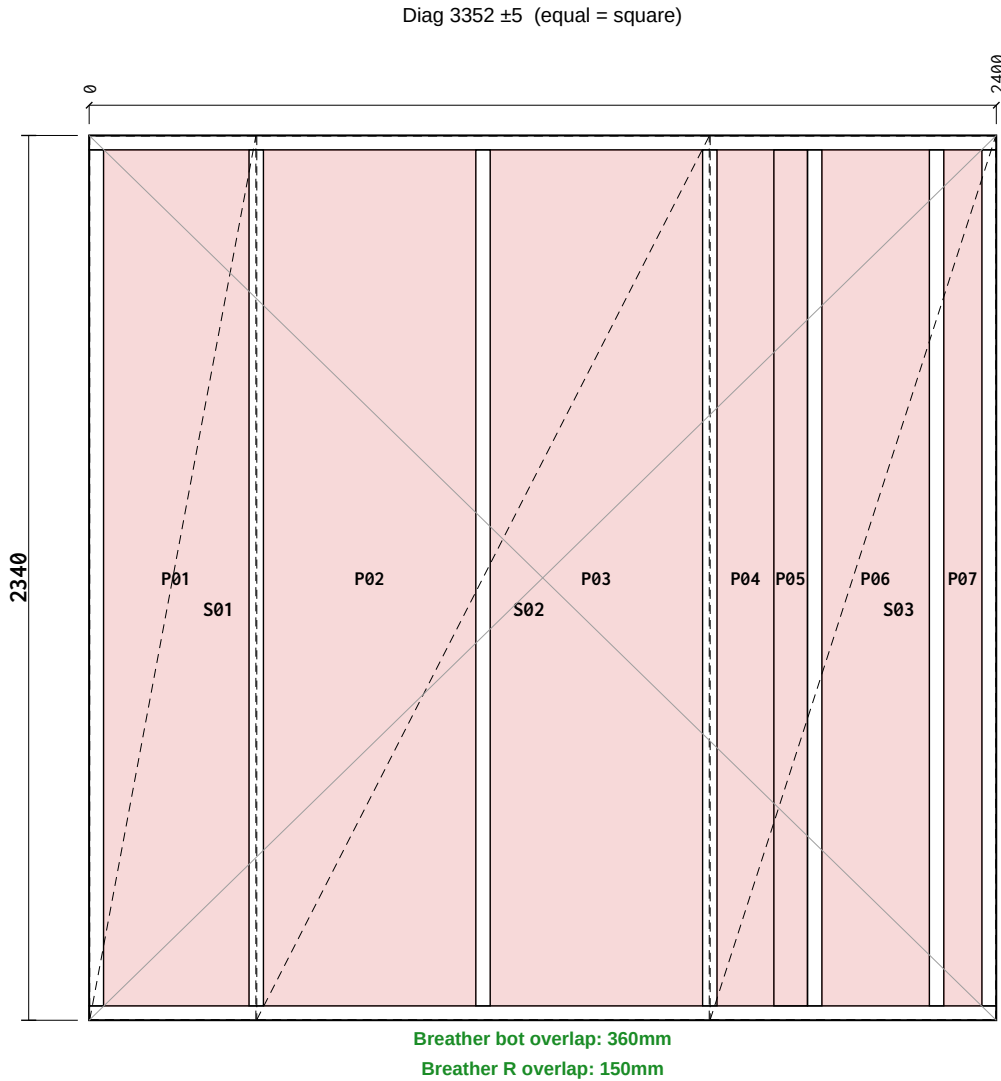

Cut List

Item	Section	Len	Bot°	Top°	Qty
BR1 Bottom Rail	38×140 C16	2400	0	0	1
TR1 Top Rail	38×140 C16	2400	0	0	1
ES1 End Stud	38×140 C16	2264	0	0	1
ES2 End Stud	38×140 C16	2264	0	0	1
VS1 Vertical Stud	38×140 C16	2264	0	0	5
JS1 Junction Stud	38×89 C16	2264	0	0	1
Total: 10 pcs / 22.91 m					

Sheathing & Insulation

Material	W	H	Label
OSB 9mm	439	2337	S01
OSB 9mm	1197	2337	S02
OSB 9mm	756	2337	S03
PIR 120mm	384	2264	P01
PIR 120mm	561	2264	P02
PIR 120mm	561	2264	P03
PIR 120mm	150	2264	P04
PIR 100mm	89	2264	P05
PIR 120mm	283	2264	P06
PIR 120mm	100	2264	P07

General Notes:

Frame Nailing:
140mm Frames Nail Using 3no, 3.1×90mm length field galvanised twisted strip nails
90mm Frames Nail Using 2no, 3.1×90mm length field galvanised twisted strip nails

Sheathing Nails:
Components ≤ 100mm should be +/- 1mm
Components > 100mm should be +/- 1.5mm
Stepped check should be +/- 1.5mm
Sloped Opening sizes are +/-2mm


Nailing:
30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.

Manufacturing Tolerances:
Length ±3 · Height ±2 · Diagonals ±5 · Openings 0/+5 (mm).
Do not scale — work to figured dimensions. All dims in mm.

Breather Membrane:
Laps 100mm horizontal / 150mm vertical, upper lapping lower.



Panel Changes:
When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.

KEY PLAN



Revisions (Rev · Date · Note):		C01 - Construction issue					
Date:	2026-09-13	Scale:	1:20	Drawn:	TS	Checked:	
Project Name:		MP Adams Plot 3, Eckington					
Site:	Eckington			Client:	MP Adams		
Title:	Panel Fabrication — 38 x 140 C16 CLS						
Project Number:	P3			Revision:	C01		
Panel No:	FF-EX14			Drawing No:	P3-MF-FF-EX14		
Panel L×H×T:	2400×2340×149			Weight:	100 kg		
Status:	CONSTRUCTION			Sheet:	1 / 1		

Nailing: OSB/Ply racking: 150mm perimeter / 300mm field nails (EC5 §9.2.4, 2:1 panel h:b)

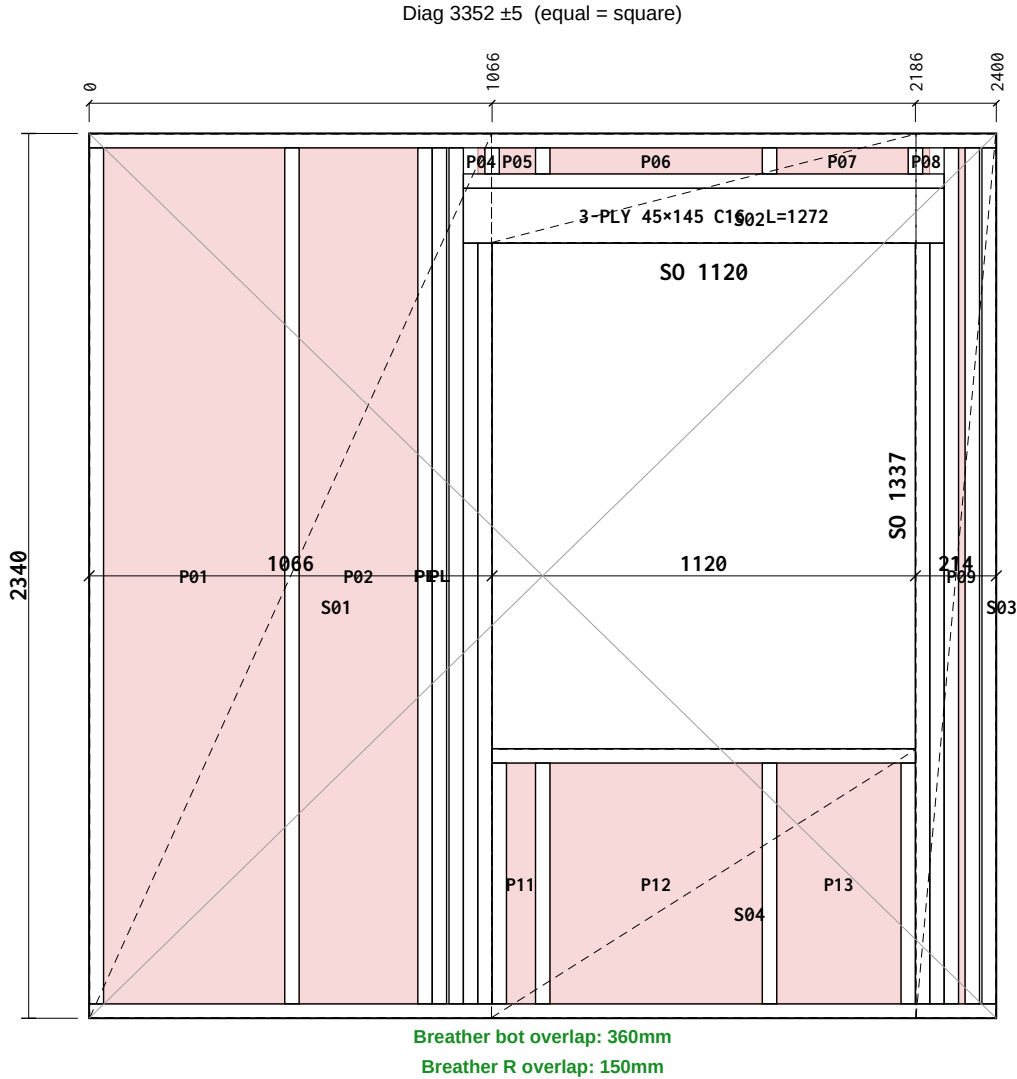

Cut List

Item	Section	Len	Bot°	Top°	Qty
BR1 Bottom Rail	38×140 C16	2400	0	0	1
TR1 Top Rail	38×140 C16	2400	0	0	1
TR2 Top Rail	38×140 C16	1272	0	0	1
ES1 End Stud	38×140 C16	2264	0	0	1
ES2 End Stud	38×140 C16	2264	0	0	1
KS1 Vertical Stud	38×140 C16	2264	0	0	2
CS1 Cripple Stud	38×140 C16	2012	0	0	4
SP1 Sill Plate	38×140 C16	1120	0	0	1
LP1 Lintel Ply	1272×45 C16	1272	0	0	3
SS1 Sill Support	38×140 C16	637	0	0	2
OS1 OSB Support	38×140 C16	69	0	0	2
VS1 Vertical Stud	38×140 C16	2264	0	0	2
VS2 Vertical Stud	38×140 C16	637	0	0	2
VS3 Vertical Stud	38×140 C16	69	0	0	2
Total: 25 pcs / 35.46 m					

Sheathing & Insulation

Material	W	H	Label
OSB 9mm	1063	2337	S01
OSB 9mm	1123	287	S02
OSB 9mm	211	2337	S03
OSB 9mm	1123	710	S04
PIR 120mm	479	2264	P01
PIR 120mm	313	2264	P02
PIR 120mm	5	2264	P03
PIR 120mm	18	69	P04
PIR 120mm	95	69	P05
PIR 120mm	561	69	P06
PIR 120mm	347	69	P07
PIR 120mm	18	69	P08
PIR 120mm	16	2264	P09
PIR 120mm	5	2264	P10
PIR 120mm	76	636	P11
PIR 120mm	561	636	P12
PIR 120mm	328	636	P13

General Notes:

Frame Nailing:
140mm Frames Nail Using 3no, 3.1×90mm length field galvanised twisted strip nails
90mm Frames Nail Using 2no, 3.1×90mm length field galvanised twisted strip nails

Sheathing Nails:
Components ≤ 100mm should be +/- 1mm
Components > 100mm should be +/- 1.5mm
Stepped check should be +/- 1.5mm
Sloped Opening sizes are +/-2mm


Nailing:
30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.

Manufacturing Tolerances:
Length ±3 · Height ±2 · Diagonals ±5 · Openings 0/+5 (mm).
Do not scale — work to figured dimensions. All dims in mm.

Breather Membrane:
Laps 100mm horizontal / 150mm vertical, upper lapping lower.

Panel Changes:
When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.


KEY PLAN




Revisions (Rev · Date · Note):		C01 - Construction issue					
Date:	2026-09-13	Scale:	1:20	Drawn:	TS	Checked:	
Project Name:		MP Adams Plot 3, Eckington					
Site:	Eckington			Client:	MP Adams		
Title:	Panel Fabrication — 38 x 140 C16 CLS						
Project Number:	P3			Revision:	C01		
Panel No:	FF-EX15			Drawing No:	P3-MF-FF-EX15		
Panel L×H×T:	2400×2340×149			Weight:	114 kg		
Status:	CONSTRUCTION			Sheet:	1 / 1		

Nailing: OSB/Ply racking: 150mm perimeter / 300mm field nails (EC5 §9.2.4, 2:1 panel h:b)


Diag 2465 ±5 (equal = square)

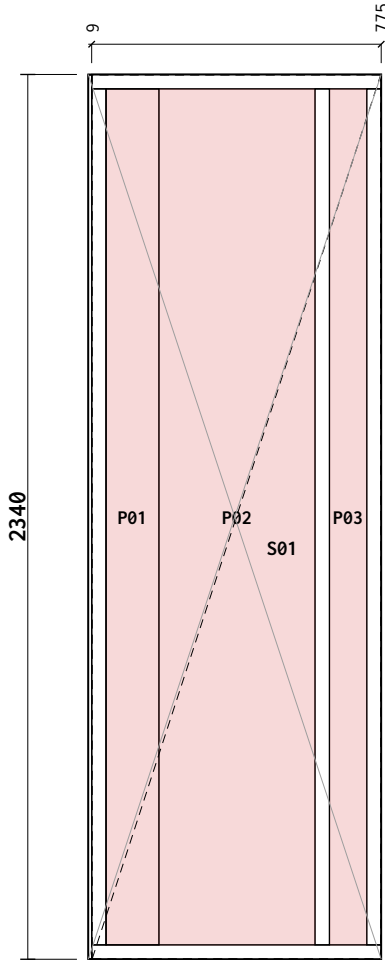

Breather bot overlap: 360mm
Breather R overlap: 150mm



Section A-A



Cut List

Item	Section	Len	Bot°	Top°	Qty
BR1 Bottom Rail	38×140 C16	766	0	0	1
TR1 Top Rail	38×140 C16	766	0	0	1
ES1 End Stud	38×140 C16	2264	0	0	1
ES2 End Stud	38×140 C16	2264	0	0	1
VS1 Vertical Stud	38×140 C16	2264	0	0	1
JS1 Junction Stud	38×140 C16	2264	0	0	1
Total: 6 pcs / 10.59 m					

Sheathing & Insulation

Material	W	H	Label
OSB 9mm	763	2337	S01
PIR 100mm	140	2264	P01
PIR 120mm	413	2264	P02
PIR 120mm	98	2264	P03
OSB End Cap 9mm	146	2337	E01

General Notes:

Frame Nailing:
140mm Frames Nail Using 3no, 3.1×90mm length field galvanised twisted strip nails
90mm Frames Nail Using 2no, 3.1×90mm length field galvanised twisted strip nails

Sheathing Nails:
Components ≤ 100mm should be +/- 1mm
Components > 100mm should be +/- 1.5mm
Stepped check should be +/- 1.5mm
Sloped Opening sizes are +/-2mm


Nailing:
30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.

Manufacturing Tolerances:
Length ±3 · Height ±2 · Diagonals ±5 · Openings 0/+5 (mm).
Do not scale — work to figured dimensions. All dims in mm.

Breather Membrane:
Laps 100mm horizontal / 150mm vertical, upper lapping lower.

Panel Changes:
When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.

KEY PLAN






Revisions (Rev · Date · Note):

C01 - Construction issue

Date:	2026-09-13	Scale:	1:20	Drawn:	TS	Checked:	
Project Name:		MP Adams Plot 3, Eckington					
Site:	Eckington			Client:	MP Adams		
Title:		Panel Fabrication — 38 x 140 C16 CLS					
Project Number:		P3		Revision:	C01		
Panel No:		FF-EX16		Drawing No:	P3-MF-FF-EX16		
Panel L×H×T:		775×2340×149		Weight:	41 kg		
Status:		CONSTRUCTION		Sheet:	1 / 1		

Nailing: OSB/Ply racking: 150mm perimeter / 300mm field nails (EC5 §9.2.4, 2:1 panel h:b)

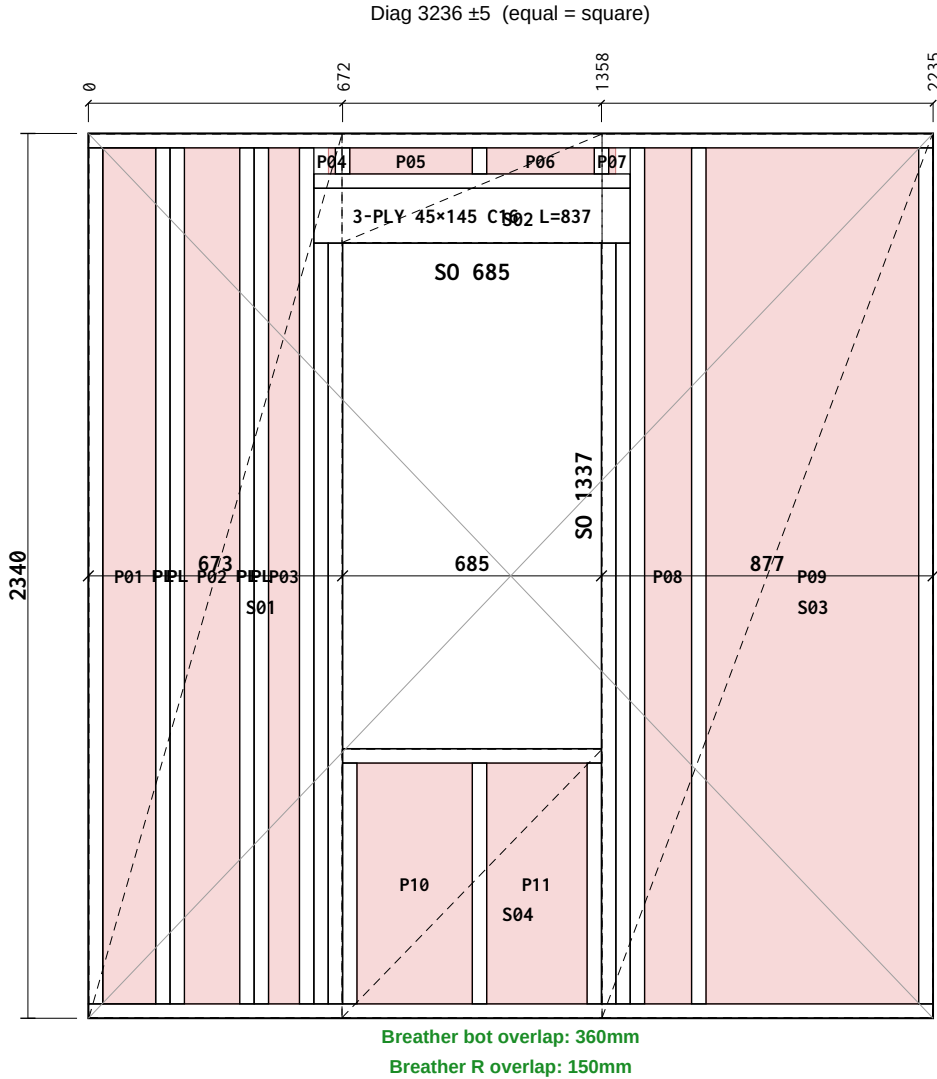

Cut List

Item	Section	Len	Bot°	Top°	Qty
BR1 Bottom Rail	38×140 C16	2235	0	0	1
TR1 Top Rail	38×140 C16	2235	0	0	1
TR2 Top Rail	38×140 C16	837	0	0	1
ES1 End Stud	38×140 C16	2264	0	0	1
ES2 End Stud	38×140 C16	2264	0	0	1
KS1 Vertical Stud	38×140 C16	2264	0	0	2
CS1 Cripple Stud	38×140 C16	2012	0	0	4
SP1 Sill Plate	38×140 C16	685	0	0	1
LP1 Lintel Ply	837×45 C16	837	0	0	3
SS1 Sill Support	38×140 C16	637	0	0	2
OS1 OSB Support	38×140 C16	69	0	0	2
VS1 Vertical Stud	38×140 C16	2264	0	0	1
VS2 Vertical Stud	38×140 C16	637	0	0	1
VS3 Vertical Stud	38×140 C16	69	0	0	1
JS1 Junction Stud	38×140 C16	2264	0	0	1

Total: 23 pcs / 32.25 m

Sheathing & Insulation

Material	W	H	Label
OSB 9mm	670	2337	S01
OSB 9mm	688	287	S02
OSB 9mm	874	2337	S03
OSB 9mm	688	710	S04
PIR 100mm	139	2264	P01
PIR 120mm	146	2264	P02
PIR 120mm	80	2264	P03
PIR 120mm	18	69	P04
PIR 120mm	323	69	P05
PIR 120mm	284	69	P06
PIR 120mm	18	69	P07
PIR 120mm	123	2264	P08
PIR 120mm	562	2264	P09
PIR 120mm	304	636	P10
PIR 120mm	265	636	P11

General Notes:

Frame Nailing:
140mm Frames Nail Using 3no, 3.1×90mm length field galvanised twisted strip nails
90mm Frames Nail Using 2no, 3.1×90mm length field galvanised twisted strip nails

Sheathing Nails:
Components ≤ 100mm should be +/- 1mm
Components > 100mm should be +/- 1.5mm
Stepped check should be +/- 1.5mm
Sloped Opening sizes are +/-2mm


Nailing:
30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.

Manufacturing Tolerances:
Length ±3 · Height ±2 · Diagonals ±5 · Openings 0/+5 (mm).
Do not scale — work to figured dimensions. All dims in mm.

Breather Membrane:
Laps 100mm horizontal / 150mm vertical, upper lapping lower.

Panel Changes:
When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.

KEY PLAN






Revisions (Rev · Date · Note):

C01 - Construction issue

Date:	2026-09-13	Scale:	1:20	Drawn:	TS	Checked:	
Project Name:		MP Adams Plot 3, Eckington					
Site:	Eckington			Client:	MP Adams		
Title:	Panel Fabrication — 38 x 140 C16 CLS						
Project Number:	P3			Revision:	C01		
Panel No:	FF-EX17			Drawing No:	P3-MF-FF-EX17		
Panel L×H×T:	2235×2340×149			Weight:	108 kg		
Status:	CONSTRUCTION			Sheet:	1 / 1		

Nailing: OSB/Ply racking: 150mm perimeter / 300mm field nails (EC5 §9.2.4, 2:1 panel h:b)

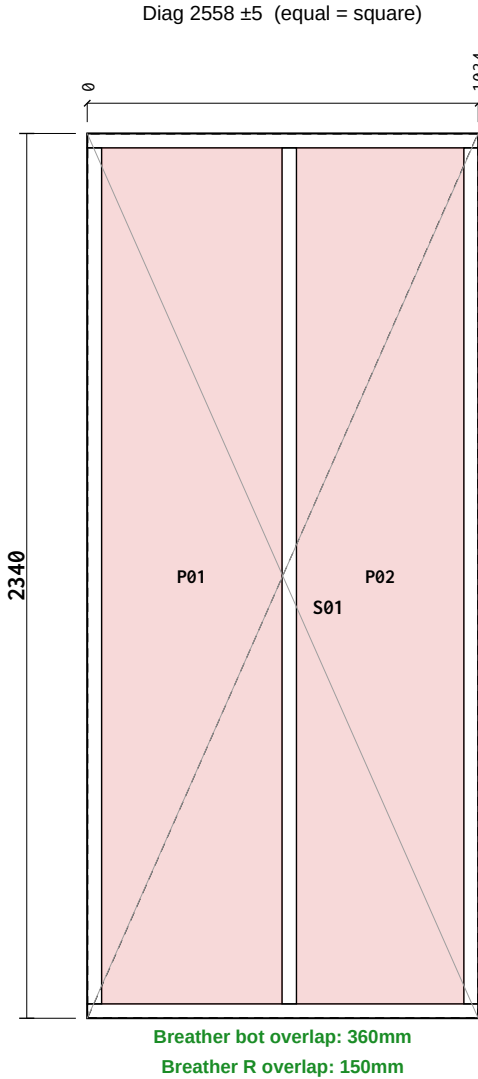

Cut List

Item	Section	Len	Bot°	Top°	Qty
BR1 Bottom Rail	38×140 C16	1035	0	0	1
TR1 Top Rail	38×140 C16	1035	0	0	1
ES1 End Stud	38×140 C16	2264	0	0	1
ES2 End Stud	38×140 C16	2264	0	0	1
VS1 Vertical Stud	38×140 C16	2264	0	0	1
Total: 5 pcs / 8.86 m					

Sheathing & Insulation

Material	W	H	Label
OSB 9mm	1032	2337	S01
PIR 120mm	477	2264	P01
PIR 120mm	442	2264	P02

General Notes:

Frame Nailing:
140mm Frames Nail Using 3no, 3.1×90mm length field galvanised twisted strip nails
90mm Frames Nail Using 2no, 3.1×90mm length field galvanised twisted strip nails

Sheathing Nails:
Components ≤ 100mm should be +/- 1mm
Components > 100mm should be +/- 1.5mm
Stepped check should be +/- 1.5mm
Sloped Opening sizes are +/-2mm


Nailing:
30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.

Manufacturing Tolerances:
Length ±3 · Height ±2 · Diagonals ±5 · Openings 0/+5 (mm).
Do not scale — work to figured dimensions. All dims in mm.

Breather Membrane:
Laps 100mm horizontal / 150mm vertical, upper lapping lower.

Panel Changes:
When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.

KEY PLAN

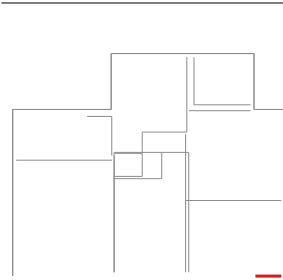

Revisions (Rev · Date · Note):		C01 - Construction issue					
Date:	2026-09-13	Scale:	1:20	Drawn:	TS	Checked:	
Project Name:		MP Adams Plot 3, Eckington					
Site:	Eckington			Client:	MP Adams		
Title:		Panel Fabrication — 38 x 140 C16 CLS					
Project Number:		P3		Revision:		C01	
Panel No:		FF-EX18		Drawing No:		P3-MF-FF-EX18	
Panel LxHxT:		1035x2340x149		Weight:		42 kg	
Status:		CONSTRUCTION		Sheet:		1 / 1	

Cut List






Item	Section	Len	Bot°	Top°	Qty
BR1 Bottom Rail	38×140 C16	1219	0	0	1
TR1 Top Rail	38×140 C16	1219	0	0	1
ES1 End Stud	38×140 C16	2264	0	0	1
ES2 End Stud	38×140 C16	2264	0	0	1
VS1 Vertical Stud	38×140 C16	2264	0	0	1
JS1 Junction Stud	38×140 C16	2264	0	0	1
Total: 6 pcs / 11.49 m					
Sheathing & Insulation					
Material			W	HLabel	
OSB 9mm			637	2337	S01
OSB 9mm			577	2337	S02
PIR 100mm			140	2264	P01
PIR 120mm			442	2264	P02
PIR 120mm			521	2264	P03
OSB End Cap 9mm			146	2337	E01

C01 - Construction issue

Date:	2026-09-13	Scale:	1:20	Drawn:	TS	Checked:	
Project Name:		MP Adams Plot 3, Eckington					
Site:	Eckington			Client:	MP Adams		
Title:	Panel Fabrication — 38 x 140 C16 CLS						
Project Number:	P3			Revision:	C01		
Panel No:	FF-EX19			Drawing No:	P3-MF-FF-EX19		
Panel L×H×T:	1228×2340×149			Weight:	53 kg		
Status:	CONSTRUCTION			Sheet:	1 / 1		

Nailing: OSB/Ply racking: 150mm perimeter / 300mm field nails (EC5 §9.2.4, 2:1 panel h:b)

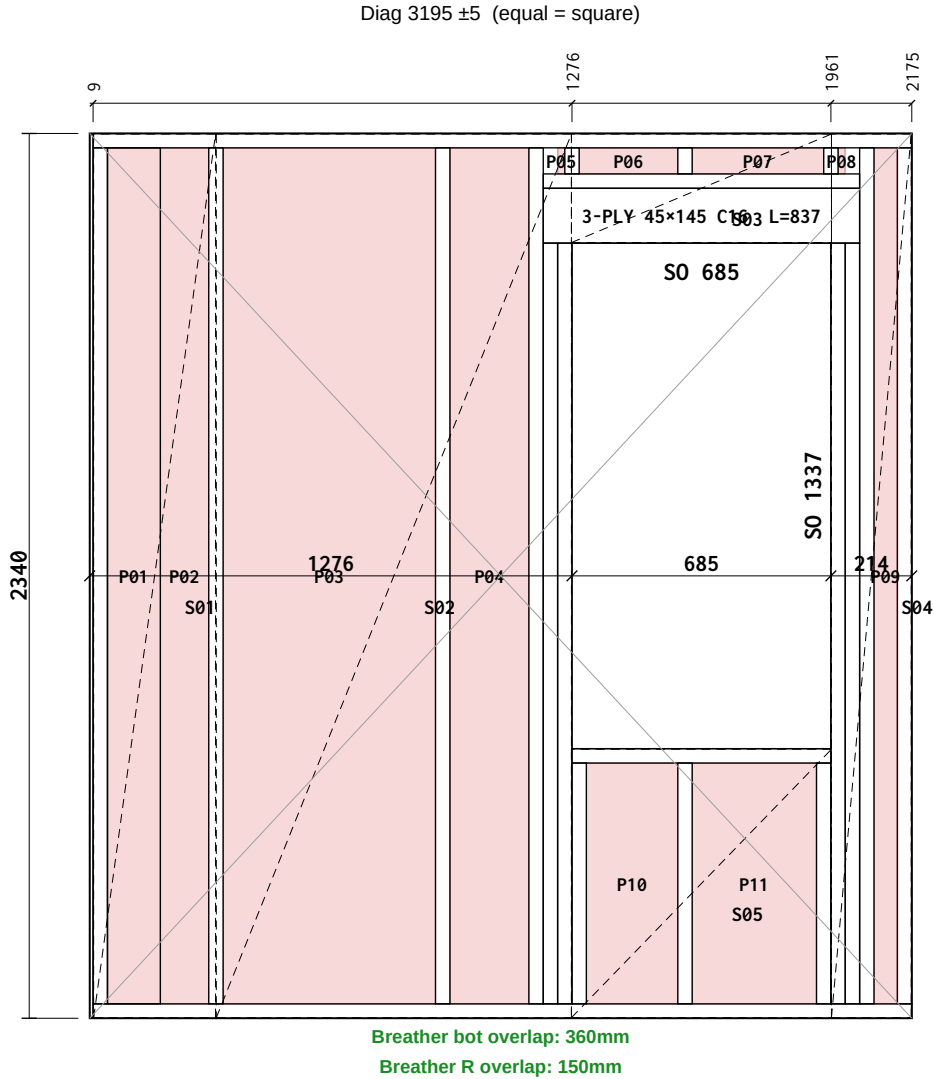

Cut List

Item	Section	Len	Bot°	Top°	Qty
BR1 Bottom Rail	38×140 C16	2166	0	0	1
TR1 Top Rail	38×140 C16	2166	0	0	1
TR2 Top Rail	38×140 C16	837	0	0	1
ES1 End Stud	38×140 C16	2264	0	0	1
ES2 End Stud	38×140 C16	2264	0	0	1
KS1 Vertical Stud	38×140 C16	2264	0	0	2
CS1 Cripple Stud	38×140 C16	2012	0	0	4
SP1 Sill Plate	38×140 C16	685	0	0	1
LP1 Lintel Ply	837×45 C16	837	0	0	3
SS1 Sill Support	38×140 C16	637	0	0	2
OS1 OSB Support	38×140 C16	69	0	0	2
VS1 Vertical Stud	38×140 C16	2264	0	0	2
VS2 Vertical Stud	38×140 C16	637	0	0	1
VS3 Vertical Stud	38×140 C16	69	0	0	1
JS1 Junction Stud	38×140 C16	2264	0	0	1

Total: 24 pcs / 34.38 m

Sheathing & Insulation

Material	W	H	Label
OSB 9mm	322	2337	S01
OSB 9mm	940	2337	S02
OSB 9mm	688	287	S03
OSB 9mm	211	2337	S04
OSB 9mm	688	710	S05
PIR 100mm	140	2264	P01
PIR 120mm	127	2264	P02
PIR 120mm	561	2264	P03
PIR 120mm	208	2264	P04
PIR 120mm	18	69	P05
PIR 120mm	260	69	P06
PIR 120mm	347	69	P07
PIR 120mm	18	69	P08
PIR 120mm	61	2264	P09
PIR 120mm	241	636	P10
PIR 120mm	328	636	P11
OSB End Cap 9mm	146	2337	E01

General Notes:

Frame Nailing:
140mm Frames Nail Using 3no, 3.1×90mm length field galvanised twisted strip nails
90mm Frames Nail Using 2no, 3.1×90mm length field galvanised twisted strip nails

Sheathing Nails:
Components ≤ 100mm should be +/- 1mm
Components > 100mm should be +/- 1.5mm
Stepped check should be +/- 1.5mm
Sloped Opening sizes are +/-2mm


Nailing:
30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.

Manufacturing Tolerances:
Length ±3 · Height ±2 · Diagonals ±5 · Openings 0/+5 (mm).
Do not scale — work to figured dimensions. All dims in mm.

Breather Membrane:
Laps 100mm horizontal / 150mm vertical, upper lapping lower.

Panel Changes:
When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.

KEY PLAN




Revisions (Rev · Date · Note):

C01 - Construction issue

Date:	2026-09-13	Scale:	1:20	Drawn:	TS	Checked:	
Project Name:	MP Adams Plot 3, Eckington						
Site:	Eckington			Client:	MP Adams		
Title:	Panel Fabrication — 38 x 140 C16 CLS						
Project Number:	P3			Revision:	C01		
Panel No:	FF-EX20			Drawing No:	P3-MF-FF-EX20		
Panel L×H×T:	2175×2340×149			Weight:	115 kg		
Status:	CONSTRUCTION			Sheet:	1 / 1		

Nailing: OSB/Ply racking: 150mm perimeter / 300mm field nails (EC5 §9.2.4, 2:1 panel h:b)

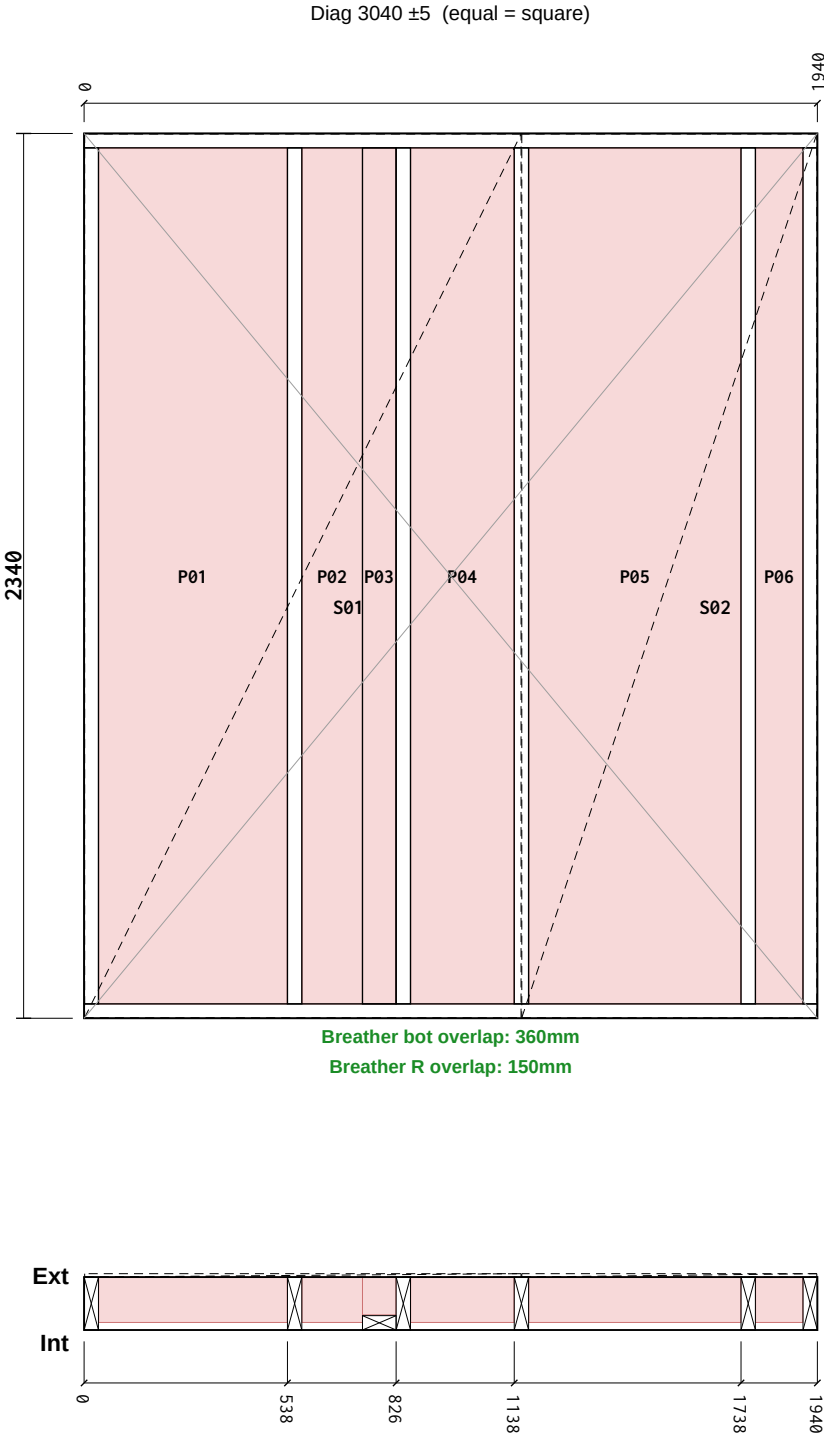

Cut List

Item	Section	Len	Bot°	Top°	Qty
BR1 Bottom Rail	38×140 C16	1940	0	0	1
TR1 Top Rail	38×140 C16	1940	0	0	1
ES1 End Stud	38×140 C16	2264	0	0	1
ES2 End Stud	38×140 C16	2264	0	0	1
VS1 Vertical Stud	38×140 C16	2264	0	0	4
JS1 Junction Stud	38×89 C16	2264	0	0	1
Total: 9 pcs / 19.73 m					

Sheathing & Insulation

Material	W	H	Label
OSB 9mm	1154	2337	S01
OSB 9mm	781	2337	S02
PIR 120mm	499	2264	P01
PIR 120mm	160	2264	P02
PIR 100mm	89	2264	P03
PIR 120mm	273	2264	P04
PIR 120mm	561	2264	P05
PIR 120mm	125	2264	P06

General Notes:

Frame Nailing:
140mm Frames Nail Using 3no, 3.1×90mm length field galvanised twisted strip nails
90mm Frames Nail Using 2no, 3.1×90mm length field galvanised twisted strip nails

Sheathing Nails:
Components ≤ 100mm should be +/- 1mm
Components > 100mm should be +/- 1.5mm
Stepped check should be +/- 1.5mm
Sloped Opening sizes are +/-2mm


Nailing:
30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.

Manufacturing Tolerances:
Length ±3 · Height ±2 · Diagonals ±5 · Openings 0/+5 (mm).
Do not scale — work to figured dimensions. All dims in mm.

Breather Membrane:
Laps 100mm horizontal / 150mm vertical, upper lapping lower.




Panel Changes:
When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.

KEY PLAN



Revisions (Rev · Date · Note):		C01 - Construction issue					
Date:	2026-09-13	Scale:	1:20	Drawn:	TS	Checked:	
Project Name:		MP Adams Plot 3, Eckington					
Site:	Eckington			Client:	MP Adams		
Title:	Panel Fabrication — 38 x 140 C16 CLS						
Project Number:	P3			Revision:	C01		
Panel No:	FF-EX21			Drawing No:	P3-MF-FF-EX21		
Panel L×H×T:	1940×2340×149			Weight:	83 kg		
Status:	CONSTRUCTION			Sheet:	1 / 1		

Nailing: OSB/Ply racking: 150mm perimeter / 300mm field nails (EC5 §9.2.4, 2:1 panel h:b)

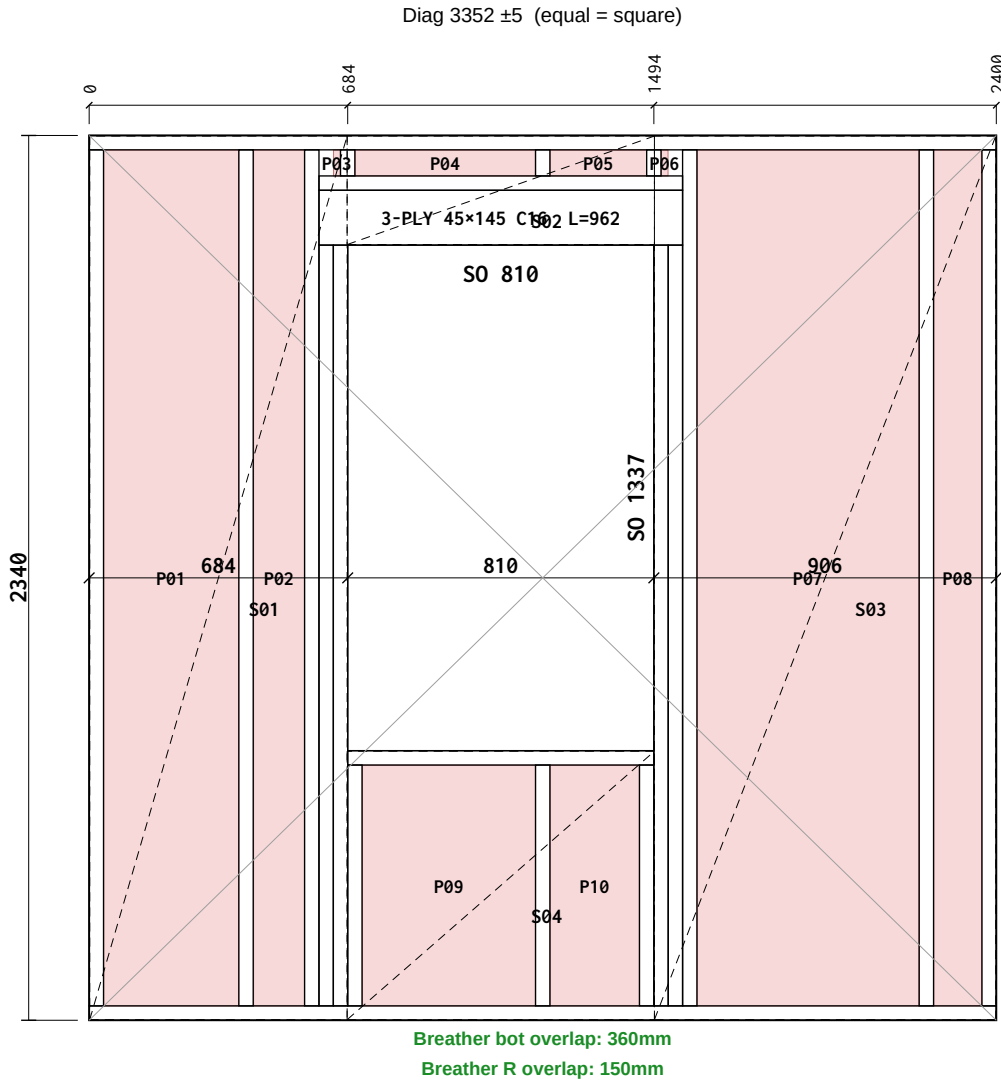

Cut List

Item	Section	Len	Bot°	Top°	Qty
BR1 Bottom Rail	38×140 C16	2400	0	0	1
TR1 Top Rail	38×140 C16	2400	0	0	1
TR2 Top Rail	38×140 C16	962	0	0	1
ES1 End Stud	38×140 C16	2264	0	0	1
ES2 End Stud	38×140 C16	2264	0	0	1
KS1 Vertical Stud	38×140 C16	2264	0	0	2
CS1 Cripple Stud	38×140 C16	2012	0	0	4
SP1 Sill Plate	38×140 C16	810	0	0	1
LP1 Lintel Ply	962×45 C16	962	0	0	3
SS1 Sill Support	38×140 C16	637	0	0	2
OS1 OSB Support	38×140 C16	69	0	0	2
VS1 Vertical Stud	38×140 C16	2264	0	0	2
VS2 Vertical Stud	38×140 C16	637	0	0	1
VS3 Vertical Stud	38×140 C16	69	0	0	1

Total: 23 pcs / 33.21 m

Sheathing & Insulation

Material	W	H	Label
OSB 9mm	681	2337	S01
OSB 9mm	813	287	S02
OSB 9mm	903	2337	S03
OSB 9mm	813	710	S04
PIR 120mm	357	2264	P01
PIR 120mm	135	2264	P02
PIR 120mm	18	69	P03
PIR 120mm	477	69	P04
PIR 120mm	255	69	P05
PIR 120mm	18	69	P06
PIR 120mm	586	2264	P07
PIR 120mm	127	2264	P08
PIR 120mm	458	636	P09
PIR 120mm	236	636	P10

General Notes:

Frame Nailing:
140mm Frames Nail Using 3no, 3.1×90mm length field galvanised twisted strip nails
90mm Frames Nail Using 2no, 3.1×90mm length field galvanised twisted strip nails

Sheathing Nails:
Components ≤ 100mm should be +/- 1mm
Components > 100mm should be +/- 1.5mm
Stepped check should be +/- 1.5mm
Sloped Opening sizes are +/-2mm


Nailing:
30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.

Manufacturing Tolerances:
Length ±3 · Height ±2 · Diagonals ±5 · Openings 0/+5 (mm).
Do not scale — work to figured dimensions. All dims in mm.

Breather Membrane:
Laps 100mm horizontal / 150mm vertical, upper lapping lower.

Panel Changes:
When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.

KEY PLAN



Revisions (Rev · Date · Note):

C01 - Construction issue

Date:	2026-09-13	Scale:	1:20	Drawn:	TS	Checked:	
Project Name:	MP Adams Plot 3, Eckington						
Site:	Eckington			Client:	MP Adams		
Title:	Panel Fabrication — 38 x 140 C16 CLS						
Project Number:	P3			Revision:	C01		
Panel No:	FF-EX22			Drawing No:	P3-MF-FF-EX22		
Panel L×H×T:	2400×2340×149			Weight:	114 kg		
Status:	CONSTRUCTION			Sheet:	1 / 1		
