




Nailing: OSB/Ply racking: 150mm perimeter / 300mm field nails (EC5 §9.2.4, 2:1 panel h:b)

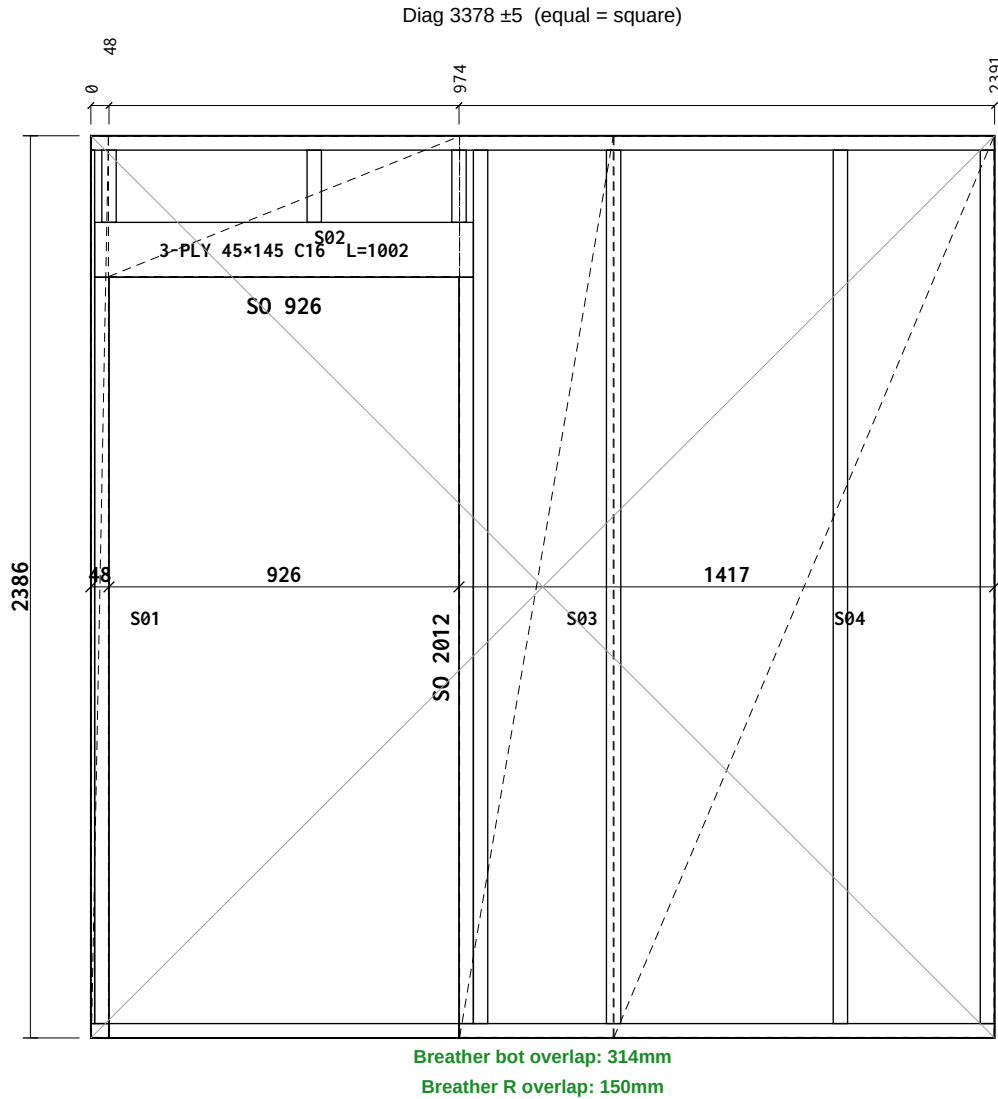

Section A-A



Cut List

Item	Section	Len	Bot°	Top°	Qty
BR1 Bottom Rail	38×140 C16	1417	0	0	1
BR2 Bottom Rail	38×140 C16	926	0	0	1
BR3 Bottom Rail	38×140 C16	48	0	0	1
TR1 Top Rail	38×140 C16	2391	0	0	1
ES1 End Stud	38×140 C16	191	0	0	1
ES2 End Stud	38×140 C16	2310	0	0	1
KS1 Vertical Stud	38×140 C16	2310	0	0	1
KS2 Vertical Stud	10×140 C16	2310	0	0	1
CS1 Cripple Stud	38×140 C16	1974	0	0	2
LP1 Lintel Ply	1002×45 C16	1002	0	0	3
OS1 OSB Support	38×140 C16	191	0	0	2
VS1 Vertical Stud	38×140 C16	2310	0	0	2

Total: 17 pcs / 23.86 m

Sheathing & Insulation

Material	W	H	Label
OSB 9mm	45	2383	S01
OSB 9mm	929	371	S02
OSB 9mm	406	2383	S03
OSB 9mm	1006	2383	S04

General Notes:

Frame Nailing:
140mm Frames Nail Using 3no, 3.1×90mm length field galvanised twisted strip nails
90mm Frames Nail Using 2no, 3.1×90mm length field galvanised twisted strip nails

Sheathing Nails:
Components ≤ 100mm should be +/- 1mm
Components > 100mm should be +/- 1.5mm
Stepped check should be +/- 1.5mm
Sloped Opening sizes are +/-2mm


Nailing:
30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.

Manufacturing Tolerances:
Length ±3 · Height ±2 · Diagonals ±5 · Openings 0/+5 (mm).
Do not scale — work to figured dimensions. All dims in mm.

Breather Membrane:
Laps 100mm horizontal / 150mm vertical, upper lapping lower.

Panel Changes:
When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.

KEY PLAN



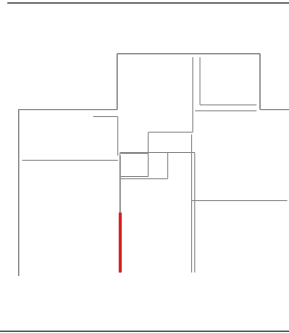


Revisions (Rev · Date · Note):

C01 - Construction issue

Date:	2026-09-13	Scale:	1:20	Drawn:	TS	Checked:	
Project Name:	MP Adams Plot 3, Eckington						
Site:	Eckington			Client:	MP Adams		
Title:	Panel Fabrication — 38 x 140 C16 CLS						
Project Number:	P3			Revision:	C01		
Panel No:	GF-IL1			Drawing No:	P3-MF-GF-IL1		
Panel L×H×T:	2391×2386×149			Weight:	72 kg		
Status:	CONSTRUCTION			Sheet:	1 / 1		

Nailing: OSB/Ply racking: 150mm perimeter / 300mm field nails (EC5 §9.2.4, 2:1 panel h:b)

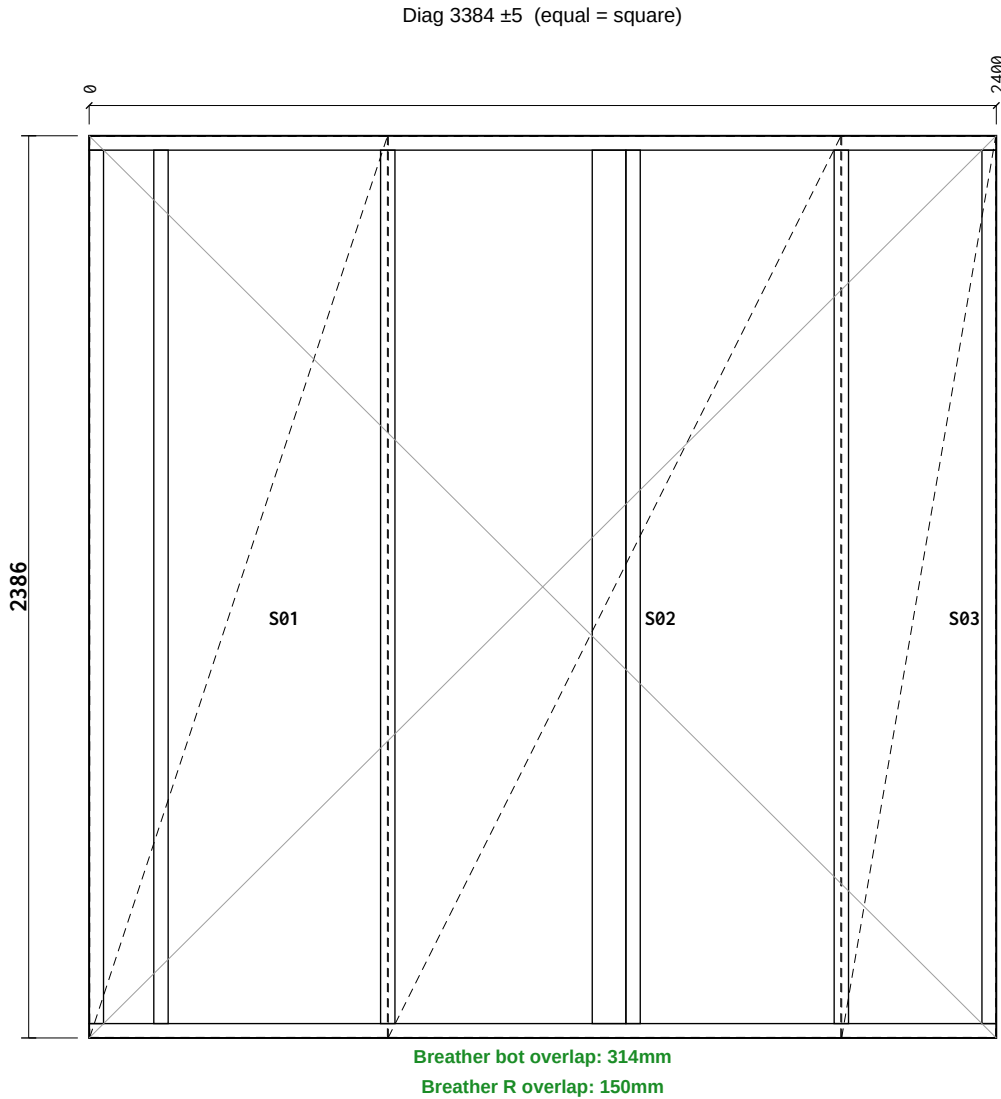

Cut List

Item	Section	Len	Bot°	Top°	Qty
BR1 Bottom Rail	38×140 C16	2400	0	0	1
TR1 Top Rail	38×140 C16	2400	0	0	1
ES1 End Stud	38×140 C16	2310	0	0	1
ES2 End Stud	38×140 C16	2310	0	0	1
VS1 Vertical Stud	38×140 C16	2310	0	0	4
JS1 Junction Stud	38×89 C16	2310	0	0	1
Total: 9 pcs / 20.97 m					

Sheathing & Insulation

Material	W	H	Label
OSB 9mm	787	2383	S01
OSB 9mm	1197	2383	S02
OSB 9mm	408	2383	S03

General Notes:

Frame Nailing:
140mm Frames Nail Using 3no, 3.1×90mm length field galvanised twisted strip nails
90mm Frames Nail Using 2no, 3.1×90mm length field galvanised twisted strip nails

Sheathing Nails:
Components ≤ 100mm should be +/- 1mm
Components > 100mm should be +/- 1.5mm
Stepped check should be +/- 1.5mm
Sloped Opening sizes are +/-2mm


Nailing:
30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.

Manufacturing Tolerances:
Length ±3 · Height ±2 · Diagonals ±5 · Openings 0/+5 (mm).
Do not scale — work to figured dimensions. All dims in mm.

Breather Membrane:
Laps 100mm horizontal / 150mm vertical, upper lapping lower.




Panel Changes:
When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.

KEY PLAN



Revisions (Rev · Date · Note):		C01 - Construction issue					
Date:	2026-09-13	Scale:	1:20	Drawn:	TS	Checked:	
Project Name:		MP Adams Plot 3, Eckington					
Site:	Eckington			Client:	MP Adams		
Title:	Panel Fabrication — 38 x 140 C16 CLS						
Project Number:	P3			Revision:	C01		
Panel No:	GF-IL2			Drawing No:	P3-MF-GF-IL2		
Panel L×H×T:	2400×2386×149			Weight:	76 kg		
Status:	CONSTRUCTION			Sheet:	1 / 1		

Nailing: OSB/Ply racking: 150mm perimeter / 300mm field nails (EC5 §9.2.4, 2:1 panel h:b)

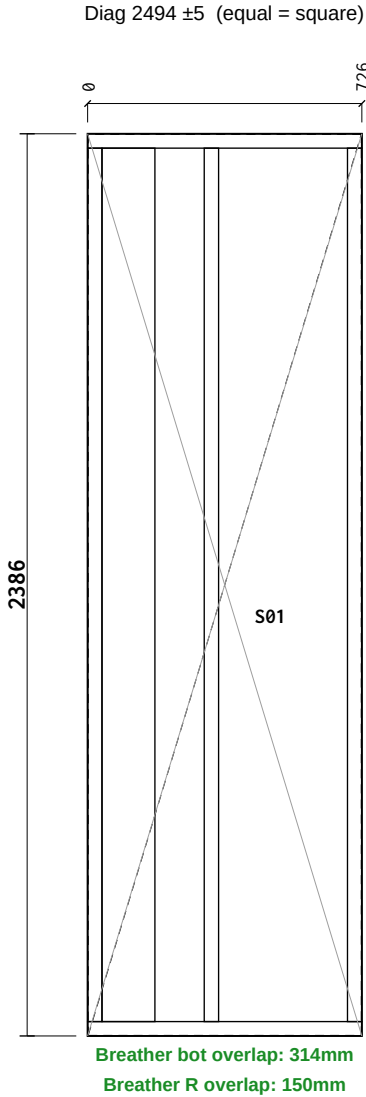

Cut List

Item	Section	Len	Bot°	Top°	Qty
BR1 Bottom Rail	38×140 C16	725	0	0	1
TR1 Top Rail	38×140 C16	725	0	0	1
ES1 End Stud	38×140 C16	2310	0	0	1
ES2 End Stud	38×140 C16	2310	0	0	1
VS1 Vertical Stud	38×140 C16	2310	0	0	1
JS1 Junction Stud	38×140 C16	2310	0	0	1
Total: 6 pcs / 10.69 m					

Sheathing & Insulation

Material	W	H	Label
OSB 9mm	722	2383	S01

General Notes:

Frame Nailing:
140mm Frames Nail Using 3no, 3.1×90mm length field galvanised twisted strip nails
90mm Frames Nail Using 2no, 3.1×90mm length field galvanised twisted strip nails

Sheathing Nails:
Components ≤ 100mm should be +/- 1mm
Components > 100mm should be +/- 1.5mm
Stepped check should be +/- 1.5mm
Sloped Opening sizes are +/-2mm


Nailing:
30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.

Manufacturing Tolerances:
Length ±3 · Height ±2 · Diagonals ±5 · Openings 0/+5 (mm).
Do not scale — work to figured dimensions. All dims in mm.

Breather Membrane:
Laps 100mm horizontal / 150mm vertical, upper lapping lower.




Panel Changes:
When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.

KEY PLAN



Revisions (Rev · Date · Note):		C01 - Construction issue					
Date:	2026-09-13	Scale:	1:20	Drawn:	TS	Checked:	
Project Name:		MP Adams Plot 3, Eckington					
Site:	Eckington			Client:	MP Adams		
Title:	Panel Fabrication — 38 x 140 C16 CLS						
Project Number:	P3			Revision:	C01		
Panel No:	GF-IL3			Drawing No:	P3-MF-GF-IL3		
Panel L×H×T:	725×2386×149			Weight:	33 kg		
Status:	CONSTRUCTION			Sheet:	1 / 1		

Nailing: OSB/Ply racking: 150mm perimeter / 300mm field nails (EC5 §9.2.4, 2:1 panel h:b)

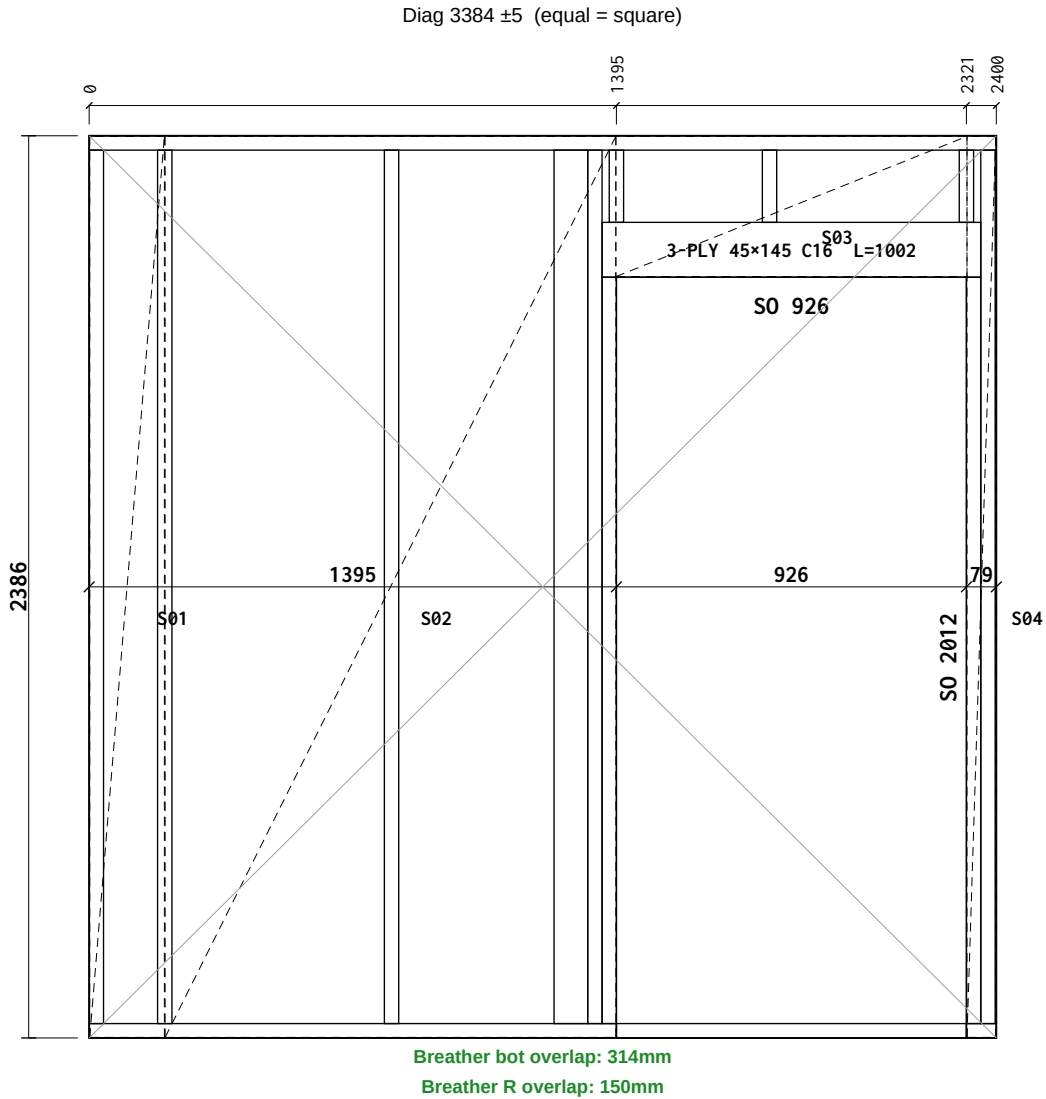

Cut List

Item	Section	Len	Bot°	Top°	Qty
BR1 Bottom Rail	38×140 C16	1395	0	0	1
BR2 Bottom Rail	38×140 C16	926	0	0	1
BR3 Bottom Rail	38×140 C16	79	0	0	1
TR1 Top Rail	38×140 C16	2400	0	0	1
ES1 End Stud	38×140 C16	2310	0	0	1
ES2 End Stud	38×140 C16	191	0	0	1
KS1 Vertical Stud	38×140 C16	2310	0	0	2
CS1 Cripple Stud	38×140 C16	1974	0	0	2
LP1 Lintel Ply	1002×45 C16	1002	0	0	3
OS1 OSB Support	38×140 C16	191	0	0	2
VS1 Vertical Stud	38×140 C16	2310	0	0	2
JS1 Junction Stud	38×89 C16	2310	0	0	1

Total: 18 pcs / 26.19 m

Sheathing & Insulation

Material	W	H	Label
OSB 9mm	198	2383	S01
OSB 9mm	1192	2383	S02
OSB 9mm	929	371	S03
OSB 9mm	76	2383	S04

General Notes:

Frame Nailing:
140mm Frames Nail Using 3no, 3.1×90mm length field galvanised twisted strip nails
90mm Frames Nail Using 2no, 3.1×90mm length field galvanised twisted strip nails

Sheathing Nails:
Components ≤ 100mm should be +/- 1mm
Components > 100mm should be +/- 1.5mm
Stepped check should be +/- 1.5mm
Sloped Opening sizes are +/-2mm


Nailing:
30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.

Manufacturing Tolerances:
Length ±3 · Height ±2 · Diagonals ±5 · Openings 0/+5 (mm).
Do not scale — work to figured dimensions. All dims in mm.

Breather Membrane:
Laps 100mm horizontal / 150mm vertical, upper lapping lower.

Panel Changes:
When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.

KEY PLAN


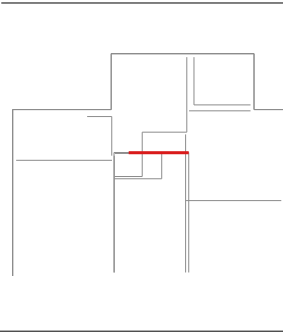


Revisions (Rev · Date · Note):

C01 - Construction issue

Date:	2026-09-13	Scale:	1:20	Drawn:	TS	Checked:	
Project Name:		MP Adams Plot 3, Eckington					
Site:	Eckington			Client:	MP Adams		
Title:	Panel Fabrication — 38 x 140 C16 CLS						
Project Number:	P3			Revision:	C01		
Panel No:	GF-IL4			Drawing No:	P3-MF-GF-IL4		
Panel L×H×T:	2400×2386×149			Weight:	79 kg		
Status:	CONSTRUCTION			Sheet:	1 / 1		

Nailing: OSB/Ply racking: 150mm perimeter / 300mm field nails (EC5 §9.2.4, 2:1 panel h:b)

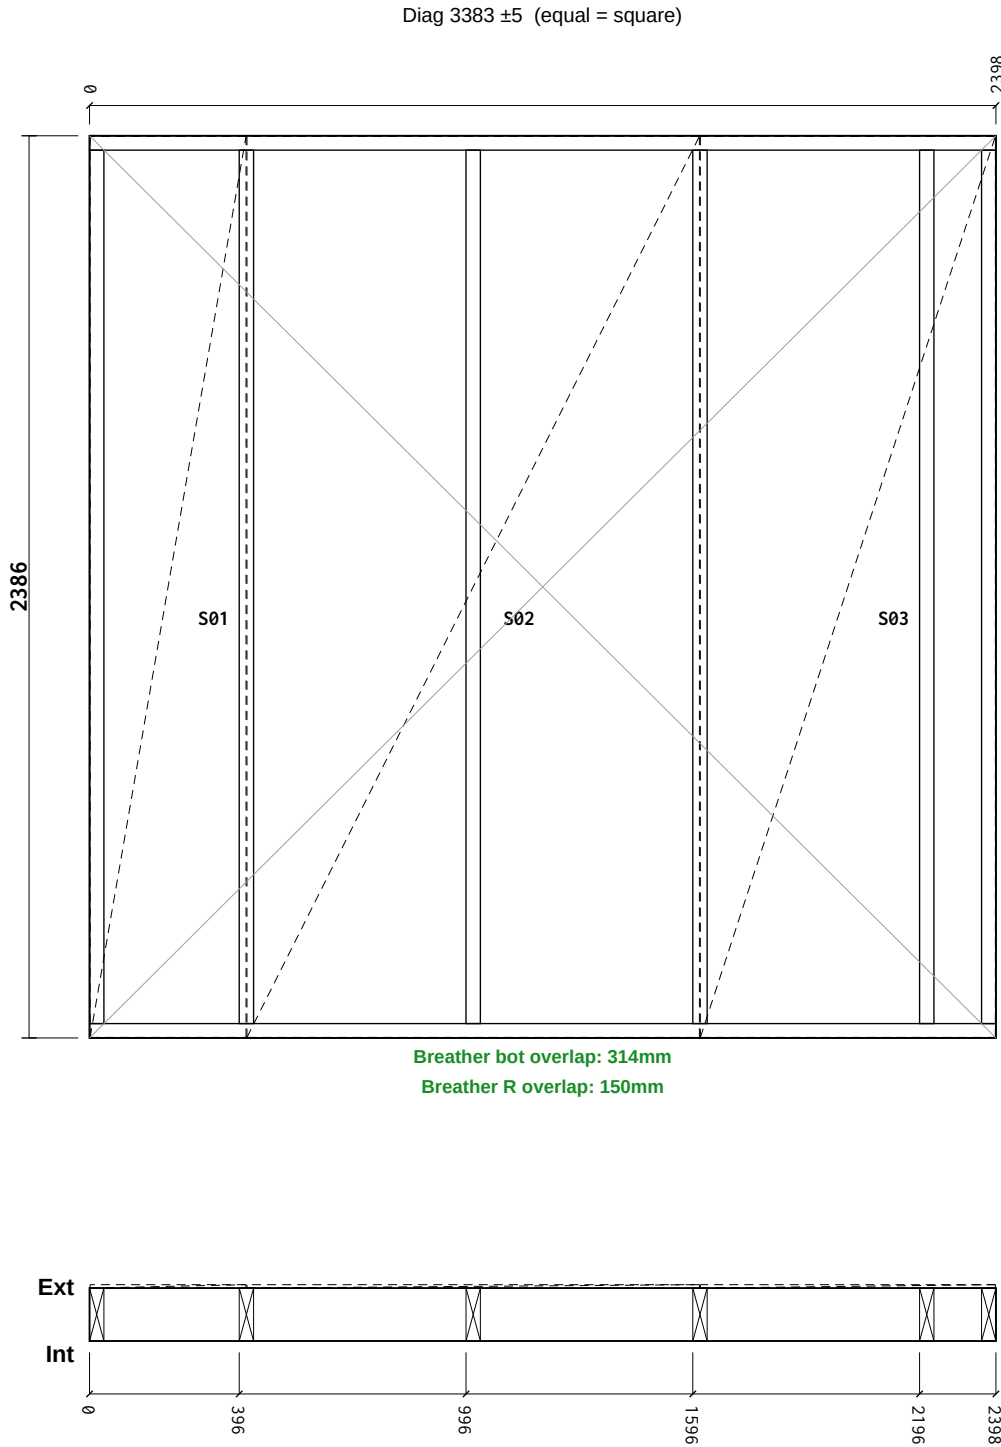

Cut List

Item	Section	Len	Bot°	Top°	Qty
BR1 Bottom Rail	38×140 C16	2398	0	0	1
TR1 Top Rail	38×140 C16	2398	0	0	1
ES1 End Stud	38×140 C16	2310	0	0	1
ES2 End Stud	38×140 C16	2310	0	0	1
VS1 Vertical Stud	38×140 C16	2310	0	0	4
Total: 8 pcs / 18.66 m					

Sheathing & Insulation

Material	W	H	Label
OSB 9mm	413	2383	S01
OSB 9mm	1197	2383	S02
OSB 9mm	780	2383	S03

General Notes:

Frame Nailing:
140mm Frames Nail Using 3no, 3.1×90mm length field galvanised twisted strip nails
90mm Frames Nail Using 2no, 3.1×90mm length field galvanised twisted strip nails

Sheathing Nails:
Components ≤ 100mm should be +/- 1mm
Components > 100mm should be +/- 1.5mm
Stepped check should be +/- 1.5mm
Sloped Opening sizes are +/-2mm


Nailing:
30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.

Manufacturing Tolerances:
Length ±3 · Height ±2 · Diagonals ±5 · Openings 0/+5 (mm).
Do not scale — work to figured dimensions. All dims in mm.

Breather Membrane:
Laps 100mm horizontal / 150mm vertical, upper lapping lower.




Panel Changes:
When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.

KEY PLAN



Revisions (Rev · Date · Note):		C01 - Construction issue					
Date:	2026-09-13	Scale:	1:20	Drawn:	TS	Checked:	
Project Name:		MP Adams Plot 3, Eckington					
Site:	Eckington			Client:	MP Adams		
Title:	Panel Fabrication — 38 x 140 C16 CLS						
Project Number:	P3			Revision:	C01		
Panel No:	GF-IL5			Drawing No:	P3-MF-GF-IL5		
Panel L×H×T:	2398×2386×149			Weight:	73 kg		
Status:	CONSTRUCTION			Sheet:	1 / 1		

Nailing: OSB/Ply racking: 150mm perimeter / 300mm field nails (EC5 §9.2.4, 2:1 panel h:b)

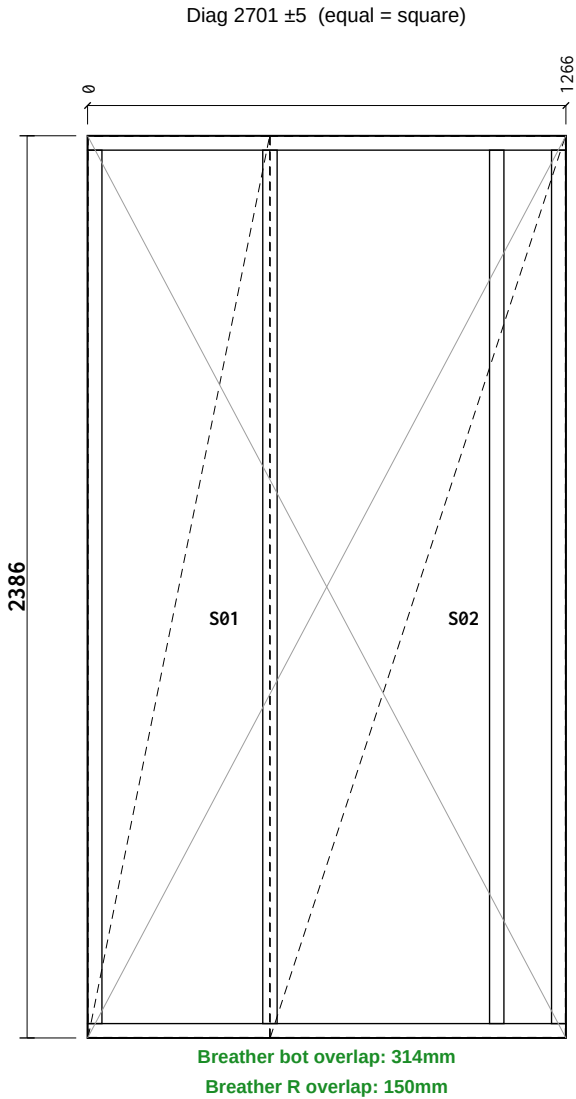

Cut List

Item	Section	Len	Bot°	Top°	Qty
BR1 Bottom Rail	38×140 C16	1265	0	0	1
TR1 Top Rail	38×140 C16	1265	0	0	1
ES1 End Stud	38×140 C16	2310	0	0	1
ES2 End Stud	38×140 C16	2310	0	0	1
VS1 Vertical Stud	38×140 C16	2310	0	0	2
Total: 6 pcs / 11.77 m					

Sheathing & Insulation

Material	W	H	Label
OSB 9mm	480	2383	S01
OSB 9mm	780	2383	S02

General Notes:

Frame Nailing:
140mm Frames Nail Using 3no, 3.1×90mm length field galvanised twisted strip nails
90mm Frames Nail Using 2no, 3.1×90mm length field galvanised twisted strip nails

Sheathing Nails:
Components ≤ 100mm should be +/- 1mm
Components > 100mm should be +/- 1.5mm
Stepped check should be +/- 1.5mm
Sloped Opening sizes are +/-2mm


Nailing:
30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.

Manufacturing Tolerances:
Length ±3 · Height ±2 · Diagonals ±5 · Openings 0/+5 (mm).
Do not scale — work to figured dimensions. All dims in mm.

Breather Membrane:
Laps 100mm horizontal / 150mm vertical, upper lapping lower.

Panel Changes:
When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.

KEY PLAN






Revisions (Rev · Date · Note):

C01 - Construction issue

Date:	2026-09-13	Scale:	1:20	Drawn:	TS	Checked:	
Project Name:		MP Adams Plot 3, Eckington					
Site:	Eckington			Client:	MP Adams		
Title:		Panel Fabrication — 38 x 140 C16 CLS					
Project Number:		P3		Revision:	C01		
Panel No:		GF-IL6		Drawing No:	P3-MF-GF-IL6		
Panel L×H×T:		1265×2386×149		Weight:	43 kg		
Status:		CONSTRUCTION		Sheet:	1 / 1		

Nailing: OSB/Ply racking: 150mm perimeter / 300mm field nails (EC5 §9.2.4, 2:1 panel h:b)

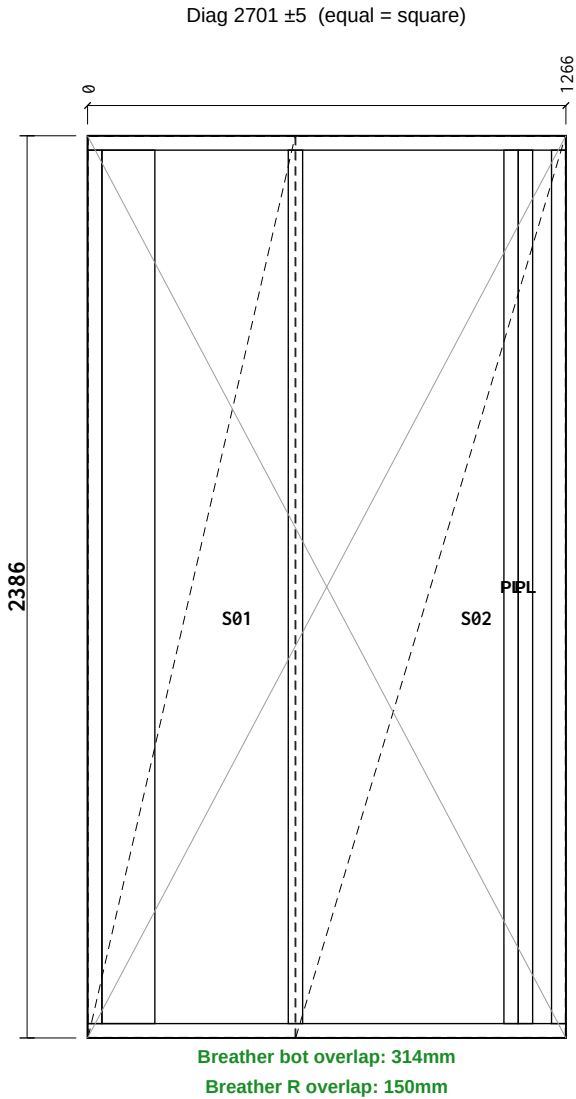

Cut List

Item	Section	Len	Bot°	Top°	Qty
BR1 Bottom Rail	38×140 C16	1265	0	0	1
TR1 Top Rail	38×140 C16	1265	0	0	1
ES1 End Stud	38×140 C16	2310	0	0	1
ES2 End Stud	38×140 C16	2310	0	0	1
VS1 Vertical Stud	38×140 C16	2310	0	0	1
JS1 Junction Stud	38×140 C16	2310	0	0	1
Total: 6 pcs / 11.77 m					

Sheathing & Insulation

Material	W	H	Label
OSB 9mm	548	2383	S01
OSB 9mm	713	2383	S02

General Notes:

Frame Nailing:
140mm Frames Nail Using 3no, 3.1×90mm length field galvanised twisted strip nails
90mm Frames Nail Using 2no, 3.1×90mm length field galvanised twisted strip nails

Sheathing Nails:
Components ≤ 100mm should be +/- 1mm
Components > 100mm should be +/- 1.5mm
Stepped check should be +/- 1.5mm
Sloped Opening sizes are +/-2mm


Nailing:
30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.

Manufacturing Tolerances:
Length ±3 · Height ±2 · Diagonals ±5 · Openings 0/+5 (mm).
Do not scale — work to figured dimensions. All dims in mm.

Breather Membrane:
Laps 100mm horizontal / 150mm vertical, upper lapping lower.

Panel Changes:
When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.

KEY PLAN



Revisions (Rev · Date · Note):		C01 - Construction issue					
Date:	2026-09-13	Scale:	1:20	Drawn:	TS	Checked:	
Project Name:		MP Adams Plot 3, Eckington					
Site:	Eckington			Client:	MP Adams		
Title:	Panel Fabrication — 38 x 140 C16 CLS						
Project Number:	P3			Revision:	C01		
Panel No:	GF-IL7			Drawing No:	P3-MF-GF-IL7		
Panel L×H×T:	1265×2386×149			Weight:	43 kg		
Status:	CONSTRUCTION			Sheet:	1 / 1		
